

2016 Readiness PSB Injection WP 9.2

BI.DIS


Magnets: 2 magnets available.
PFN: Prototype needs validation for series order by end 2015.
Controls: Generator prototype complete end 2015, series order Q2 2016

BR.KSW

Magnets: All components available. 2015 installation KSW16L1 on hold.
Powering & Controls: Prototype ready by end 2015, series to be build in 2016.

BR.TKSTR

Mechanism & Controls: 'prototype' being build for TKSTR L4, followed by series production end 2015 - start 2016.

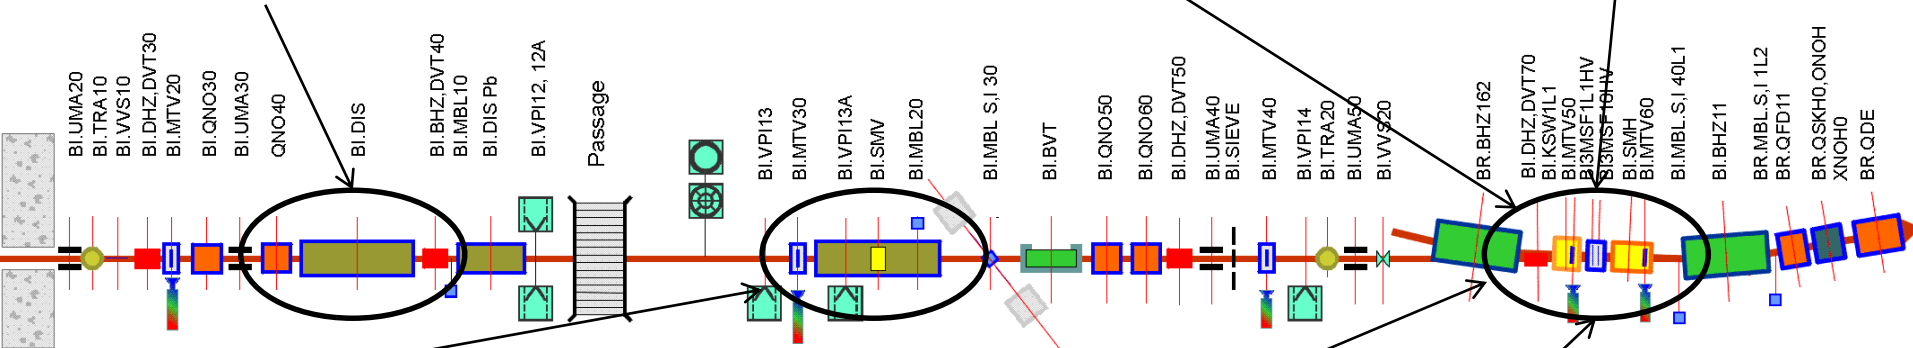

BI.SMV

Magnets: Being built, tanks have been delivered.
Powering: Done by TE-EPC.
Controls: Using existing system.

Support structure

Design almost completed, orders still to be placed this year.

BR.BSW


Magnets: 3 coils moulded
Powering: Done by TE-EPC.
Controls: Will be in time.

2016 Readiness PSB Injection WP 9.2



BI.DIS




BR.KSW

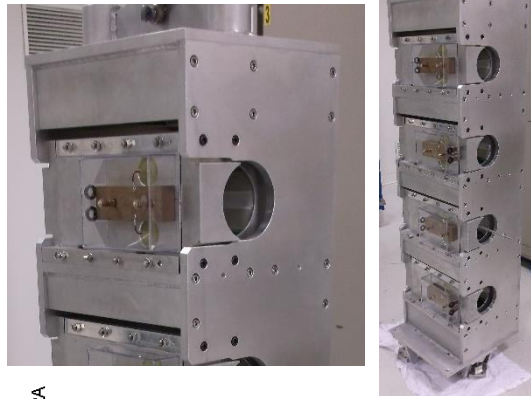

BR.TKSTR

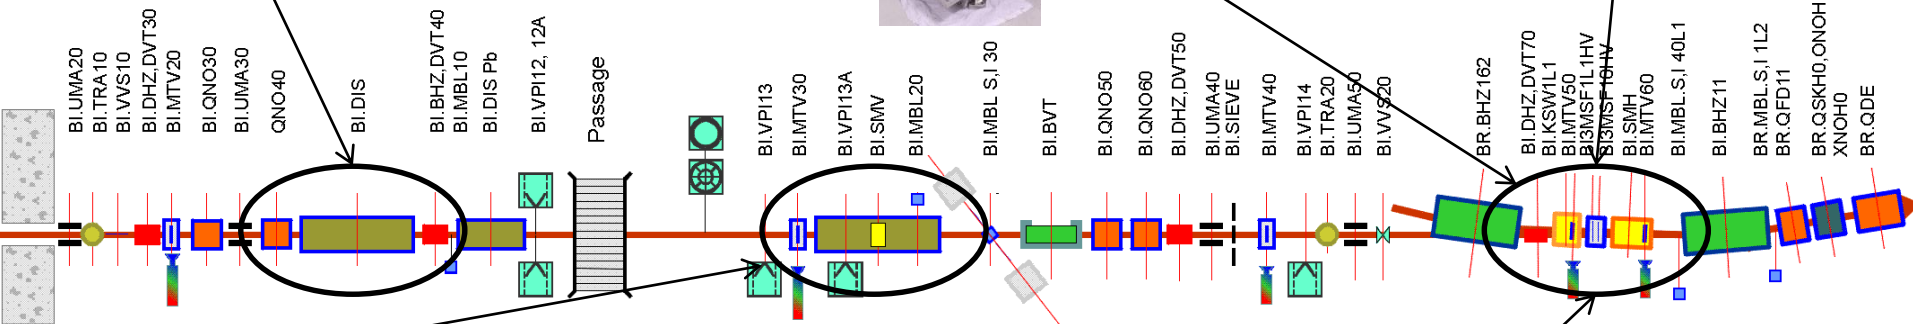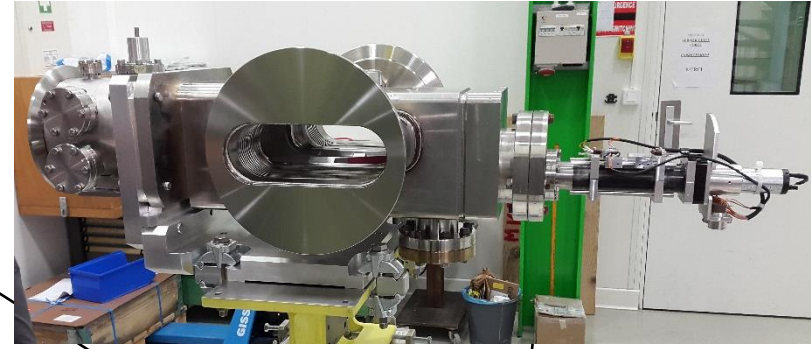

BI.SMV

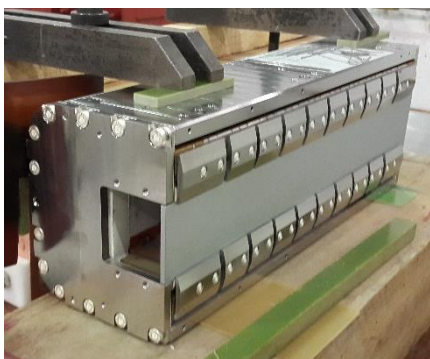

BR.BSW

