

# LIU project: preparing for the installation phase(s)

J. Coupard, G. Rumolo, M. Meddahi  
H. Damerau, A. Funken, S. Gilardoni, B. Goddard,  
K. Hanke, L. Kobzeva, A. Lombardi, D. Manglunki,  
B. Mikulec, E. Shaposhnikova, M. Vretenar



**LS2** DAYS

29-30 SEPTEMBER 2015

<http://indico.cern.ch/event/436424/>

# Outline

- Project deliverable and timeline
- Project organisational strategy for installation phases
- Baseline changes impacting (E)YETS, LS2
- Concerns

# LIU deliverable target

	$\mathcal{N}$ (x $10^{11}$ p/b)	$\varepsilon$ ( $\mu\text{m}$ )	# of bunches
SPS achieved	1.2	2.6	288
<b>SPS for HL-LHC</b>	<b>2.3</b>	<b>2.1</b>	<b>288</b>


Injectors must produce 25 ns proton beams with about double intensity and even more than double brightness.

A cascade of improvements is needed across the whole injector chain to reach this target

**=> Massive installation programme during LS2**

# Timeline

- LIU (machine, simulation, design) studies and procurement during **Run 2** until **LS2**.
- LIU installations and final hardware work mainly during **LS2**
- Beam commissioning of LIU beams
  - **Pb ion beams** need to be ready by **2021 ion run**
  - **Proton beams** during **Run 3** to be ready after **LS3**

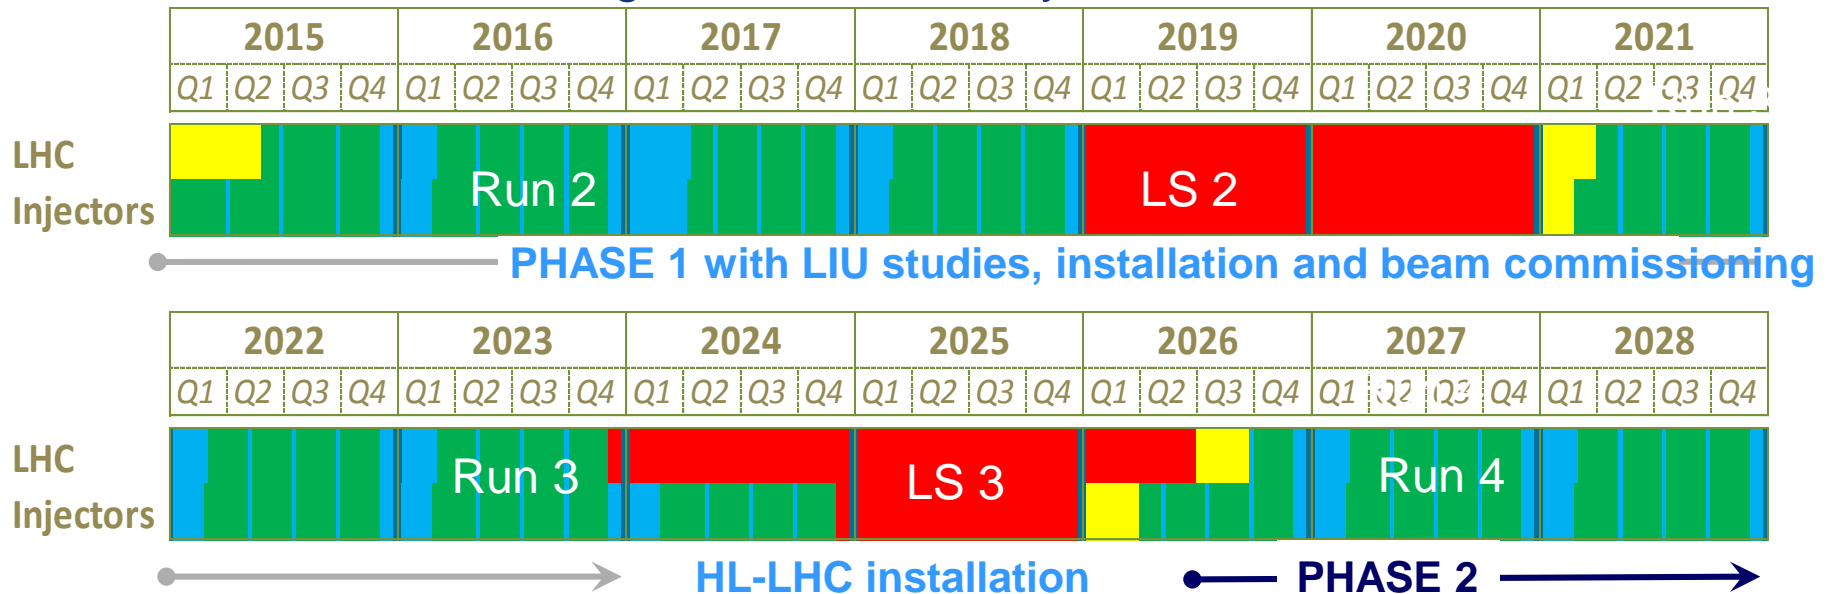


All on-going activities on planning, layout, preparation of installation phases : under the coordination of Julie Coupard – next talk

# Preparing installation phases: LIU general strategy

- LIU-PSB (Klaus Hanke), LIU-PS (Simone Gilardoni), LIU-SPS (Brennan Goddard) and LIU-IONS (Simone Gilardoni) coordination groups: definition of the needs: simulation/specification/close collaboration with equipment groups through design/procurement/assembling phases and preparation of installation + commissioning
- All groups responsible for their equipment readiness, within specification and defined timeline -> LS2 talks
- Julie Coupard to coordinate the overall Planning / Layout / Installation activities with all her EN-MEF colleagues (ECR, SSR...)
- Need to take into consideration at an early stage the requirements from other projects, incl. maintenance and CONS.
  - > To be included into the LIU planning, by Julie Coupard for the Injectors
  - > LS2 days to gather all the 'known' needs and consolidate data with PLAN inputs
- Installation priorities / conflicts to be agreed at the level of the Accelerator and Technology Director, with recommendations from related committees (LS2, IEFC, LMC)

# Preparing for LS2: LIU - Planning & Installation Coordination - EN-MEF group

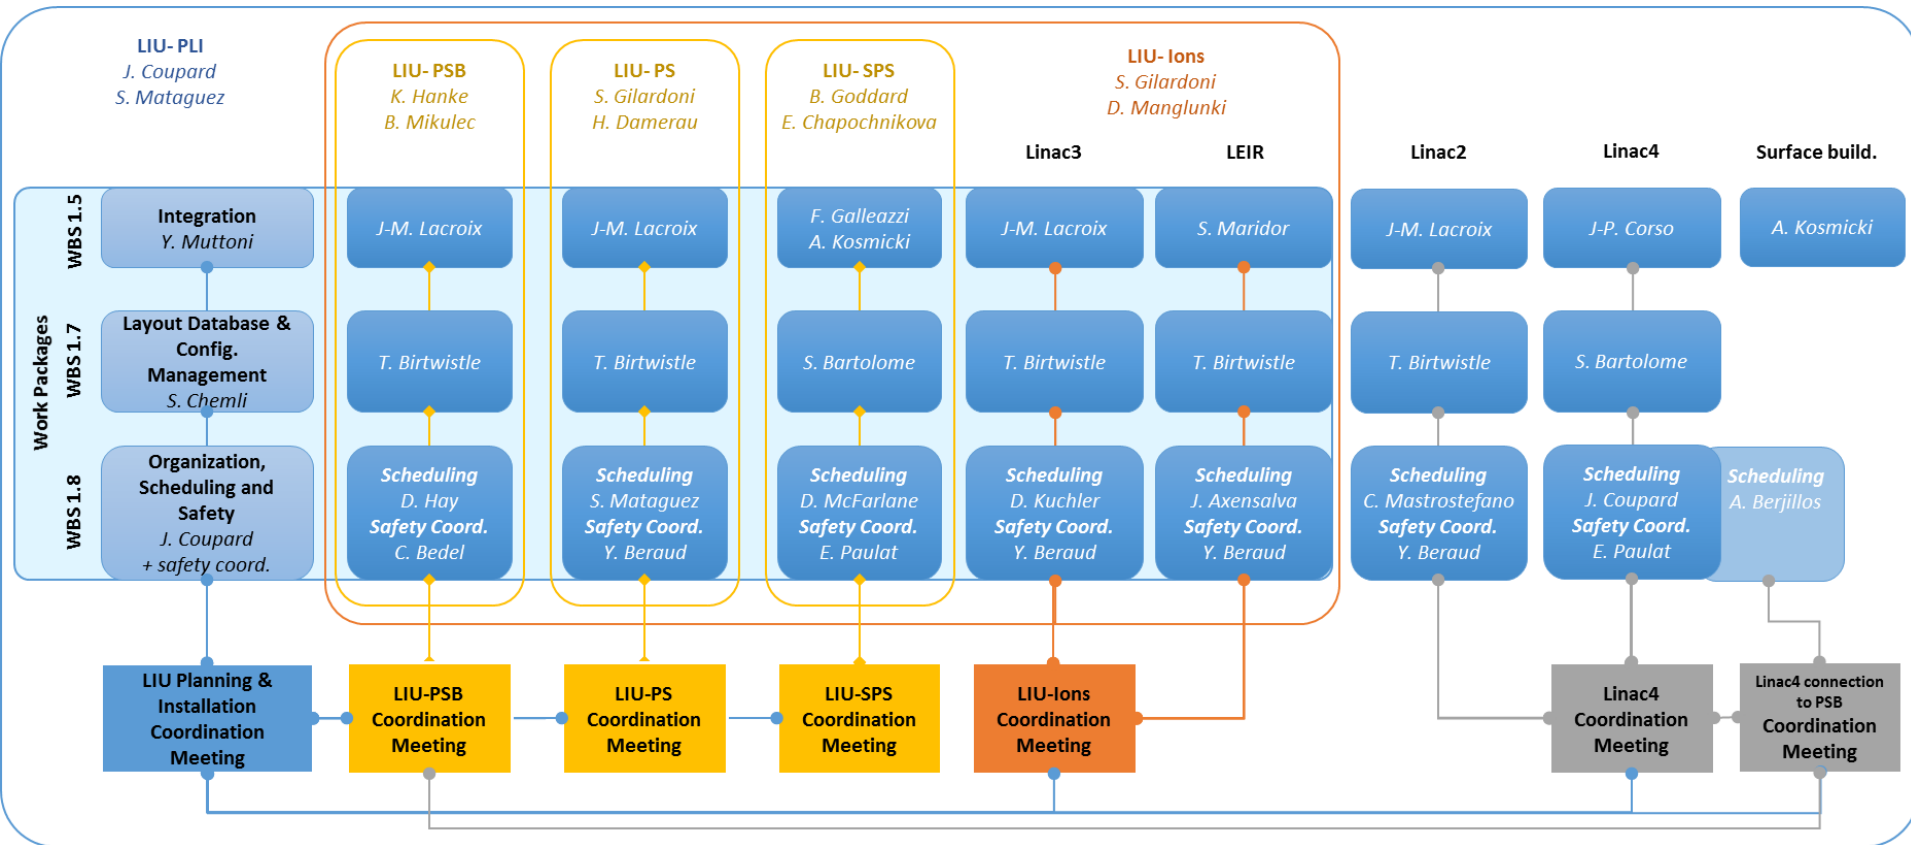

Courtesy Julie Coupard

# Project Status

- Project in execution phase, as defined by baseline presented at the Cost & Scheduling review in March 2015
- As planned, 2015 checkpoints in the project baseline took place through reviews
- Reviews outcomes related to (E)YEST, LS2 installation activities:
  - LIU-SPS External / Internal beam dump
  - LIU-SPS Scrubbing / aC coating in synergy with the LIU-SPS Impedance reduction programme

# LIU-SPS Beam dump

- Recommendations presented on 3 July 2015 at the IEFC by Etienne Carlier (coordinator)
- Strategy:
  - New TIDVG installed in LSS5 in LS2
  - Some work to be anticipated to (E)YETS
  - Removal of actual TIDVG and TIDH in LS2
  - Design and integration to be completed by end 2015
- More in equipment groups talks.



# LIU-SPS scrubbing – aC coating review

<https://indico.cern.ch/event/433608/>

**Reviewers:** W. Fischer (BNL, chair), Y. Suetsugu (KEK), K. Cornelis, J.M. Jimenez, M. Meddahi, F. Zimmermann (CERN)

Work presented by **LIU-SPS ecloud / aC teams**, years of intense theoretical and experimental studies, remarkable results.

Conclusions presented on 25 September 2015, at IEFC by Brennan.

## Review conclusion

- With scrubbing experience to date, analysis of data and simulations, LIU and HL-LHC performance goals are not guaranteed with scrubbing only
- High confidence that aC coating of MBB dipoles will deliver performance goals
- Opportunistic deployment of aC should be pursued to
  - (i) maintain/further develop coating technology, and
  - (ii) increase performance margin in the SPS

## Review recommendation

- Make aC coating of MMB dipoles the baseline until there is high confidence that scrubbing can establish LIU and HL-LHC performance goals

# LIU-SPS scrubbing – aC coating review

<https://indico.cern.ch/event/433608/>

**Proposed implementation and timeline: being analysed by equipment groups, under coordination of Paul Cruikshank**

- **EYETS 16/17:**

- pilot (up to 1 arc?) for coating QFs and QF SSS, in synergy with impedance reduction;
- a few (4?) MBB half-cells coated in-situ, to prototype the ‘final’ cleaning and coating technology;
- replacement of some (10%?) standard 156 mm drifts with coated chambers.

- **LS2:**

- complete coating of remaining QFs and QF SSS, in synergy with impedance reduction;
- Pilot (1 arc?) MBB coating, to debug full-scale logistics and quality control;
- replacement of remaining 156 mm standard drifts with coated chambers.

- **Run3:**

- Evaluation of whether these improvements, plus some improvements to the transverse damper, are already enough to reach the performance target

- **LS3:**

- If required, coating of remaining MBBs around the machine.

Coordination meeting series will be launched – Paul Cruikshank

# Concerns

- Planning / Layout / Installation activities to be integrated together with the projects, CONS, maintenance activities for the whole injectors chains – in progress
- Identification of the resources bottlenecks and strategy defined
- Critical that upgraded and new equipment are installed by end of LS2 to study the LIU beams during Run3, understand the limitations and acquire operational experience
- PRE-LS2 de-cabling campaign in PSB but also in PS and SPS
- Overall (E)YETS, LS2 cabling campaign
- Consolidation items needed for LIU operation must take place before end of LS2 (some during (E)YETS)

# Outlook

- Much work ahead
- De-cabling campaigns remain a high risk activity
- Anticipate as much installation as possible – synergies
- Need of a master schedule for the injectors chain
- Thanks to all the departments and groups for their fruitful collaboration with the LIU project and deep commitments



**LS2** DAYS

29-30 SEPTEMBER 2015

THANK YOU FOR YOUR  
ATTENTION!
