

ELENA Installation follow-up

02/04/2015

- Worksite follow-up


Worksite follow-up

- CV Works :
 - Installation of cooling pipes from b.393 finished
 - Installation of the support for the cable tray finished
- GS Works :
 - Dismantling of the kickers platform complete
 - Dismantling of the false floor complete



Worksite follow-up

- TE-ABT works (b.193):
 - Cable pulling on-going (warning on the routing of the cables)

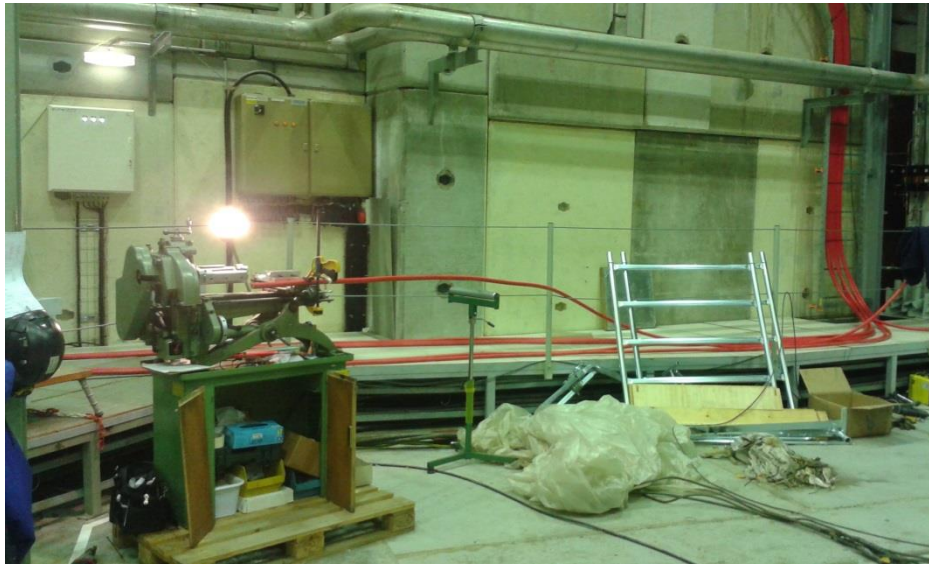

Worksite follow-up

- General cleaning of the area :



Worksite follow-up

- Updated planning for the week 14:
 - Completion of CV works on Friday (F. Moro)
 - Dismantling of kicker platform and false floor from Monday to Wednesday (D. Parchet)
 - Cleaning of the area finished on Wednesday (E. Harrouch)
 - Start of the survey work on Thursday (T. Dobers)

Worksite follow-up

- Updated planning for the week 15:
 - Installation of the lateral false floor (D. Parchet)
 - Survey marking of the 6 dipoles and the centre to be done before Wednesday 8/04 (T. Dobers)
 - Installation of the hexagonal false floor (D. Parchet)
 - CV works for the source reception (F. Moro/B. Lefort)

Planning proposal for the coming weeks

<input type="checkbox"/> Survey marking (incl. Gbar and H- source)	18 days	Mon 30/03/15	Wed 22/04/15	T. Dobers	EN/MEF	42%		Survey marking (incl. Gbar and H- source)	30/03	22/04
Importing AD references for ELENA	1 wk	Mon 30/03/15	Fri 03/04/15	T. Dobers	EN/MEF	100%		Importing AD references for ELENA	30/03	03/04
Survey marking (Dipoles and ELENA Center)	2 days	Tue 07/04/15	Wed 08/04/15	T. Dobers	EN/MEF	0%	56	Survey marking (Dipoles and ELENA Center)	07/04	08/04
Survey marking (incl. Gbar and H- source)	1 wk	Thu 16/04/15	Wed 22/04/15	T. Dobers	EN/MEF	0%	105	Survey marking (incl. Gbar and H- source)	16/04	22/04
<input type="checkbox"/> False floor	10 days	Thu 02/04/15	Wed 15/04/15	F. Butin	EN/MEF	0%		False floor	02/04	15/04
Lateral false floor	4 days	Thu 02/04/15	Tue 07/04/15	F. Butin	EN/MEF	0%		Lateral false floor	02/04	07/04
Hexagonal floor installation	1 wk	Thu 09/04/15	Wed 15/04/15	F. Butin	EN/MEF	0%	101	Hexagonal floor installation	09/04	15/04
<input type="checkbox"/> Cooling Network	10 days	Thu 23/04/15	Wed 06/05/15	A. Broche	EN/CV	0%		Cooling Network	23/04	06/05
Install cooling network	2 wks	Thu 23/04/15	Wed 06/05/15	A. Broche	EN/CV	0%	102	Install cooling network	23/04	06/05
