


# News from EP

Filippo Resnati

# Progress

- NP04 isolation finished. Welding of the corrugated membrane
- Rail system in the NP04 clean room installed
- NP04 clean room floor painted. SAS material and people finished tomorrow
- Cold box construction progressing well
- First APA arrived today. Procurement of the lifting tool. Careful crane handling needed
- Ready to install detector ground racks
- Metal structure for the NP02 clean room arriving on the week of the 17th of July
- Walls and roof installation on the week of the 24th of July.

# NP04 cryostat

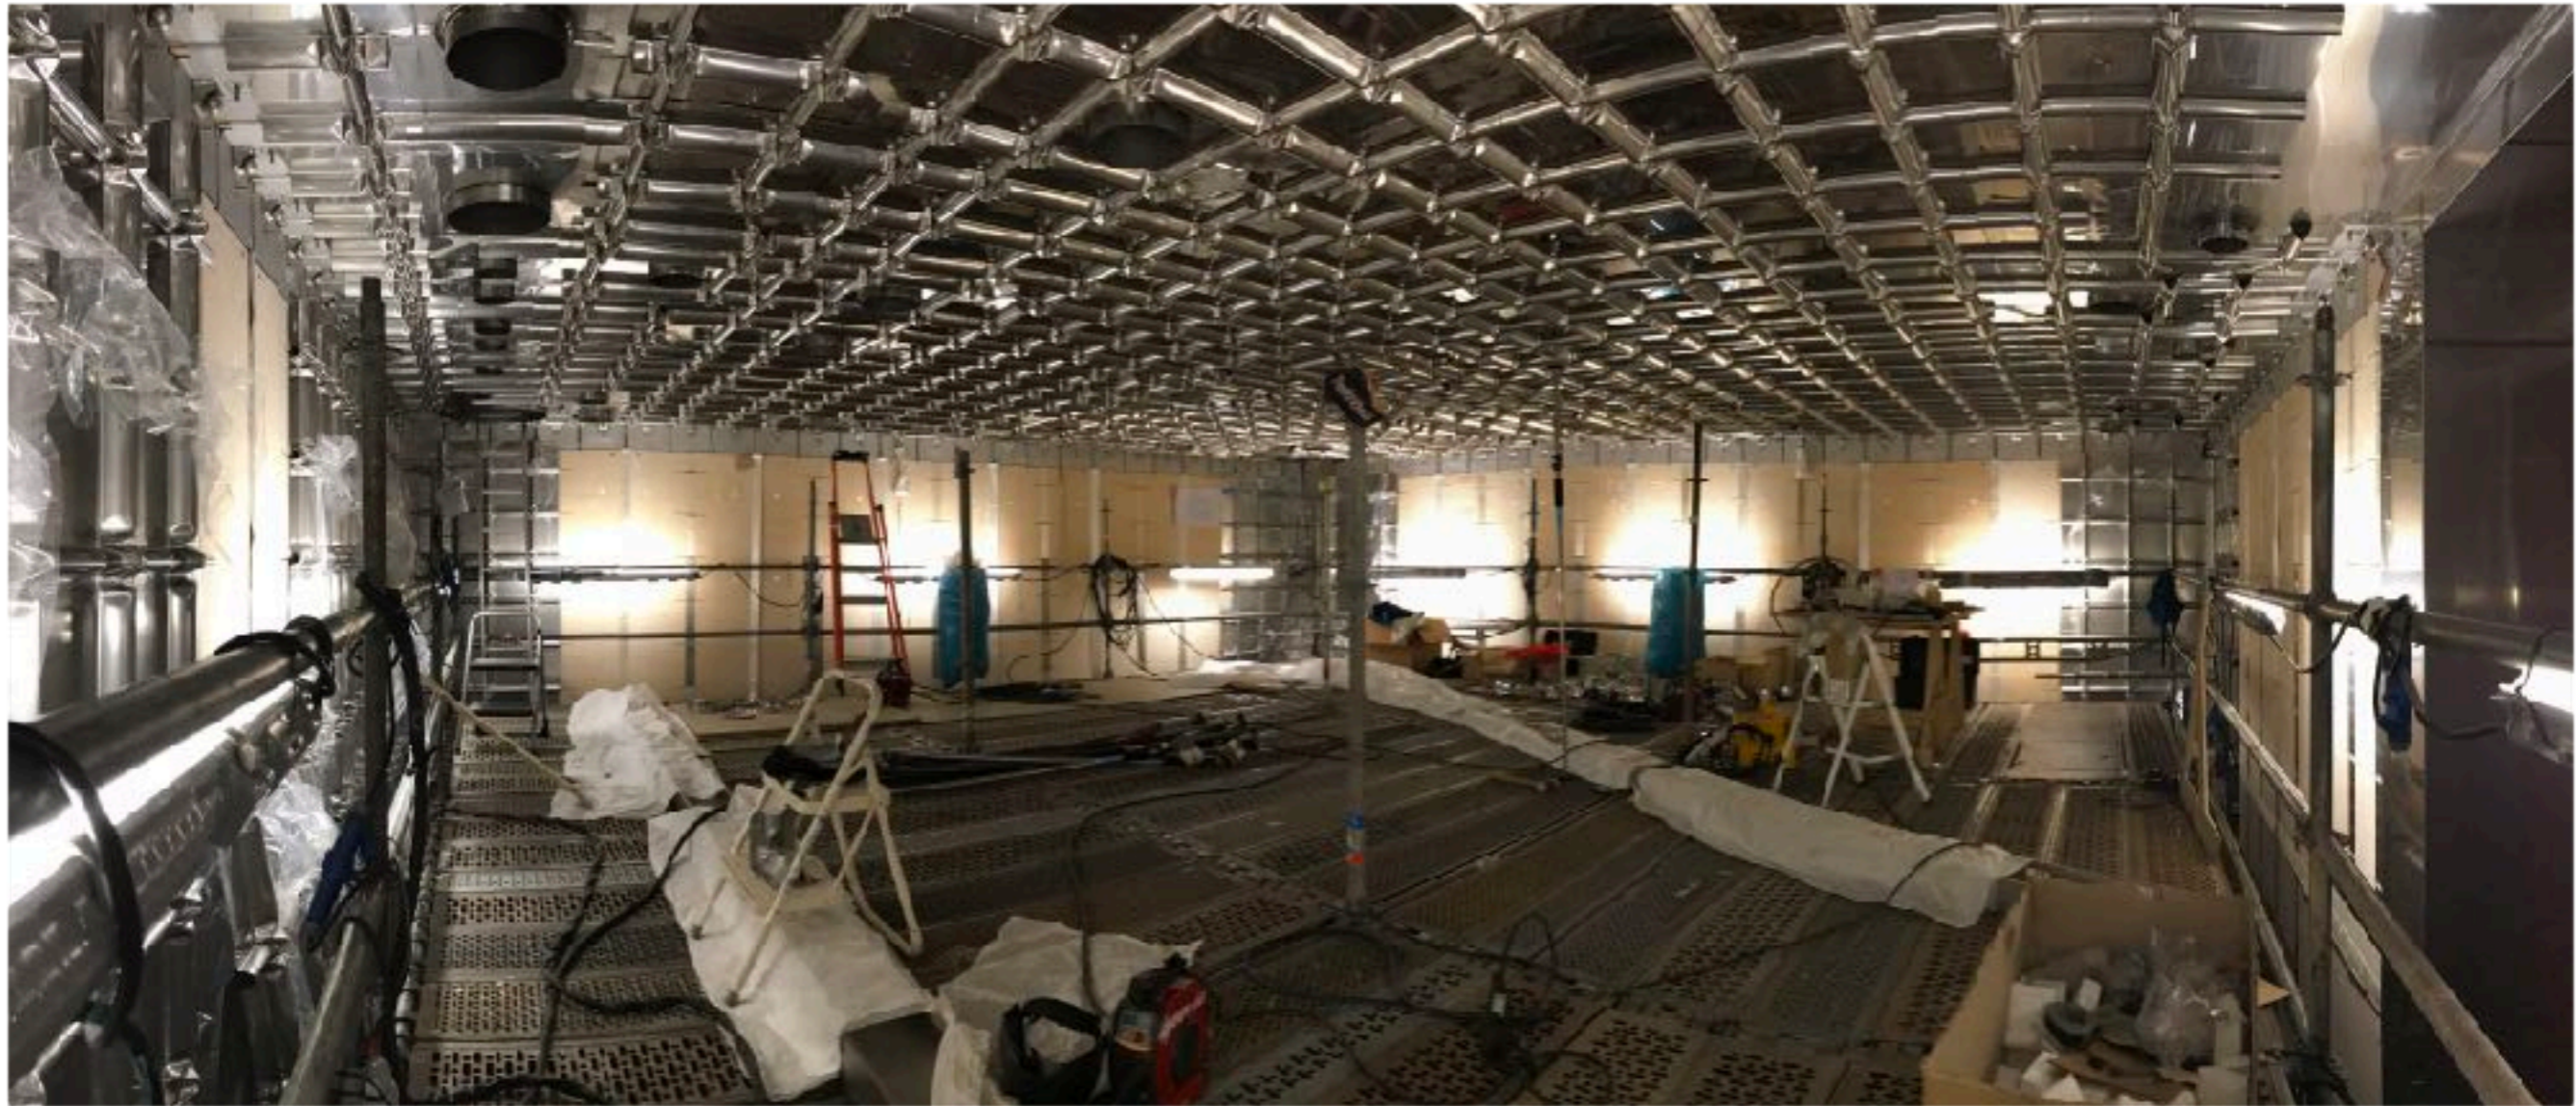

Thermal insulation installed. Welding the corrugated membrane DSS system ready, installation as soon as the roof is completed



# Clean room



Rails and trolley system installed



Thank you to everybody who worked such that the clean room was free on the 12th. Floor painting finished. Walk allowed on Monday 17th. Full dry in one week.



# Clean room



Walls and roof of the SAS persons and material finished.  
Demountable roof of the SAS material.



# Cold box





# Anode Plane Assembly



First APA arrived today (expected next Monday).  
Insertion in the clean room starting from next week
