



YETS Planning

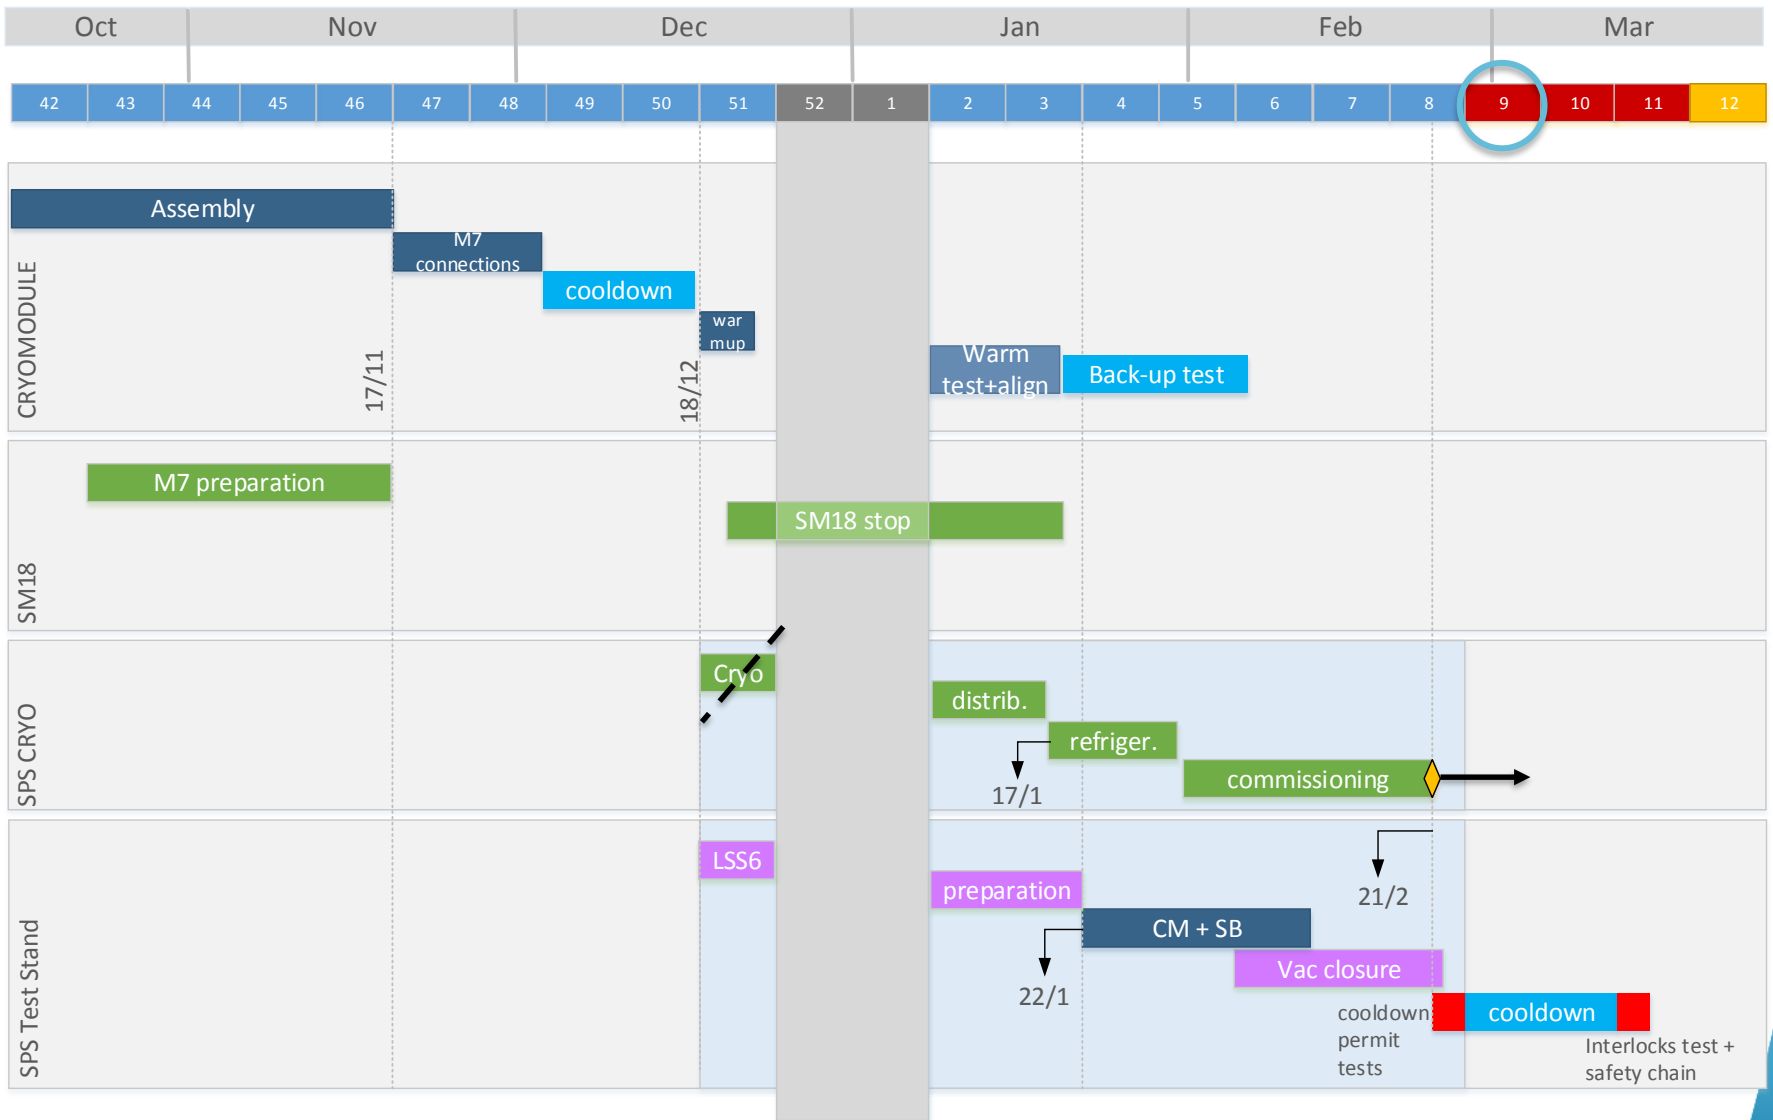

Master Schedule

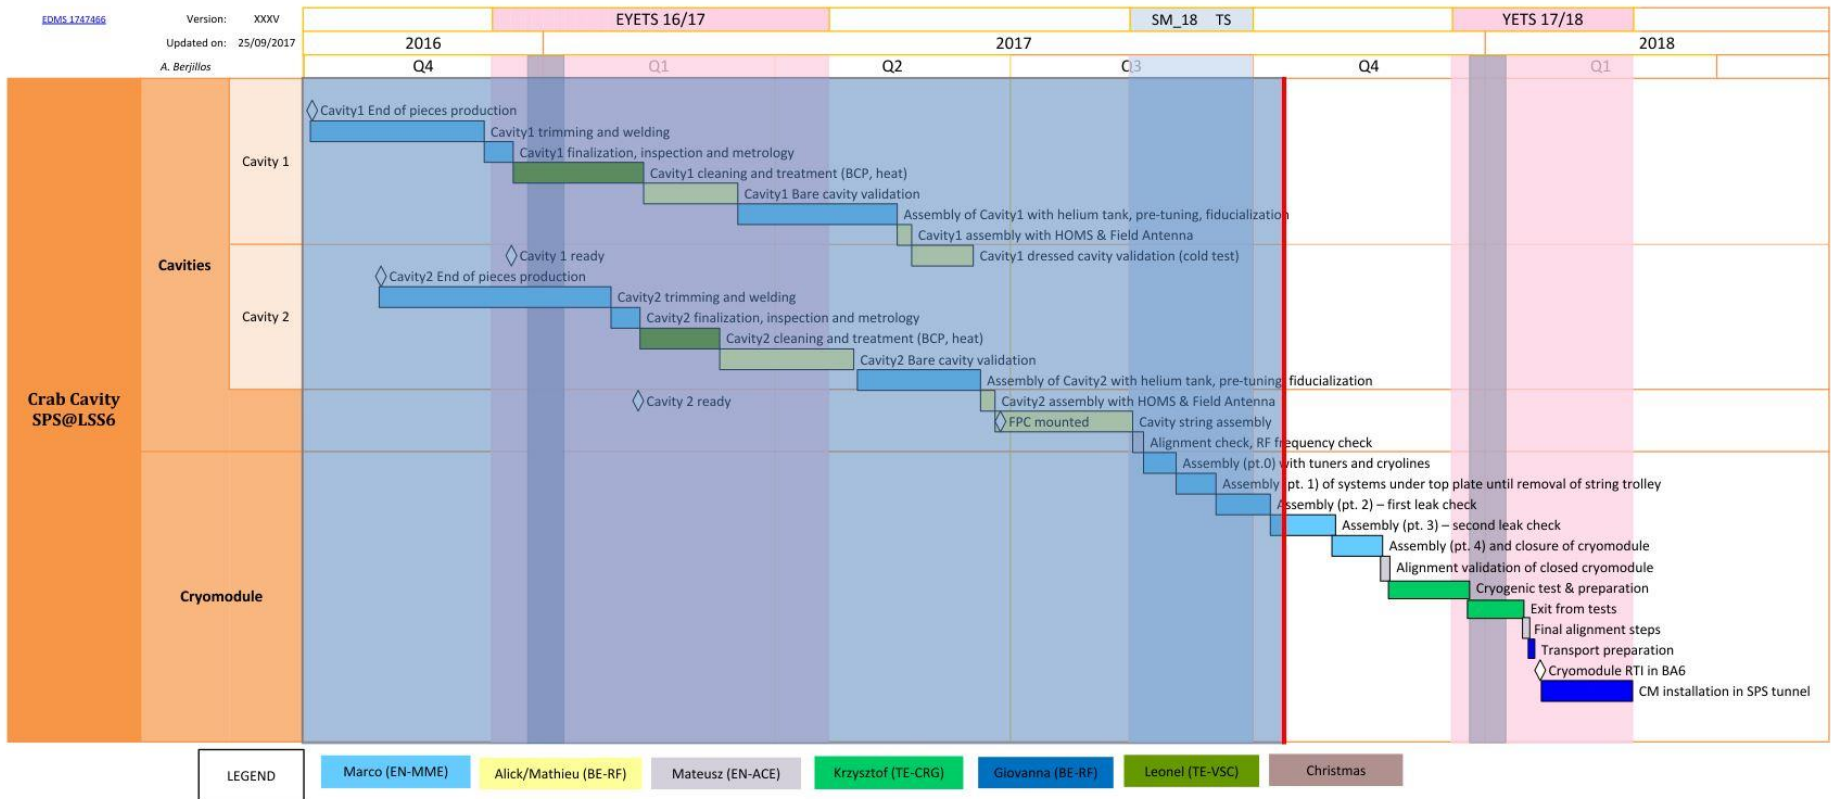

*This week's updates to be included

SM18 Test Plan

Week: 49-51
Cool-down

Christmas TS

Week: 02-03
RF/Align Checks

Week: 03-04
Cooldown
Backup

Week: 05-08
SPS Installation

	Tentative date	Temperature	Comment
Warm Measurements, cabling, instrumentation	Ongoing		
M7 Service Module Pressure Tests	16-17 Nov 17	300 K	Infrastructure Prep
Cryomodule to Bunker & Connections	20 Nov 17		
Warm Coupler Cond.			1 kW, parasitic
CM Vacuum checkout & Cooldown	4 Dec 17	300-2K	SM18-M7 Bunker
Frequency Tuning, Interlock Checkout	4-15 Dec 17		VNA, Motor Control
Q_L at 400 MHz, Full HOM spec, B-field			All RF measurements at 2K subject to the availability of time
Calibration input power (P_f, P_r, P_t)			
Coupler/Cavity Conditioning			
Kick voltage determination		2K	
LLRF loops, phase noise, stability			
Dynamic heat load, Q_0			
Warmup	18-22 Dec 17		Min 3 days
