

East Hall under construction - 1962

2nd EN-EA East Area Equipment Review Collimators planning. <u>https://indico.cern.ch/event/830225/</u>

S. Girod EN-EA







EA

EAST AREA RENOVATION

Collimators in East area

- 2 jaws collimators:
 - 2xXCSH
 - 1xXCSV

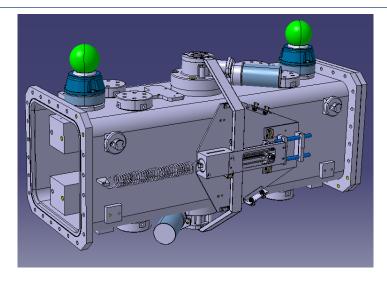

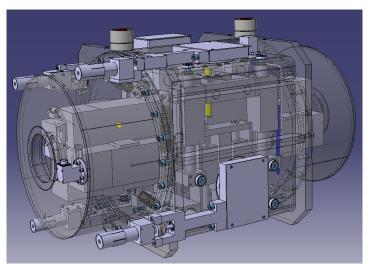

- 4 jaws collimators:
 - 4xXCHV



Collimators renovation planning

Planning LS2_EA_equipment_BIDs

						Qtr 3, 2019 Qtr 4, 2019 Qtr 1, 2020 Qtr 2, 2020 Qtr 3, 2020 Qtr 4
						Jul '19Jug '19ep '19ct '19ov '19ec '19an '20eb '20ar '20pr '20ay '20un '20ul '20ug '20ep '20ct '20o
Task Name	*	Group: 🗸	Duration 👻	Start 👻	Finish	Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct N
EAR_Equipment_BIDs			275 days	Mon 08/07/19	Fri 07/08/20	pannananananananananananananananananana
⊿ R-L40 lab			50 days	Mon 02/09/19	Thu 07/11/19	R-L40 lab
86	7-R-L40 lab re-organisation		10 wks	Mon 02/09/19	Thu 07/11/19	-867-R-L40 lab re-organisation
▲ XCHV			250 days	Mon 12/08/19	Fri 07/08/20	KCHA Antonia and
Co	mmande pieces	EN-EA	0 days	Mon 02/09/19	Mon 02/09/19	de pieces 🔶 02/09
rec	ception pieces	EN-EA	0 days	Mon 18/11/19	Mon 18/11/19	reception pieces 🗛 18/11
Pro	oduction outillage	EN-EA	13 wks	Mon 12/08/19	Thu 07/11/19	Production outillage
Re	novation XCHV 1 EAR CR-047475	EN-EA	8 wks	Mon 18/11/19	Fri 24/01/20	Renovation XCHV 1 EAR CR-047475
Re	novation XCHV 2 EAR CR-031071	EN-EA	4 wks	Mon 27/01/20	Fri 21/02/20	Renovation XCHV 2 EAR CR-031071
Re	novation XCHV 3 EAR CR-031072	EN-EA	3 wks	Mon 24/02/20	Fri 13/03/20	Renovation XCHV 3 EAR CR-031072
Re	novation XCHV 4 EAR CR-031074	EN-EA	3 wks	Mon 16/03/20	Fri 03/04/20	Renovation XCHV 4 EAR CR-031074
Ca	blage EN/STI	EN-STI	24.8 wks	Mon 17/02/20	Fri 07/08/20	Cablage EN/STI
Fid	lu EN/SMM	EN-SNM	24.8 wks	Mon 17/02/20	Fri 07/08/20	Fidu EN/SMM
⊿ XCSV/H			260 days	Mon 08/07/19	Fri 17/07/20	
Co	ntrol / mofif dossier de plan	EN-EA	5 wks	Mon 08/07/19	Fri 09/08/19	Control / mofif dossier de plan
RF	Q	EN-EA	7 wks	Mon 12/08/19	Thu 26/09/19	RFQ
Co	mmande pieces 3 coll 2b (1 EAR, 2 D)	EN-EA	0 days	Thu 26/09/19	Thu 26/09/19	(1 EAR, 2 MO) 🔶 26/09
rec	ception pieces	EN-EA	0 days	Thu 21/11/19	Thu 21/11/19	reception pieces 🔶 21/11
Pro	oduction outillage	EN-EA	15.8 wks	Mon 23/09/19	Thu 23/01/20	Production dutillage
XC	SH 1 EAR a construire T11	EN-EA	4 wks	Mon 06/04/20	Mon 04/05/20	XCSH 1 EAR a construire T11
Re	novation XCSH 2 EAR CR-027727 T9	EN-EA	4 wks	Tue 05/05/20	Mon 01/06/20	Renovation XCSH 2 EAR CR-02
Re	novation XCHV 3 EAR CR-031079 T9	EN-EA	2 wks	Tue 02/06/20	Mon 15/06/20	Renovation XCHV 3 EAR CR
Ca	blage STI	EN-STI	12.8 wks	Mon 20/04/20	Fri 17/07/20	Cablage STI



Divers

- 10 universal tables ordered \rightarrow delivery Sep 2019
- 3 tanks XBPF with XBPF flanges ordered \rightarrow delivery Nov 2019
 - 6 flanges DN219 to be send to the manufacturer (via P. Frichot)
- 1 tank XBPF with flanges available at 867/R-L40

