

*East Hall under construction - 1962*

# Planning EA Deliverables

E. Harrouch



ENGINEERING  
DEPARTMENT



**EAST AREA RENOVATION**








# Jan 2020 – Jun 2020

Date with margin

Date without margin

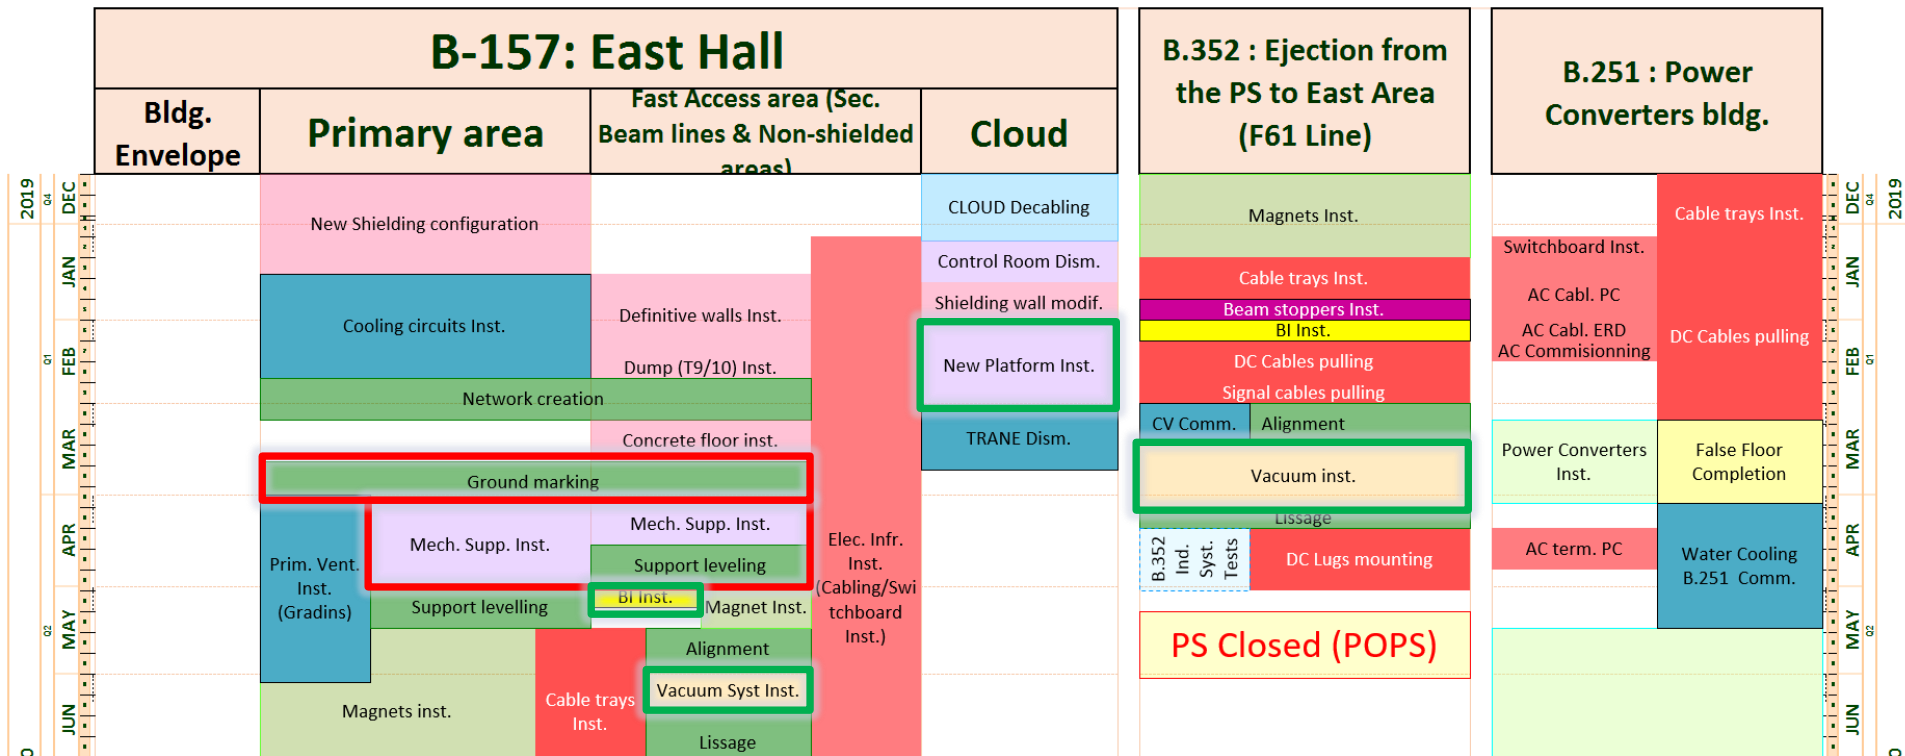

## B.157 :

- Optics : MadX files to be sent to the surveyors (4wks before marking) : 15/02/20 (No Slack)
- Mechanical supports for F63, T08, T09, T10, T11 : Ready for inst. 01/04/20 (No Slack)
- Instrumentation Exp Area (XCET, XSCI, XBPF) : 01/05/20 (~3mo slack)
- Vacuum system EA: T09, T10, T11 : Ready for inst. 01/06/20 (~3mo slack)
- CLOUD Platform : Ready for inst. 01/02/2020 (~1y slack)


## B.352 :

- Vacuum system : F61, F62, F6D, T8 : Ready for inst. 10/03/20 (~2mo slack)

# Jul 2020 – Dec 2020

Date with margin

Date without margin

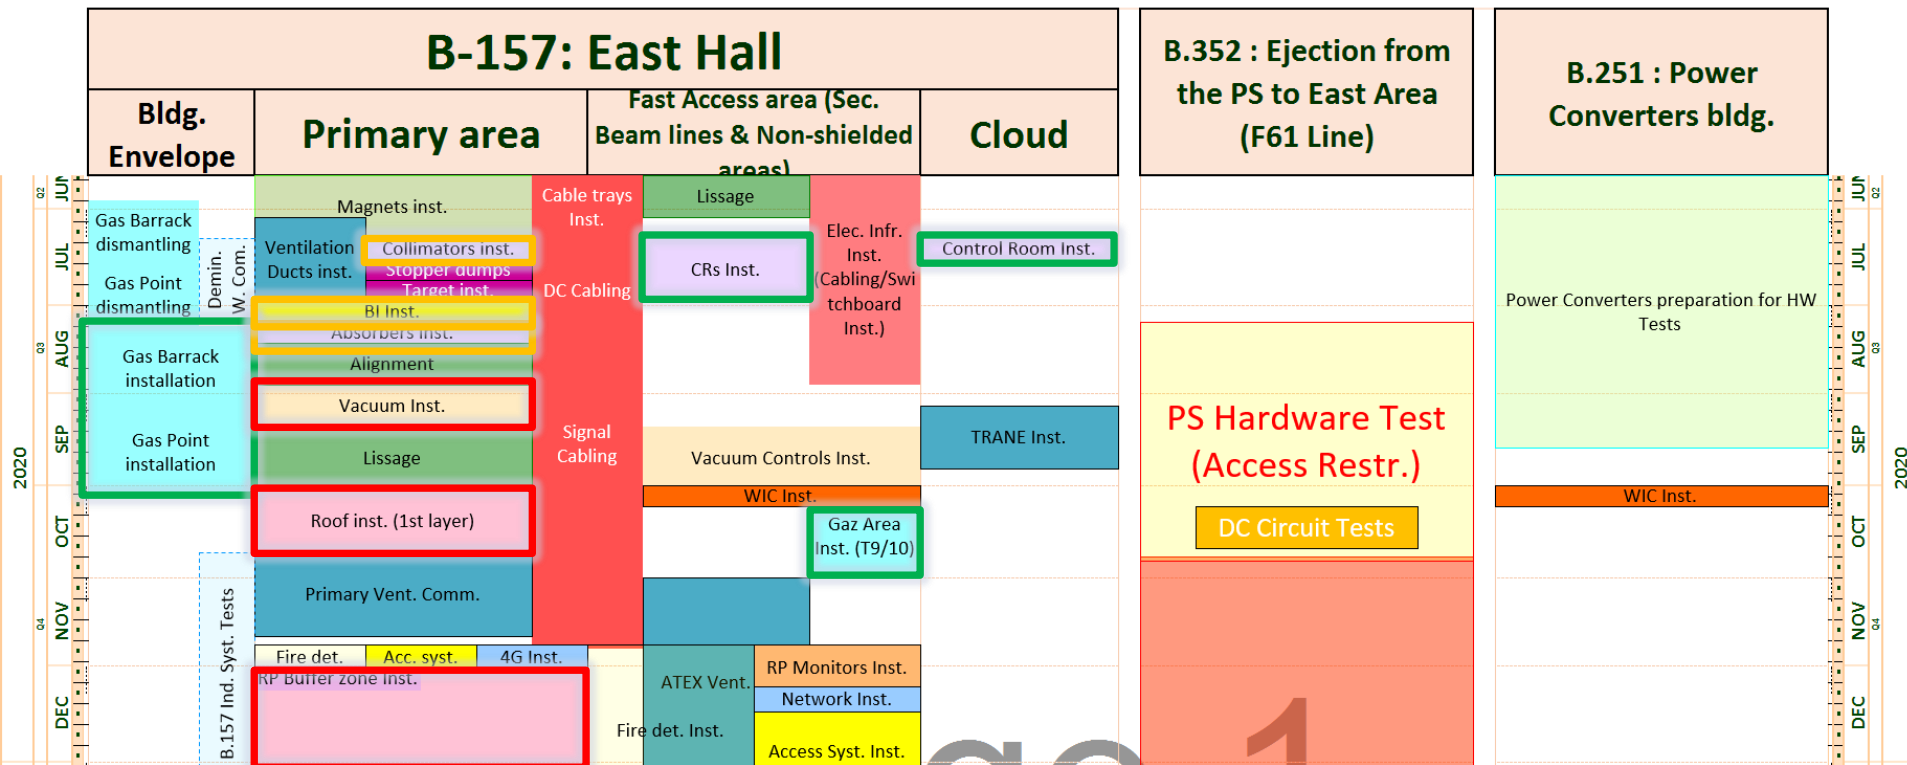


## B.157 :

- Gas systems : Installation start 01/08/20 (~5mo slack)
- TCX, Collimators, absorbers : Installation start 15/07/20 (~1mo slack)
- Vacuum system Prim. And mixed Area: T08, T09, T10, T11 : Ready for inst. 01/09/20 (No Slack)
- 1st layer of the roof of primary area (Beams + Sealing) : 01/10/20 (No Slack)
- Supporting structure for the mixed area + completion of the roof : 01/10/20 (No Slack)
- Control rooms : Installation start 01/07/20 (~6mo slack)

# Jan 2021 – May 2021

Date with margin

Date without margin

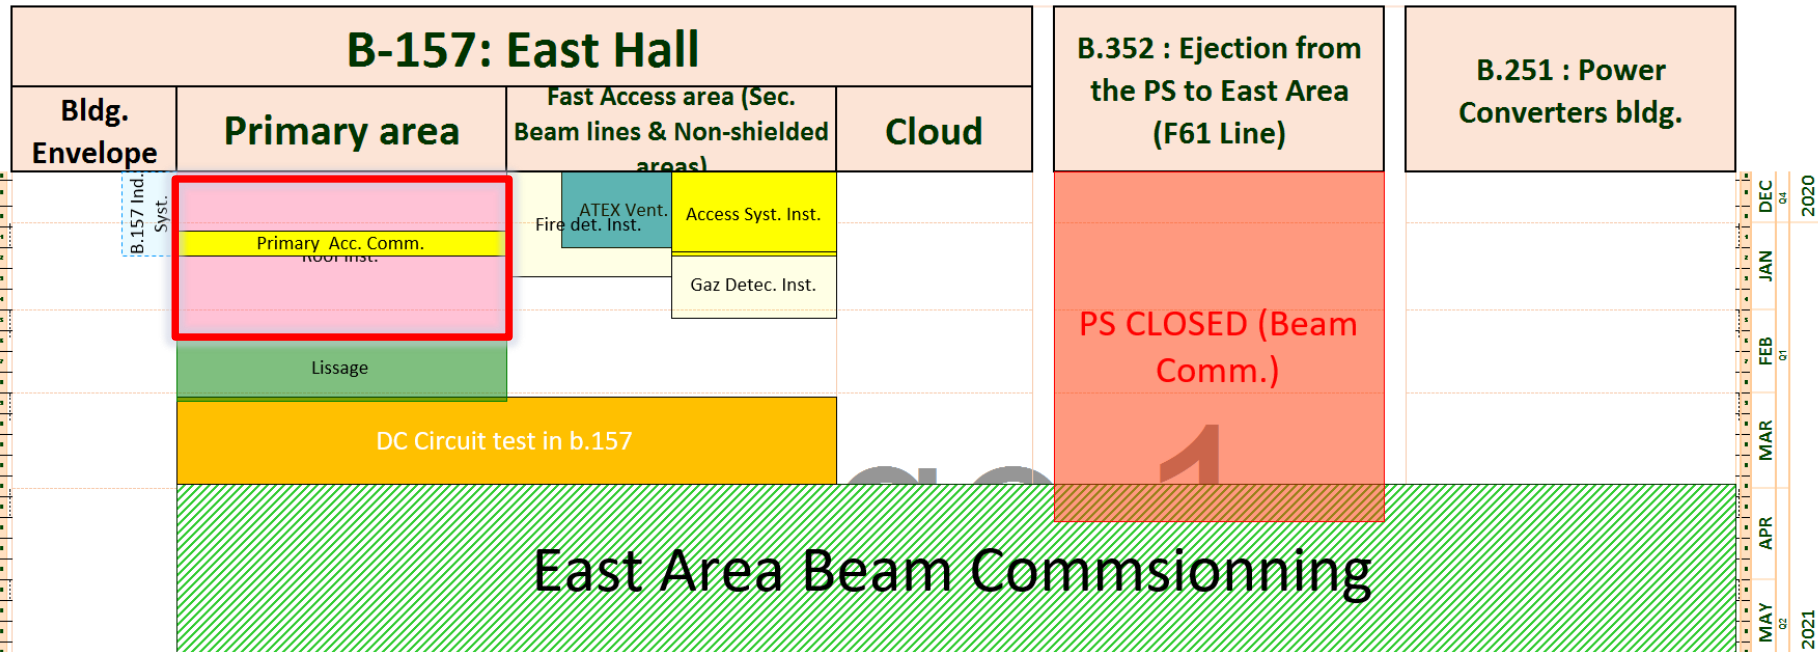

Commissioning = Readiness of the group to operate the area (Controls, commissioning plan, ...)



# Thanks for your attention !



## **EAST AREA RENOVATION**
