

East Hall under construction - 1962

### 4<sup>nd</sup> EN-EA East Area Equipment Review Collimators planning. <u>https://indico.cern.ch/event/860674/</u>

S. Girod EN-EA







**EAST AREA RENOVATION** 

# **Collimators in East area**

- 2 jaws collimators:
  - 2xXCSH
  - 1xXCSV

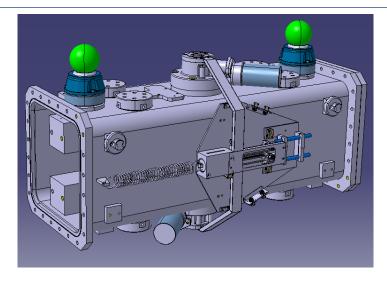

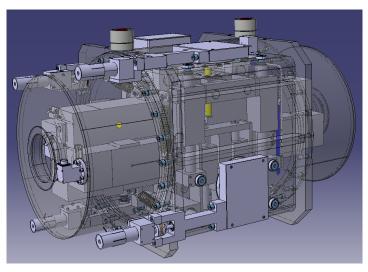

- 4 jaws collimators:
  - 4xXCHV



# **Collimators renovation planning**

#### Planning LS2\_EA\_equipment\_BIDs

						Qtr 3, 2019 Qtr 4	4, 2019 Qtr 1, 2020 Qtr 2, 2020 Qtr 3, 2020 Qtr 4
						lul '19\ug '19ep '19ct '19o	w '1)ec '1!an '2(eb '2(lar '2)pr '2(lay '2)un '2(lul '2(lug '2)ep '2()ct '2(lo
Task Nar	me 🔻	Group: 🗸	Duration 👻	Start 👻	Finish	Jul Aug Sep Oct M	Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct M
EAR_Equipment_BIDs			275 days	Mon 08/07/19	Fri 07/08/20	Υ <mark>γ</mark>	
⊿ R-L	.40 lab		50 days	Mon 02/09/19	Thu 07/11/19	R-L40 lab 🔽	2
8	867-R-L40 lab re-organisation		10 wks	Mon 02/09/19	Thu 07/11/19		867-R-L40 lab re-organisation
⊿ XC	HV		250 days	Mon 12/08/19	Fri 07/08/20	КСНЛ Данана и на	Common and the common
(	Commande pieces	EN-EA	0 days	Mon 02/09/19	Mon 02/09/19	de pieces 🔶 <del>02/09</del>	
r	reception pieces	EN-EA	0 days	Mon 18/11/19	Mon 18/11/19	reception pieces	• 18/11
F	Production outillage	EN-EA	13 wks	Mon 12/08/19	Thu 07/11/19		Production outillage
l i	Renovation XCHV 1 EAR CR-047475	EN-EA	8 wks	Mon 18/11/19	Fri 24/01/20		Renovation XCHV 1 EAR CR-047475
F	Renovation XCHV 2 EAR CR-031071	EN-EA	4 wks	Mon 27/01/20	Fri 21/02/20		Renovation XCHV 2 EAR CR-031071
1	Renovation XCHV 3 EAR CR-031072	EN-EA	3 wks	Mon 24/02/20	Fri 13/03/20		Renovation XCHV 3 EAR CR-031072
F	Renovation XCHV 4 EAR CR-031074	EN-EA	3 wks	Mon 16/03/20	Fri 03/04/20		Renovation XCHV 4 EAR CR-031074
(	Cablage EN/STI	EN-STI	24.8 wks	Mon 17/02/20	Fri 07/08/20		Cablage EN/STI
F	Fidu EN/SMM	EN-SNM	24.8 wks	Mon 17/02/20	Fri 07/08/20		Fidu EN/SMM
⊿ XC	sv/H		260 days	Mon 08/07/19	Fri 17/07/20	<b>Q</b>	
(	Control / mofif dossier de plan	EN-EA	5 wks	Mon 08/07/19	Fri 09/08/19	Control / mofif	dossier de plan
F	RFQ	EN-EA	7 wks	Mon 12/08/19	Thu 26/09/19	RFQ	
	Commande pieces 3 coll 2b (1 EAR, 2 MO)	EN-EA	0 days	Thu 26/09/19	Thu 26/09/19	(1 EAR, 2 MO) <mark>ቅ 26/0</mark> 9	
r	reception pieces	EN-EA	0 days	Thu 21/11/19	Thu 21/11/19	reception piece	21/11
F	Production outillage	EN-EA	15.8 wks	Mon 23/09/19	Thu 23/01/20		Production dutillage
)	XCSH 1 EAR a construire T11	EN-EA	4 wks	Mon 06/04/20	Mon 04/05/20		XCSH 1 EAR a construire T11
F	Renovation XCSH 2 EAR CR-027727 T9	EN-EA	4 wks	Tue 05/05/20	Mon 01/06/20		Renovation XCSH 2 EAR CR-0
F	Renovation XCHV 3 EAR CR-031079 T9	EN-EA	2 wks	Tue 02/06/20	Mon 15/06/20		📩 Renovation XCHV 3 EAR C
(	Cablage STI	EN-STI	12.8 wks	Mon 20/04/20	Fri 17/07/20		Cablage STI



## **Divers**

- 10 universal tables ordered  $\rightarrow$  delivery Sep 2019
- 3 tanks XBPF with XBPF flanges ordered  $\rightarrow$  delivery Nov 2019
  - 6 flanges DN219 to be send to the manufacturer (via P. Frichot)
- 1 tank XBPF with flanges available at 867/R-L40

