

East Hall under construction - 1962

EA Renovation project team meeting # 37

Building 251

Gurkan Dogru/ EN-EA, 03-07-2020



ENGINEERING
DEPARTMENT




EAST AREA RENOVATION



False floor metallic structure to install (red color)

 To install

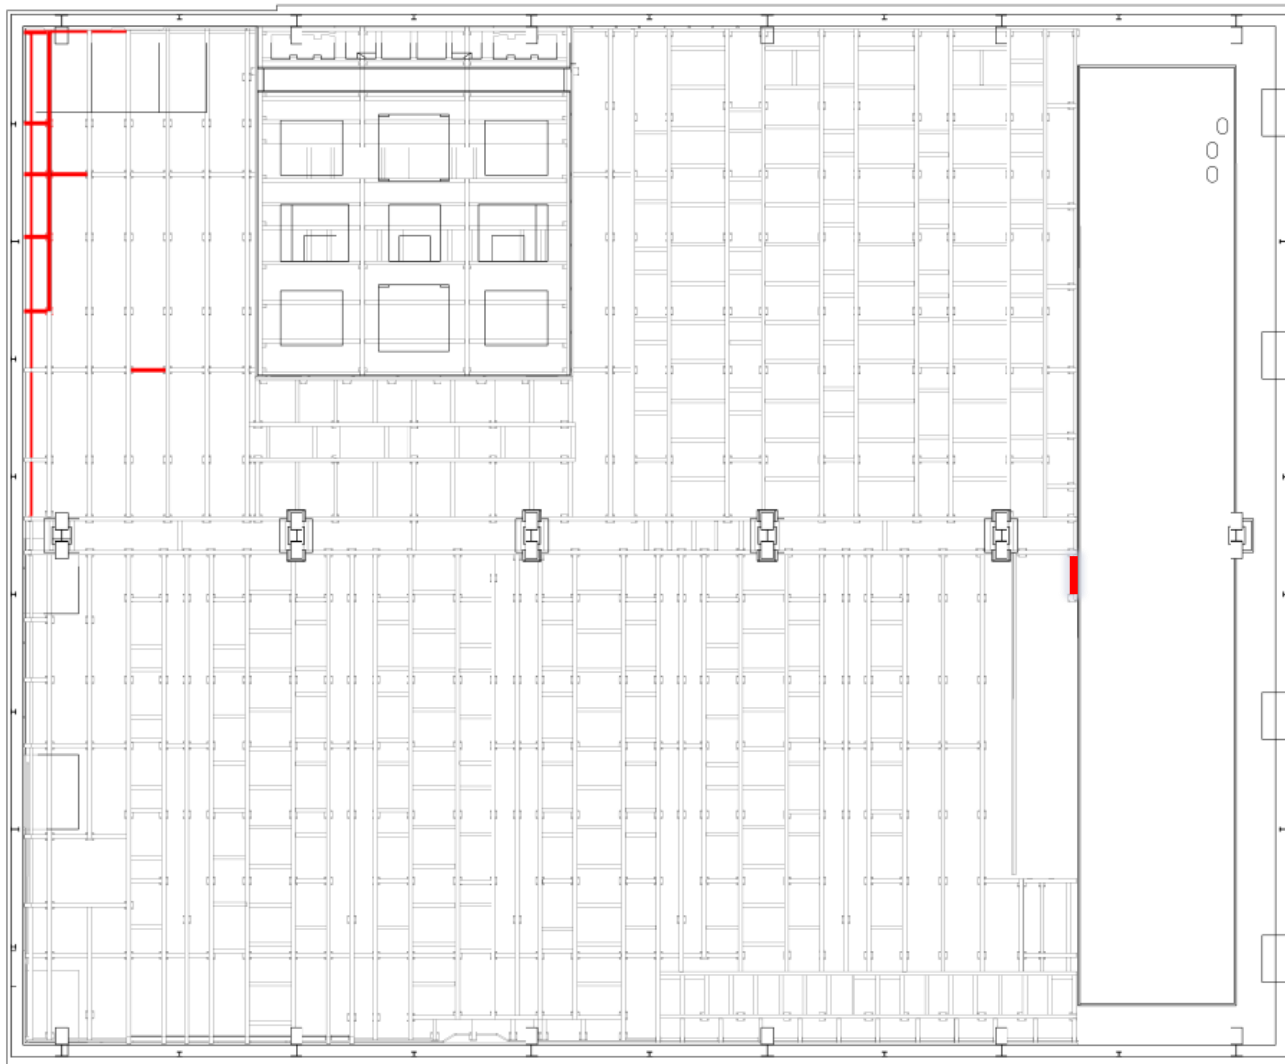


False floor metallic structure to install



DC cabling

Pulling completed


Remains the test of DC cables

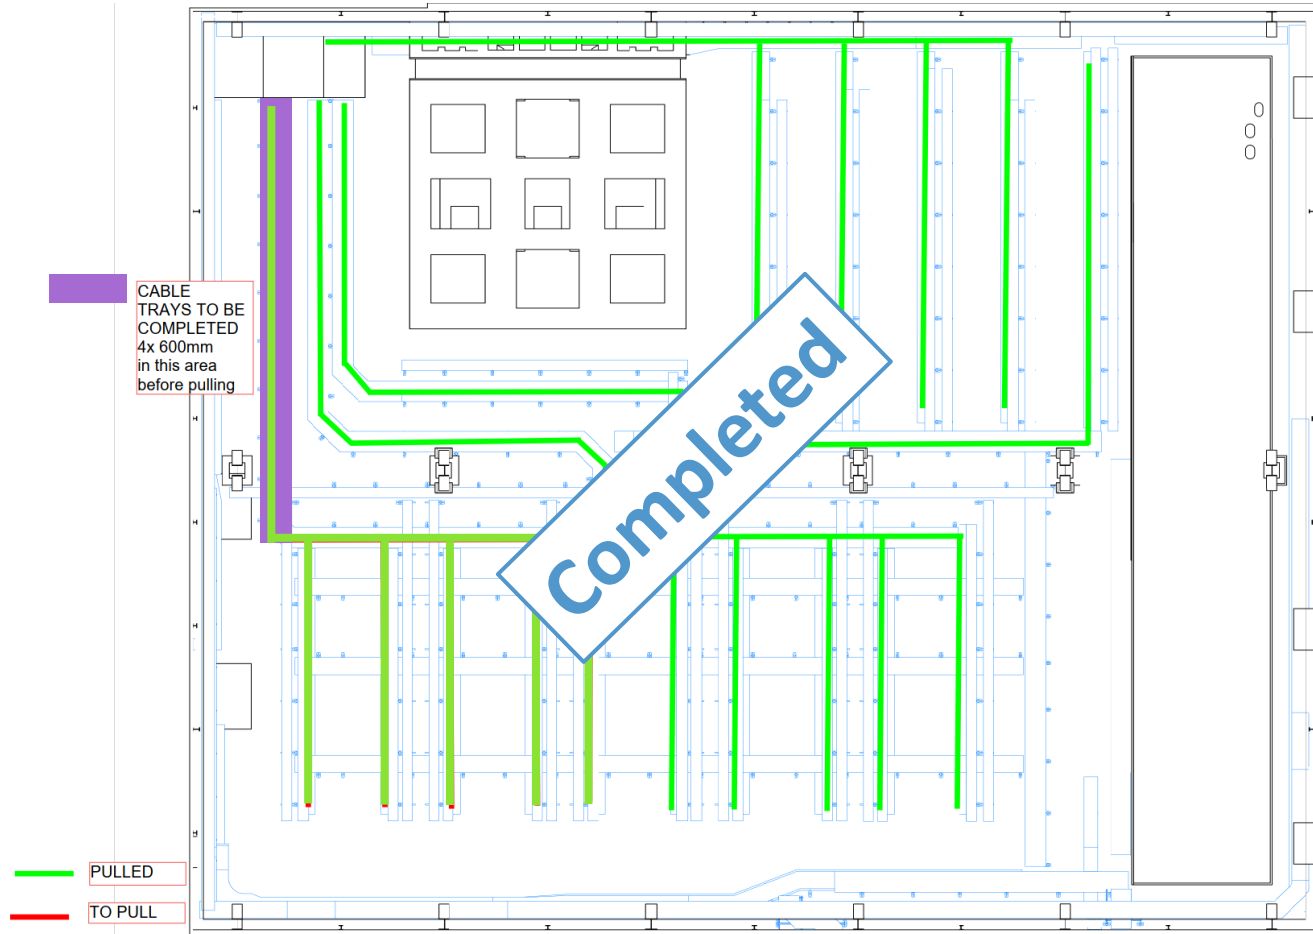

AC cabling

Pulling completed

Remains one cabletray to install

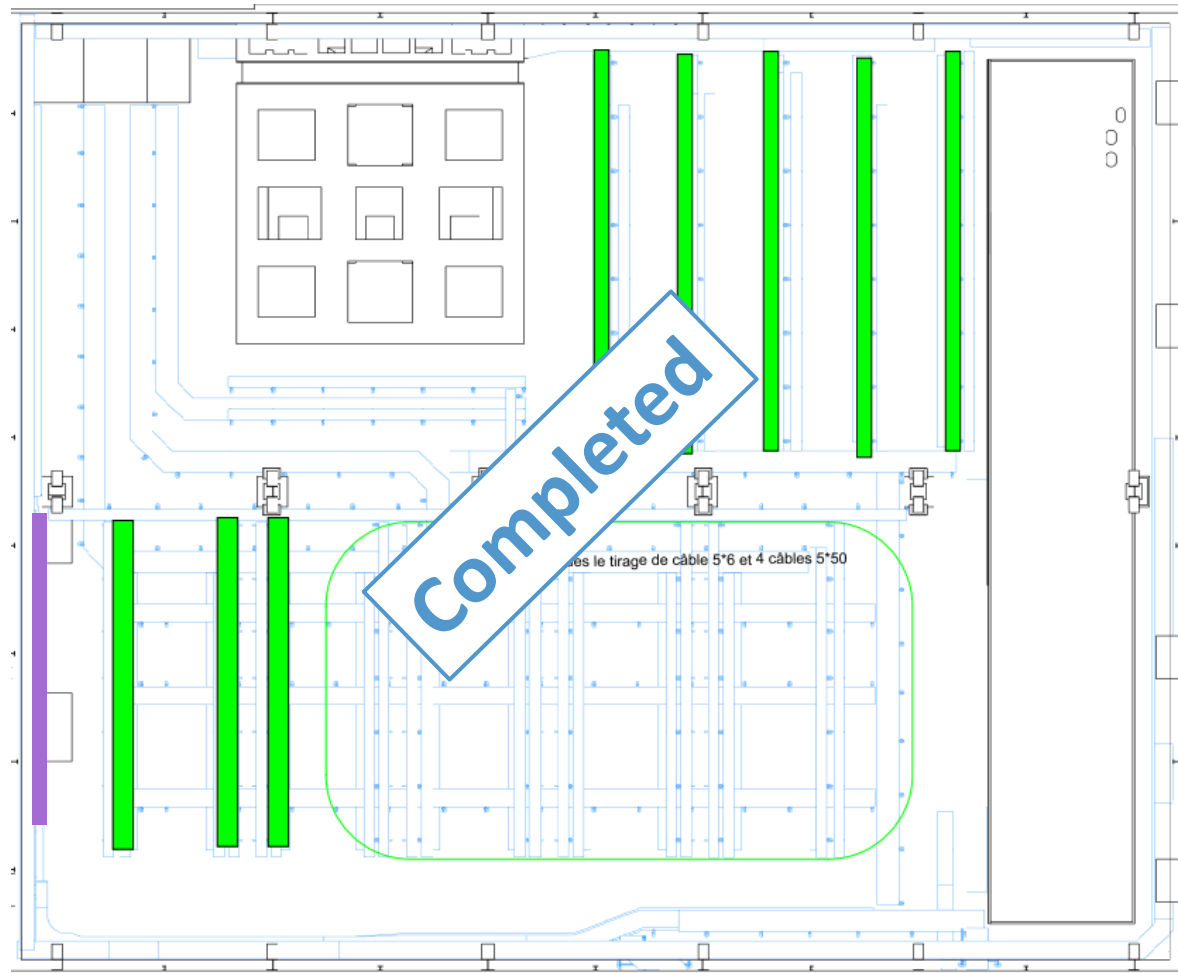


Cabletrays to install

Completed

Après le tirage de câble 5*6 et 4 câbles 5*50

Racks to install

5 Racks to install
(3 of five were installed
this week)

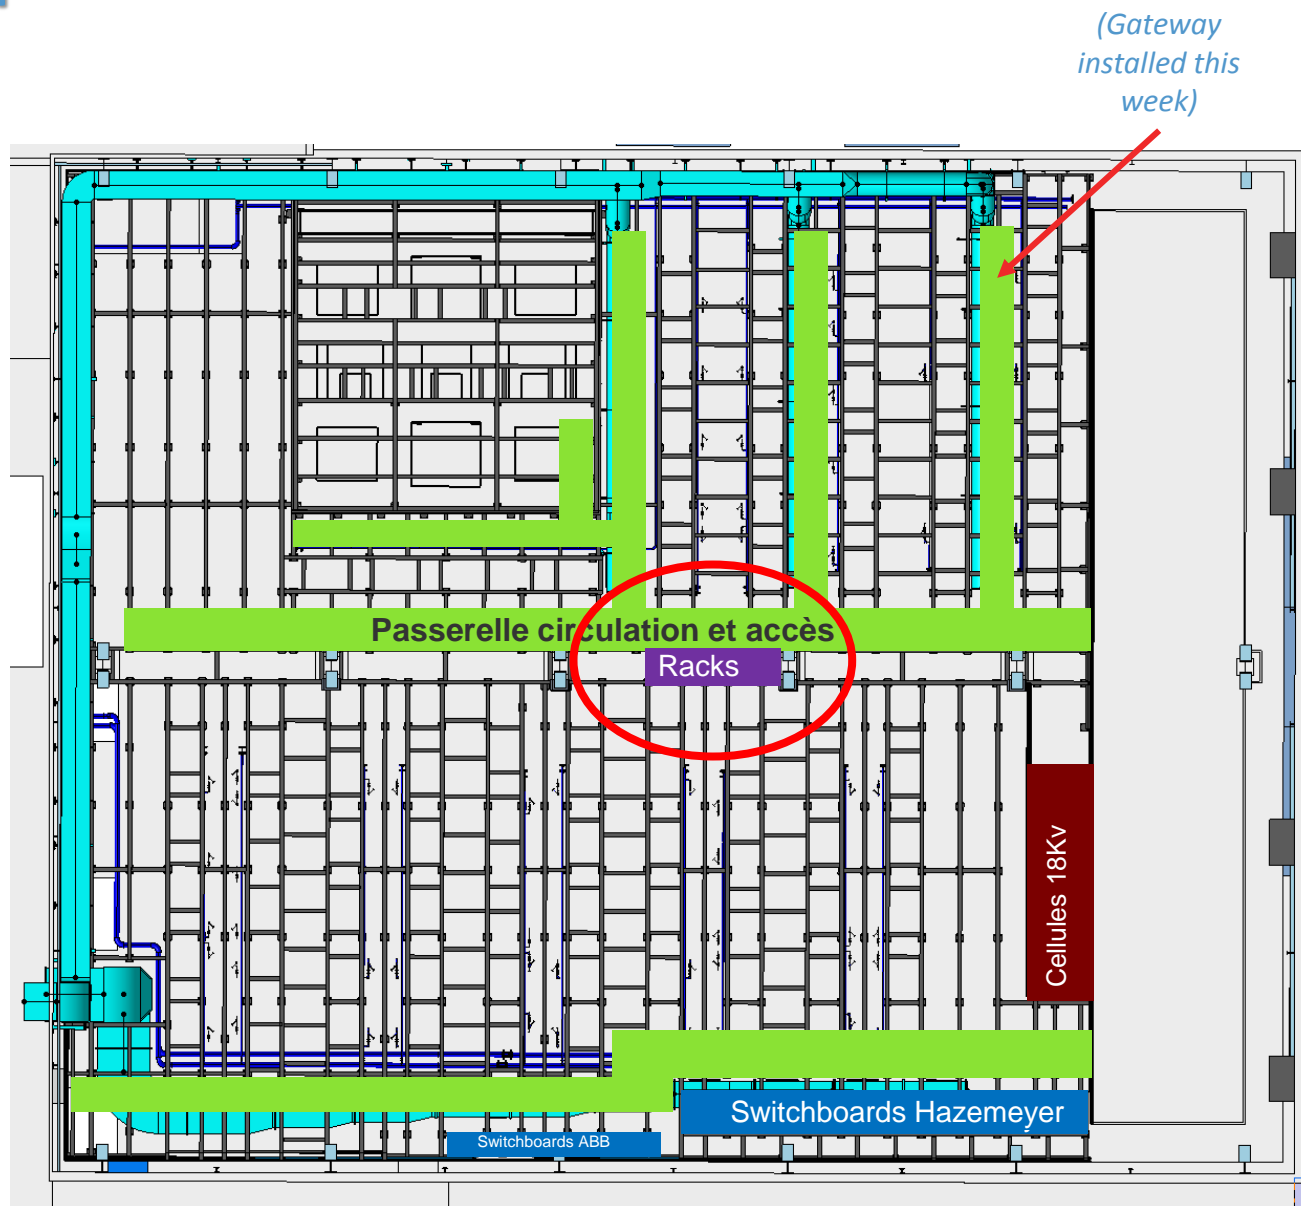

IT cables to pull


IT-CS:

IT cables to pull

Start 02.07 to 03.07

EN-CV:

Panoplies installation

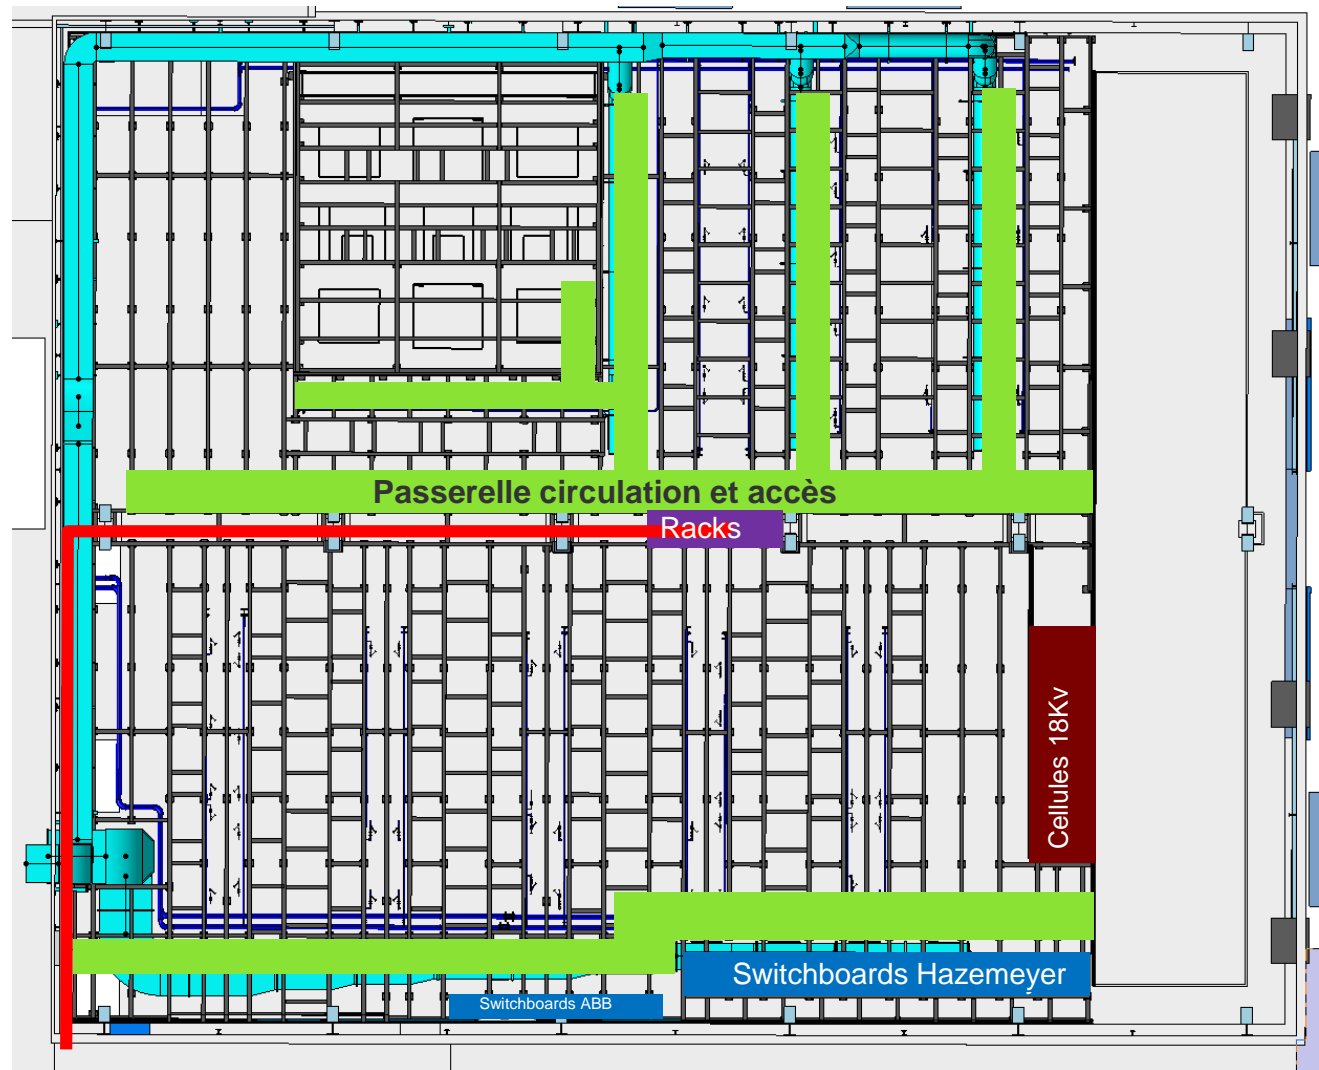

Cleaning & Gateways – Start 06.07 to 10.07

EN-CV

There will be a pressure test on the water pipes this week.


For 2 hours there should be no other activity in the building.

DOSIM:


Cleaning activity
Zone 1 first

OUVAROFF:

Gateways to remove
(Priority)

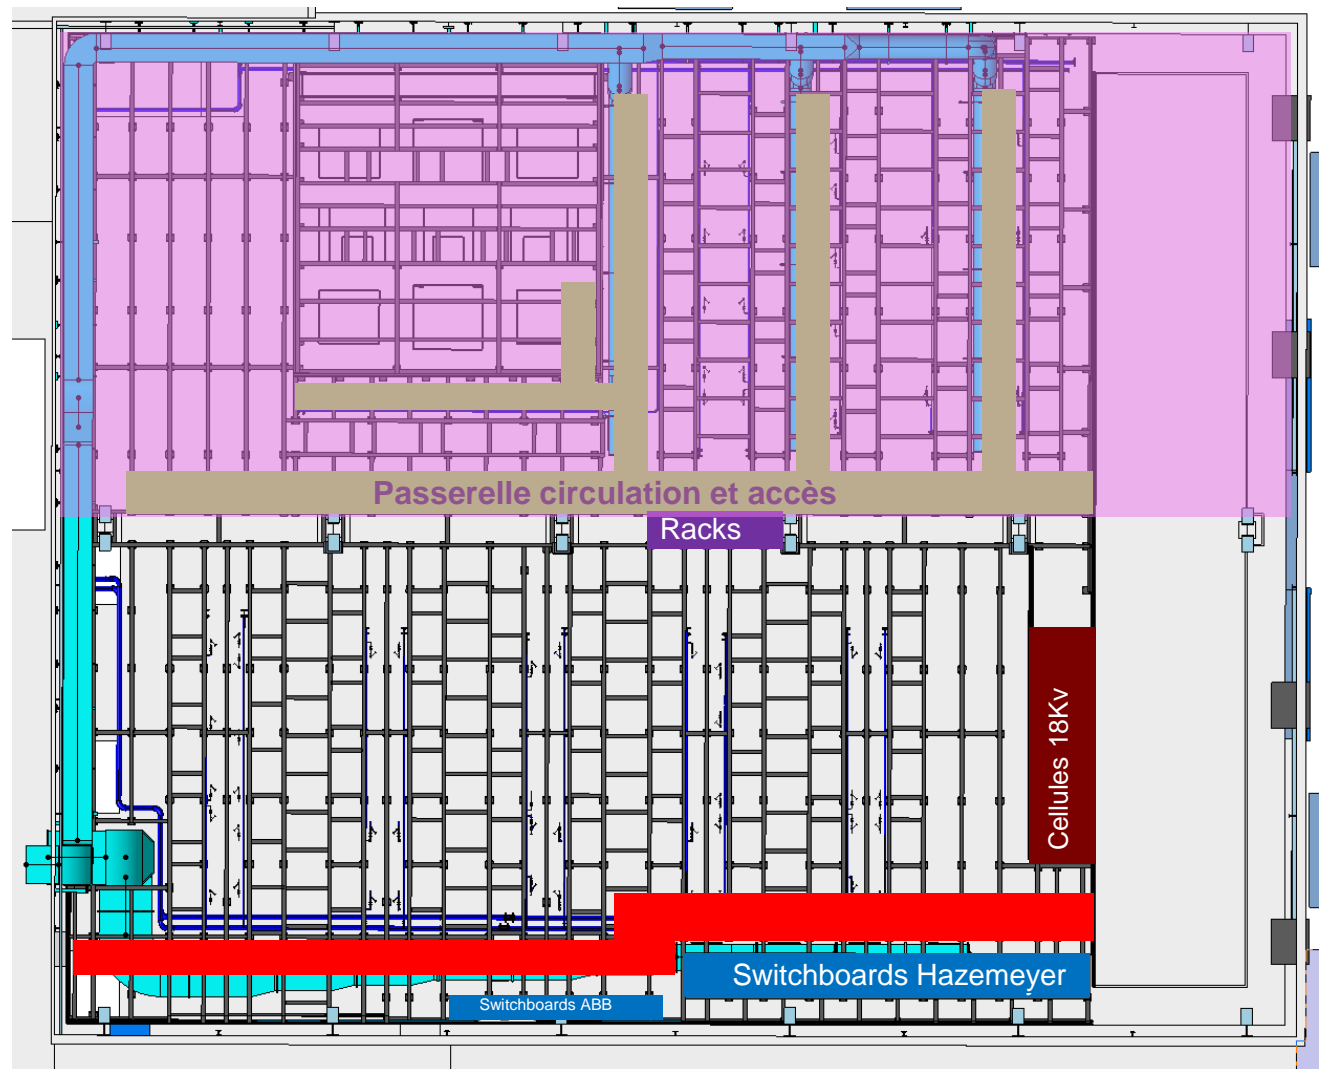

Cleaning – Start 06.07 to 10.07

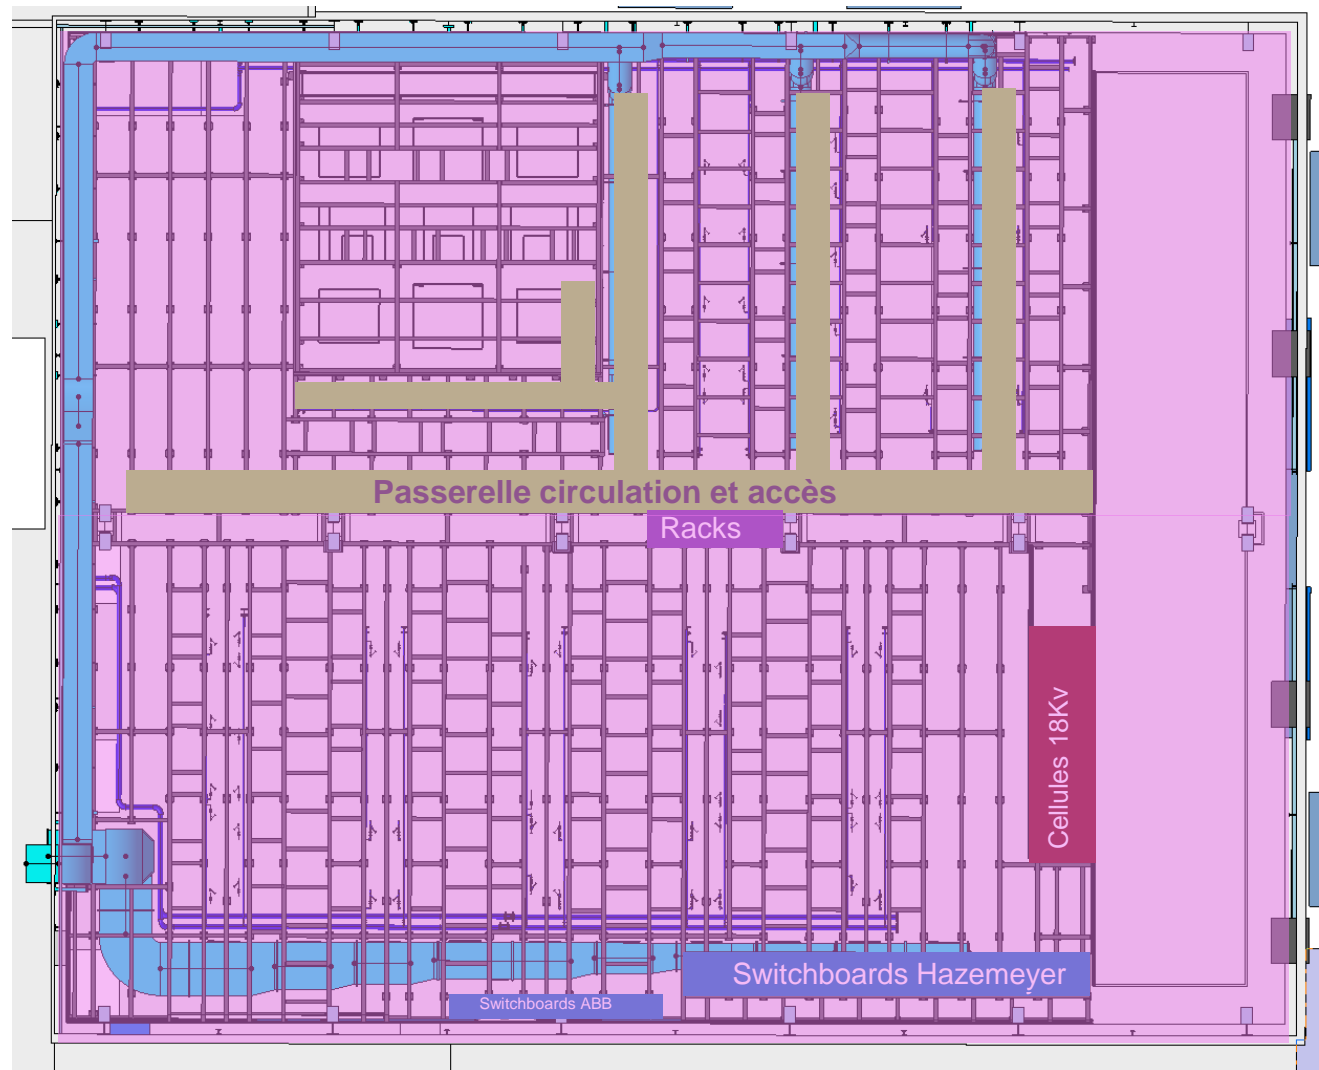


DOSIM:
Cleaning activity - Zone 2

Converters to install – Gateways to install

– Start 13.07 to 07.08

TE-EPC:
Converters to install
Priority zone 1

OVAROFF:
Gateways to install
Zone 2 (4 days)

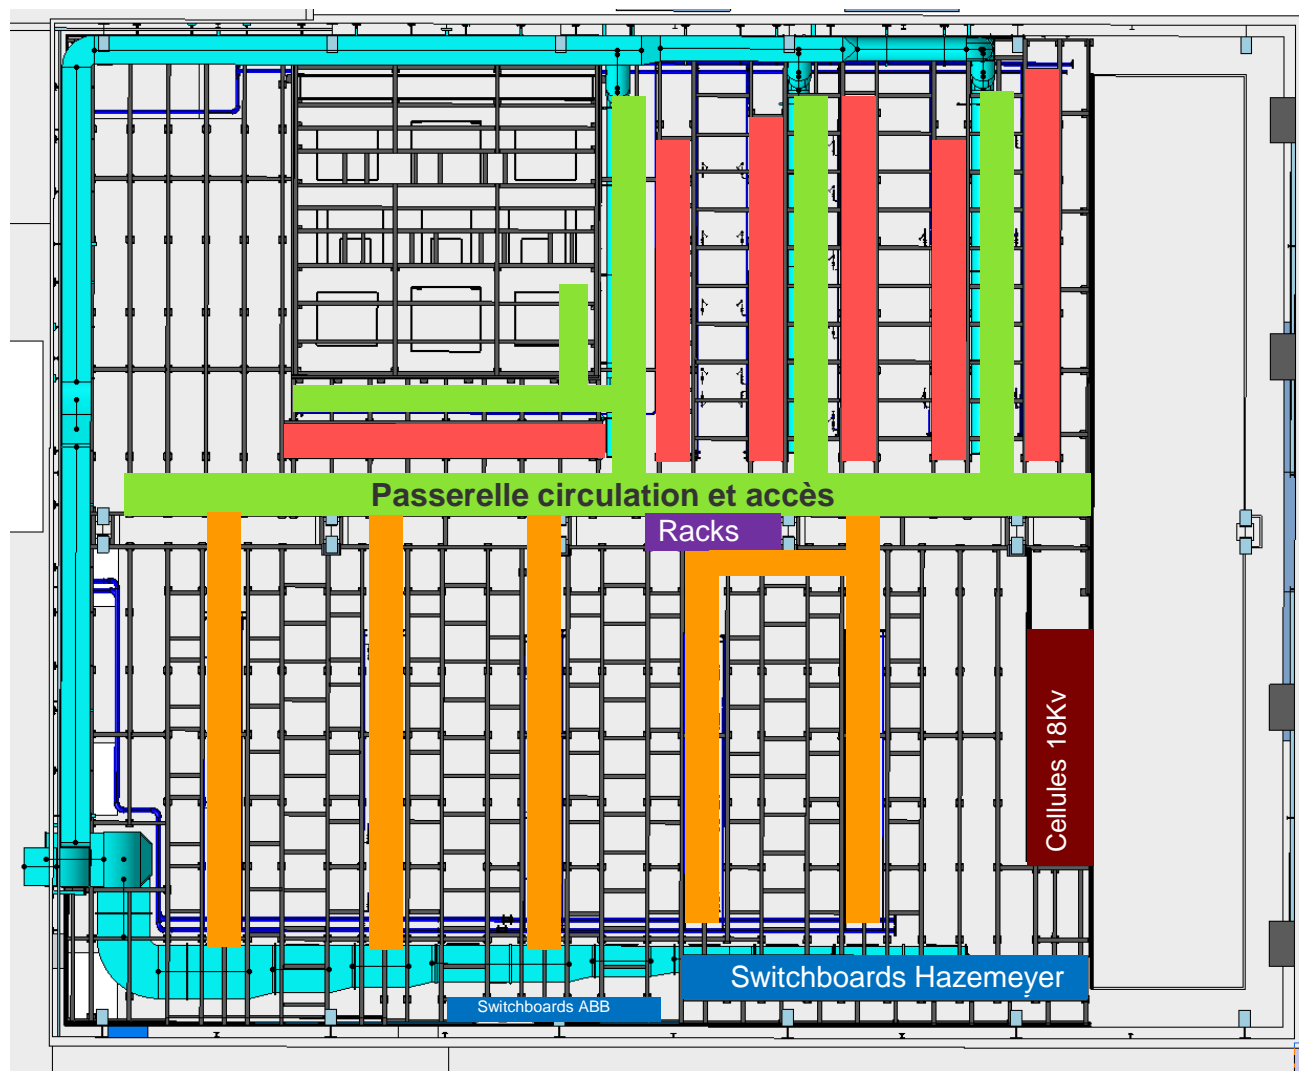


Converters to install – EN-EL

– Start 13.07 to 07.08

TE-EPC:
Converters to install
Zone 2

EN-EL:
Tests of DC cables ?

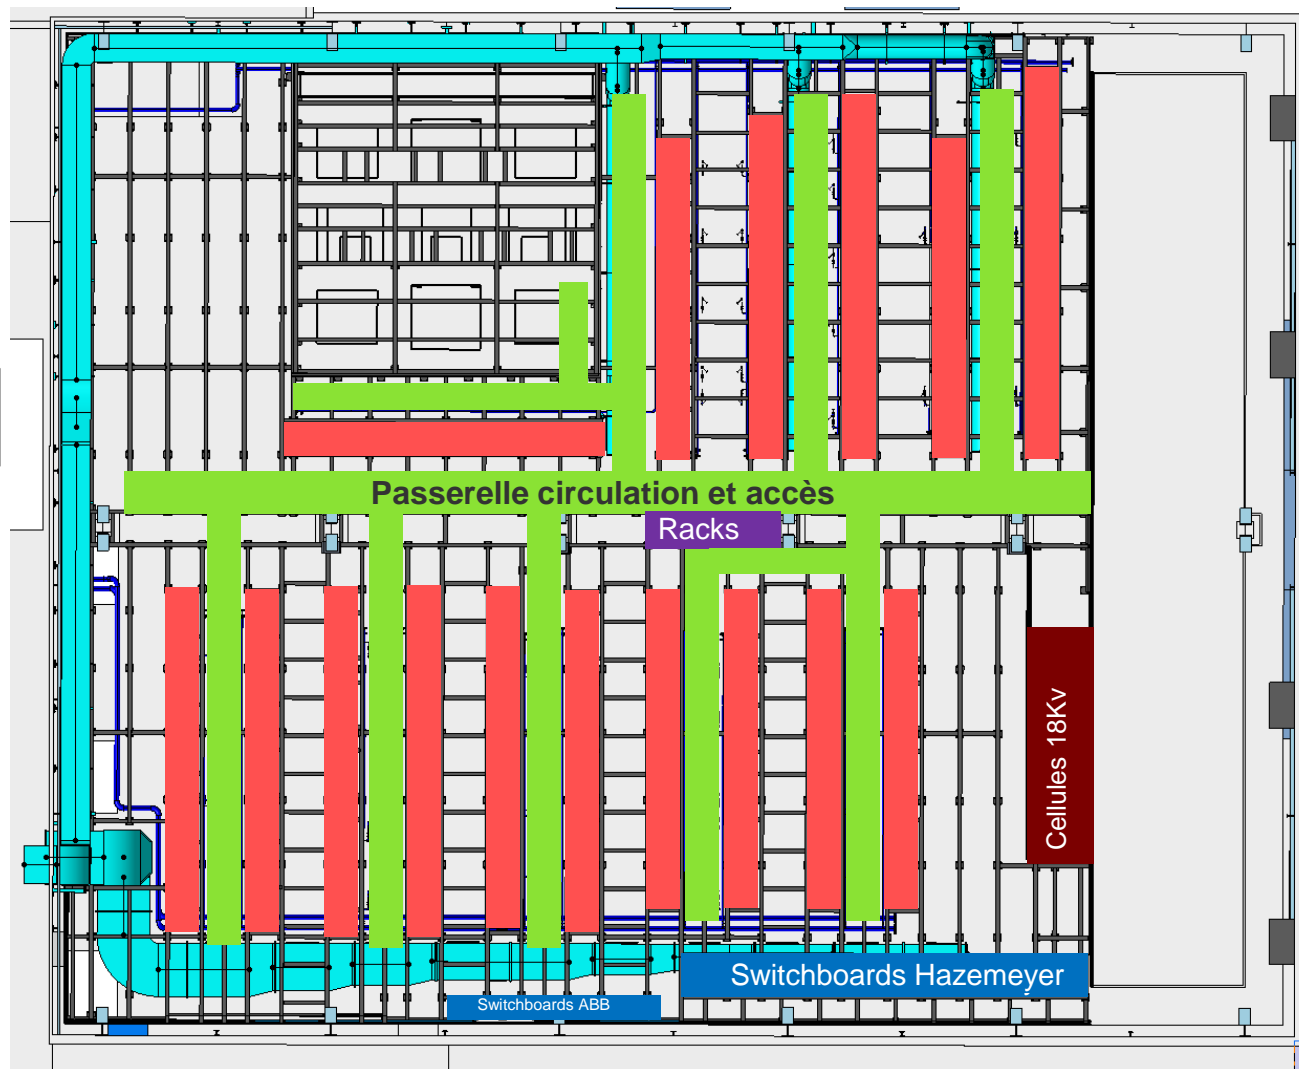

EN-EL, EN-CV, TE-EPC connections

– Start 10.08 to ?

TE-EPC:


Connection activity
Start on 10.08 ?
Duration ? Weeks

EN-EL:

Connection activity
Start on 10.08 ?
Duration ? weeks

EN-CV:

Connection activity
Start on 10.08 ?
Duration ? weeks

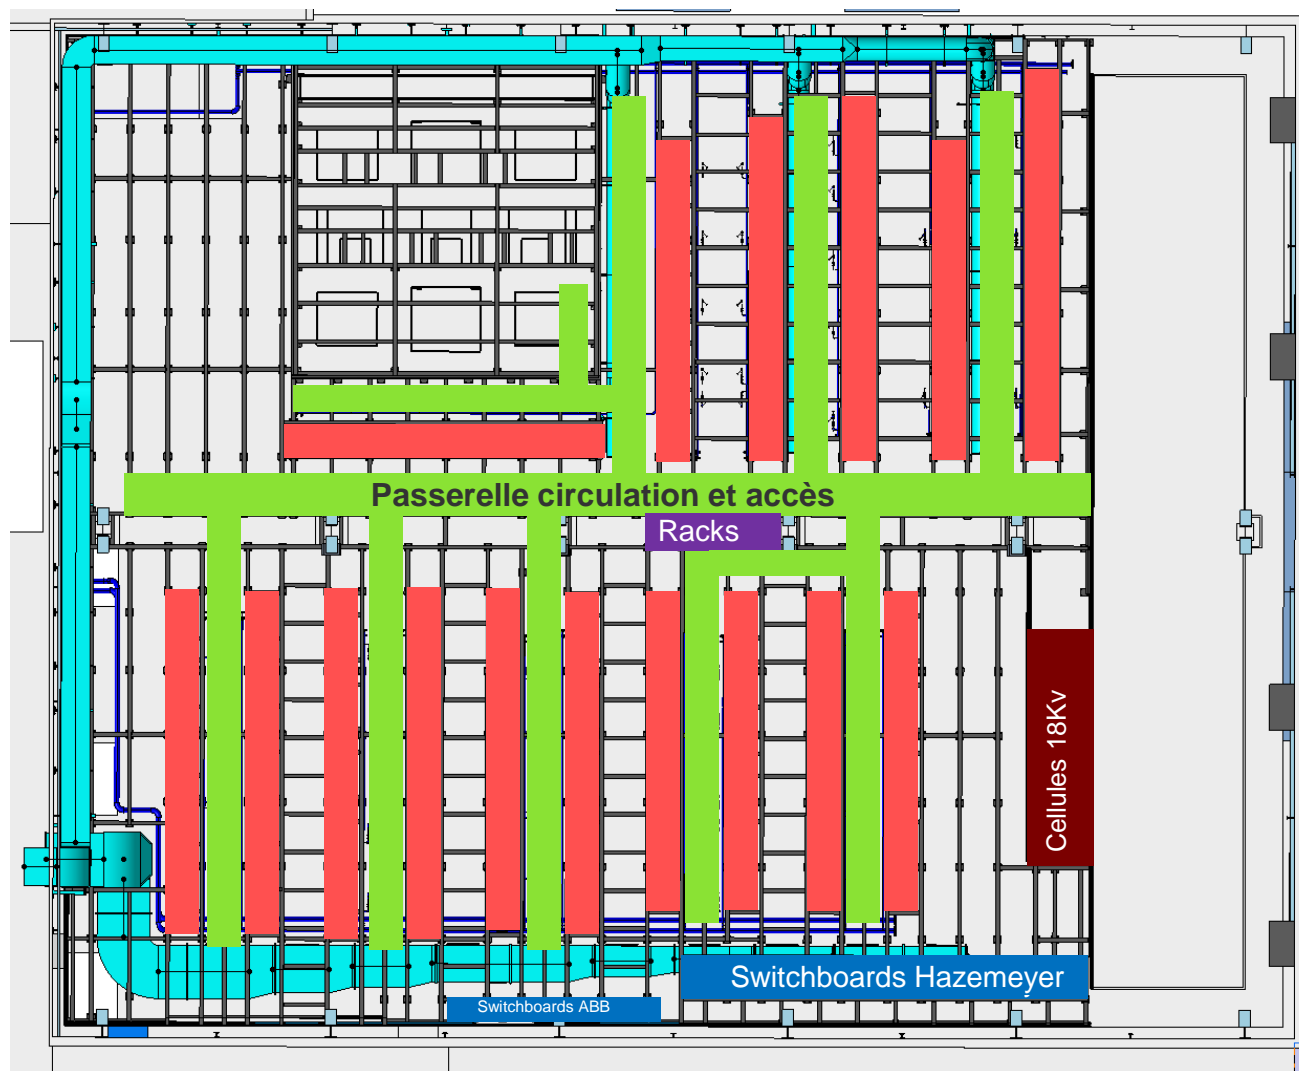


Gateways to uninstall

OVAROFF:

Activity start on ?

Duration 5 days (To define)

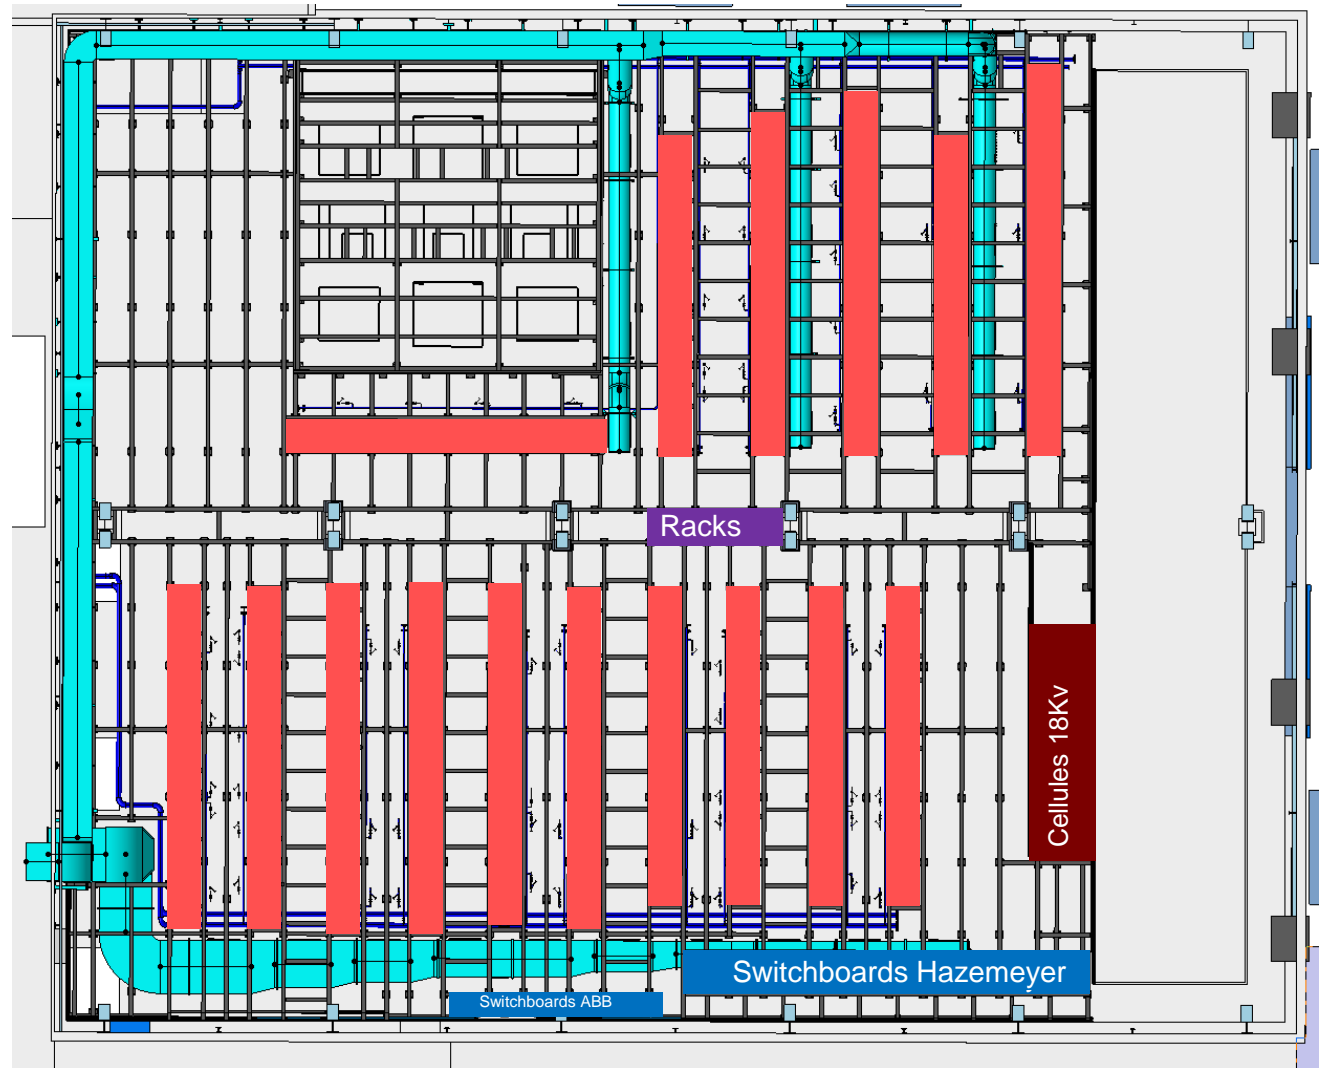


Altéad – False floor closure

ALTEAD:

Activity start on october ?

Duration ?

End of installation of the structure to Install

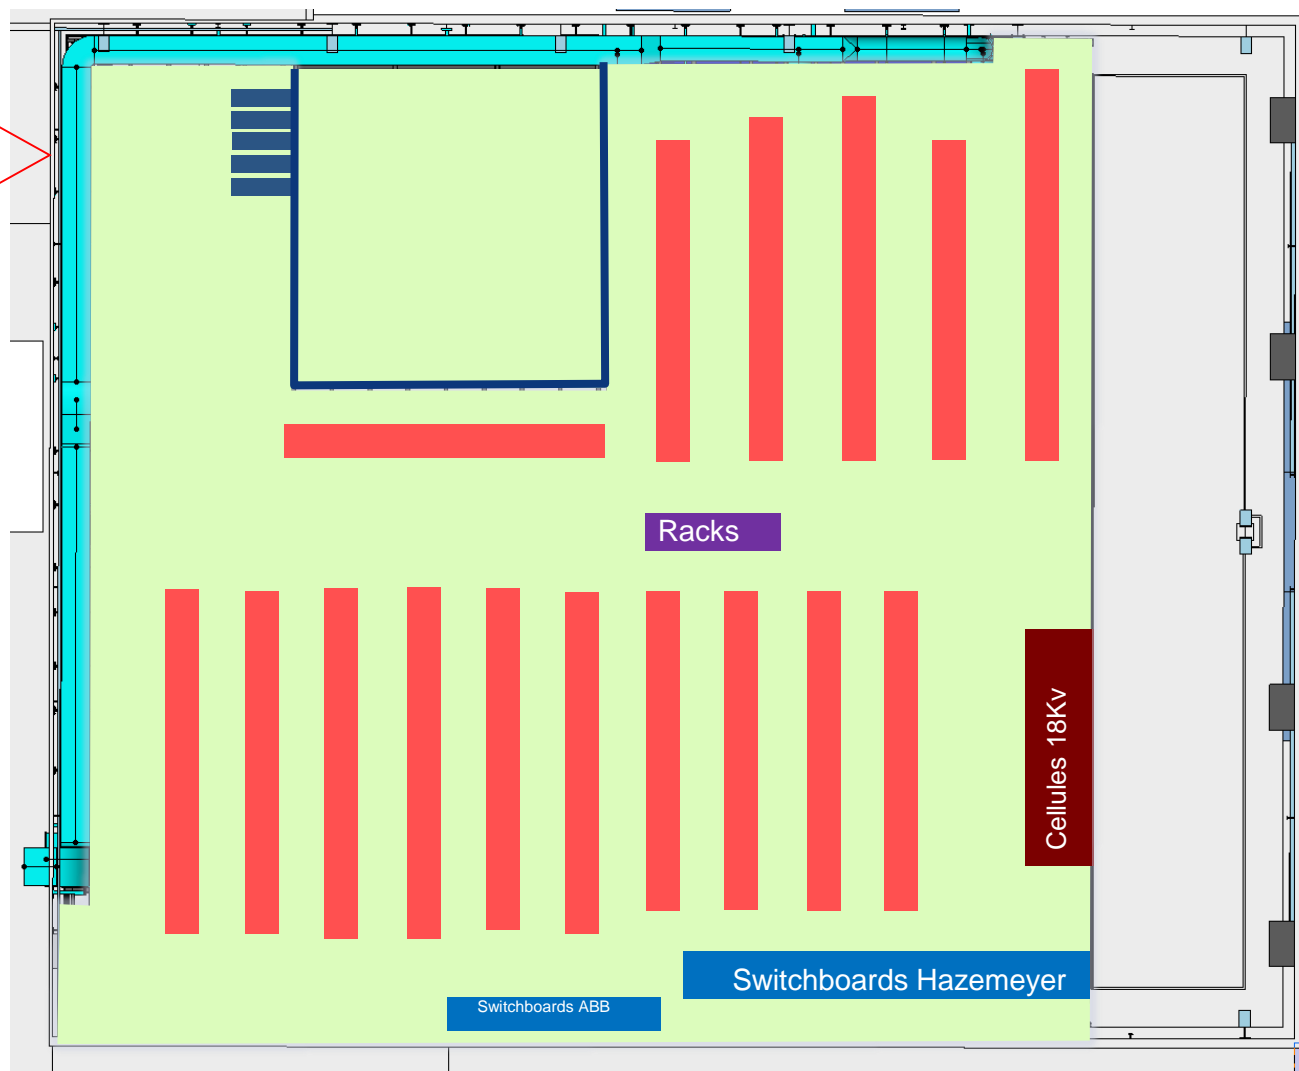

IMPORTANT

- I would like to point out that with the efforts of all the teams EN-EL, EN-CV, IT-CS, EN-EA, TE-EPC, ALTEAD, OUVAROFF ...
- **We were able to advance the installation of the converters by 3 weeks.**
- Also, a big thank you to all the teams for their implications, their responsiveness and the work accomplished.
- **Thank you for your efforts!**

Thank you for your attention



EAST AREA RENOVATION
