



HiRadMat facilities presentation

SPS Planning meeting for YETS 2024-25 & LS3 preparation, No.05

A. Ebn Rahmoun, A. Goillot, B, Rae

17 December 2024

Overview HiRadMat facilities

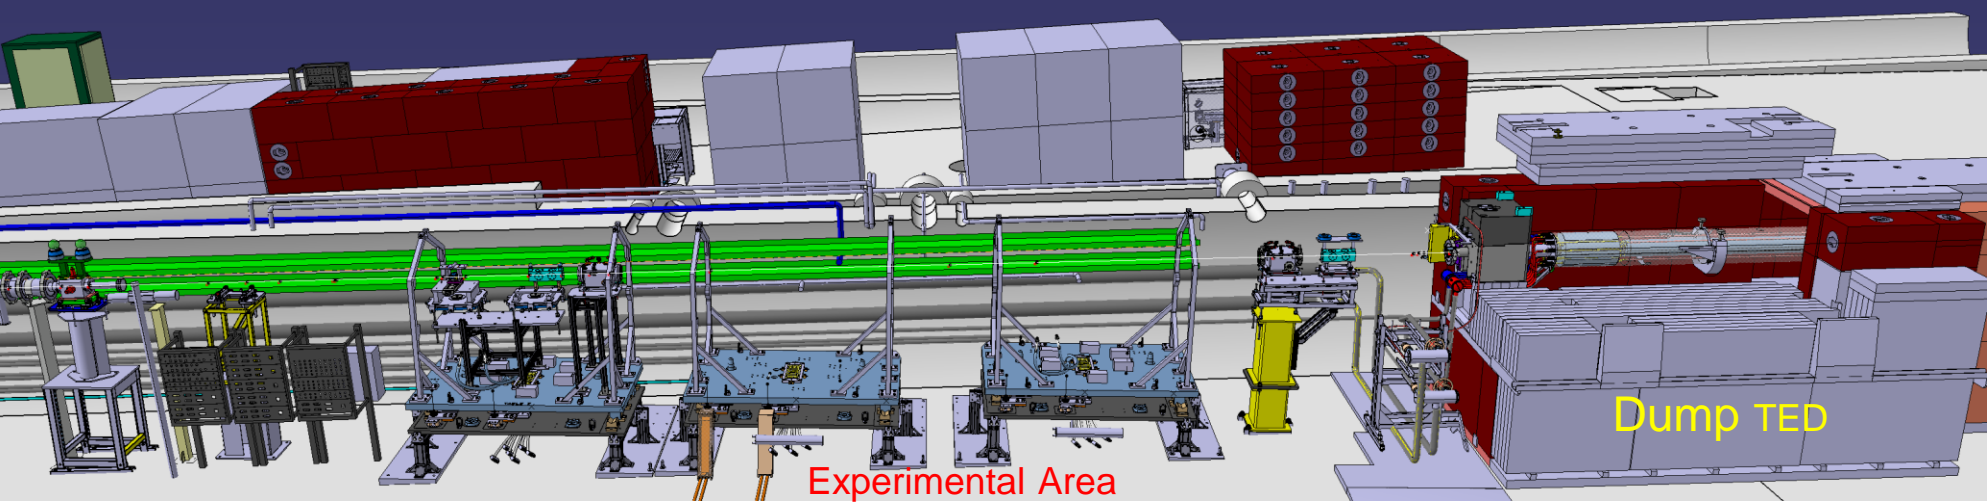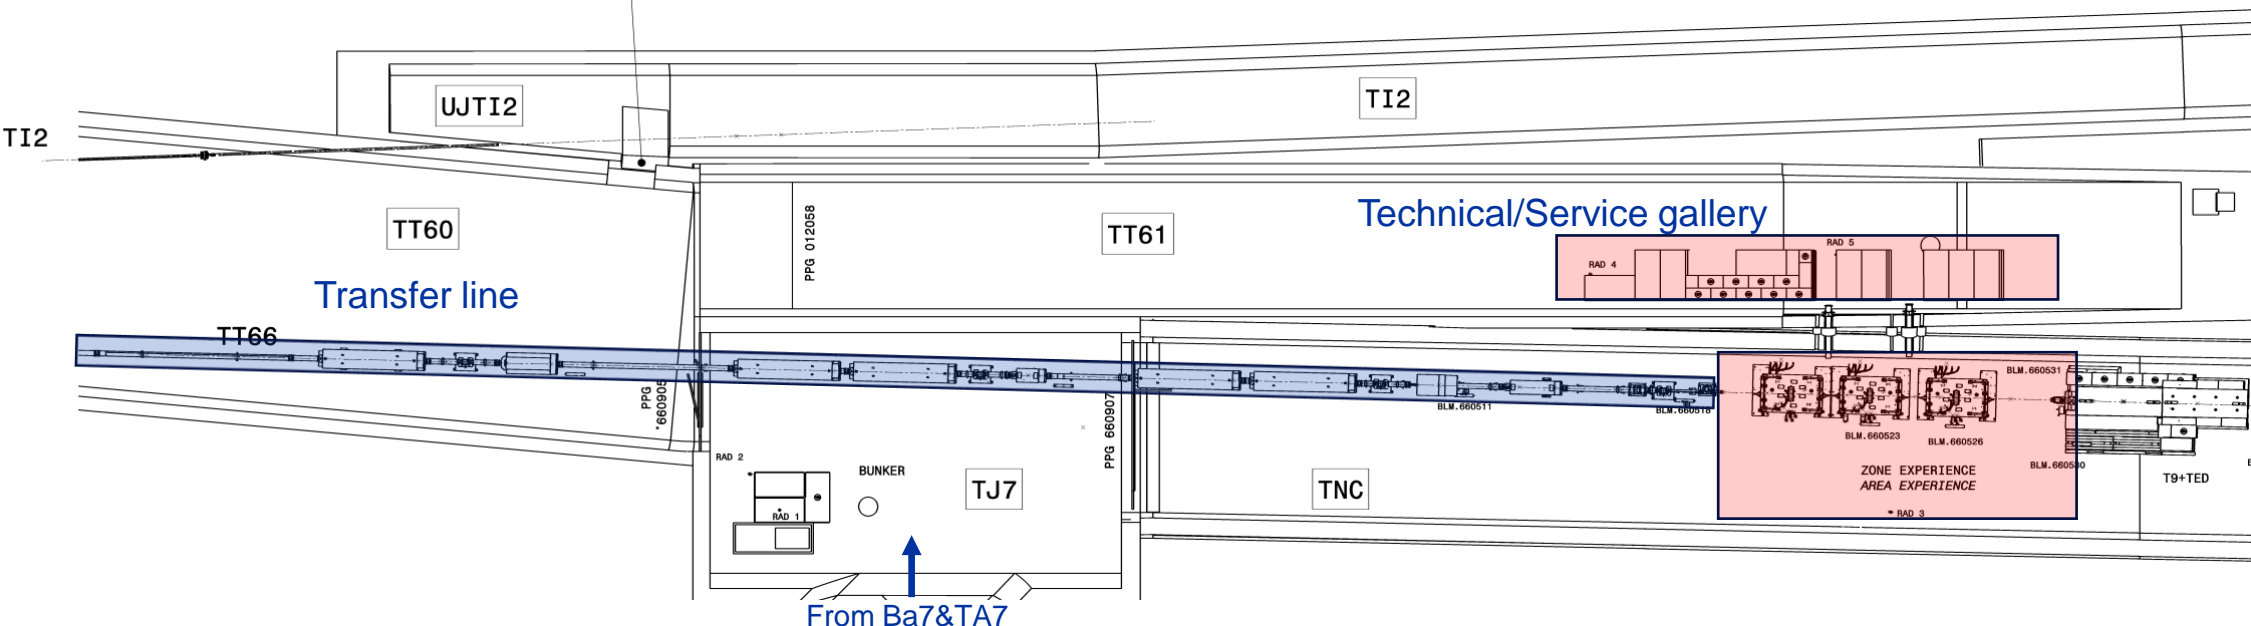


YETS 2024-25 & LS3

Activity YEST2024-25	Contact	Duration	Group involved
Handling Iron blocks from TT61&TNC to Isolde	A-P. Bernardes	1 month	EN-HE; SY-STI; BE-EA
The replacement of the BTV 660528	S. Burger; J. Albertone.	2 weeks	SY-BI; EN-HE; BE-GM; BE-EA
Painting access door TT61-TCC6 YDPS02.012058=TT61	D. Vaxelaire	1 week	SCE-SAM;
Management user & control cables	A-M. Goillot	1 week	BE-CEM; BE-EA
HiRadMat lab. renovation	A. Ebn Rahmoun	2 months	BE-EA

- **LS3 activities, all major activities were completed in YETS23-24 and moved forward to YETS24-25.**

This list is not exhaustive.

Thanks to all the groups who involve in the annual maintenance.



Thanks all groups involved

<https://cern.ch/be-dep-ea>

Feedback YETS 2023-24

- **Ba.7 :**
 - **HiRadMat lab.** The renovation is progressing well, with the aim of having the same layout of the stands installed in both the tunnel and the preparation lab.;

- **TNC & TT61:**

A few activities have started before the YETS to prepare for the major events.

- **TED dump**, has been modified, extended tube , new window & collimator installed;
- **BPKG relocated** and new **BTV** has been installed;
- **New vacuum system installation & modification** end of line **TT66**;
- The **GSM cables** have been replaced;
- **TT61**, new electrical & grounding circuits have been installed for the users.

*The list is not exhaustive, thanks to all the groups who involved in the annual maintenance and installation activities.

- **Minor points:**

- We experienced a **4 days delay** with the installation of the **BTV** and **BPKG**. After discussions with **BE-OP** and **EN-ACE**, we managed to find this time during the **SPS HC** period to complete it;
- The activities of **TJ7**, which serves as a hub for **HRM**, **TCC6**, **TI2**, and **SPS**.
