




# TRACI Oxford Status

## Leak issue:

When the commissioning test was provided we've detected leaks in TRACI.



In order to locate these leaks we used CO2 sniffer and we made tightness tests.

Leaks

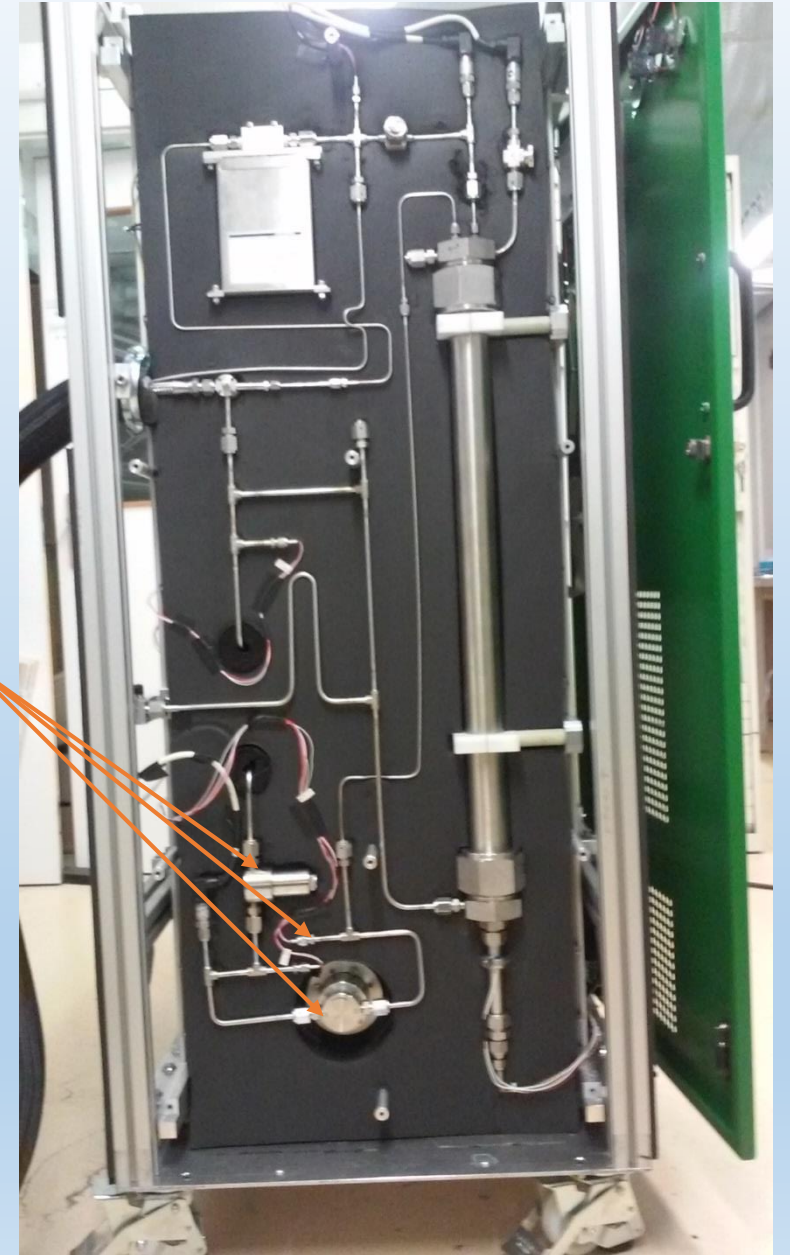

## Leaks:

- a leak caused by connections in the pump (inlet and outlet). In this connections we found cooper gaskets and we changed it for stainless steel gaskets.
- a leak caused by connections in the inline filter.
- a leak caused by temperature sensor connection.
- a leak caused by dummy load connection

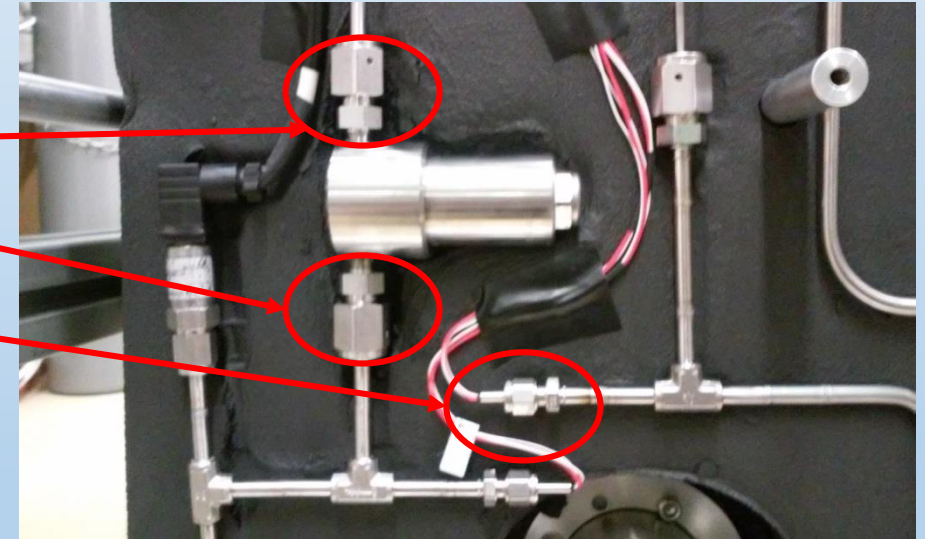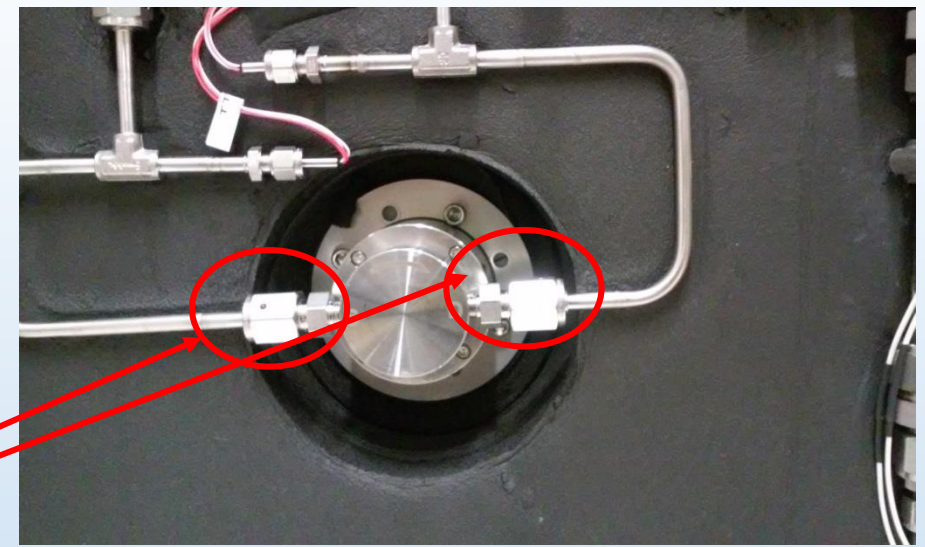


## Leak Test:

We have provided even better diagnostics tests and for that we used tester which is detecting leaks by helium.



## Leak Test:

Now we are waiting for new measurements .

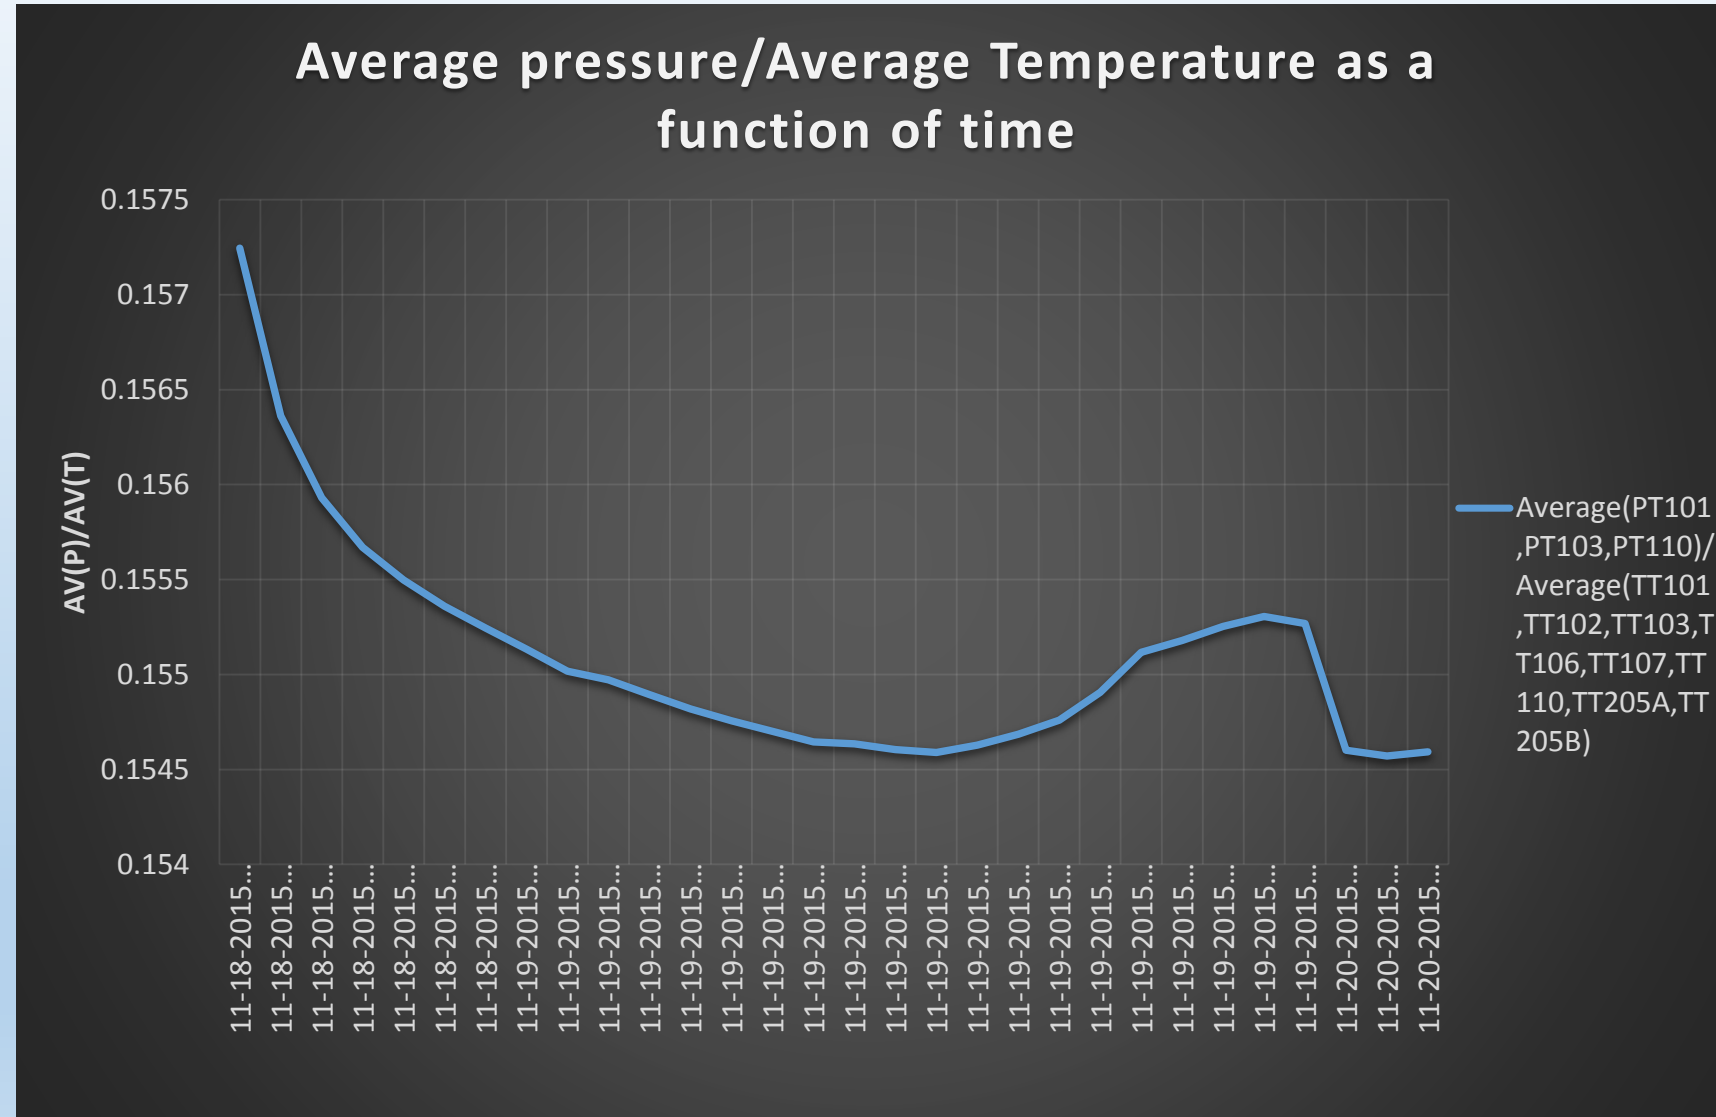

# TRACI Sheffield Status

TRACI Sheffield is ready for commissioning test.



# TRACI Milano Status

The material inside the pump seems to be not suitable for low temperature application.

Actually we are waiting for M-pump specialist.

