

SPS W28-29



Availability

91.1%

Blocking Faults



39

Total Faults

41

Fault Duration (overlap excluded)

15.5h

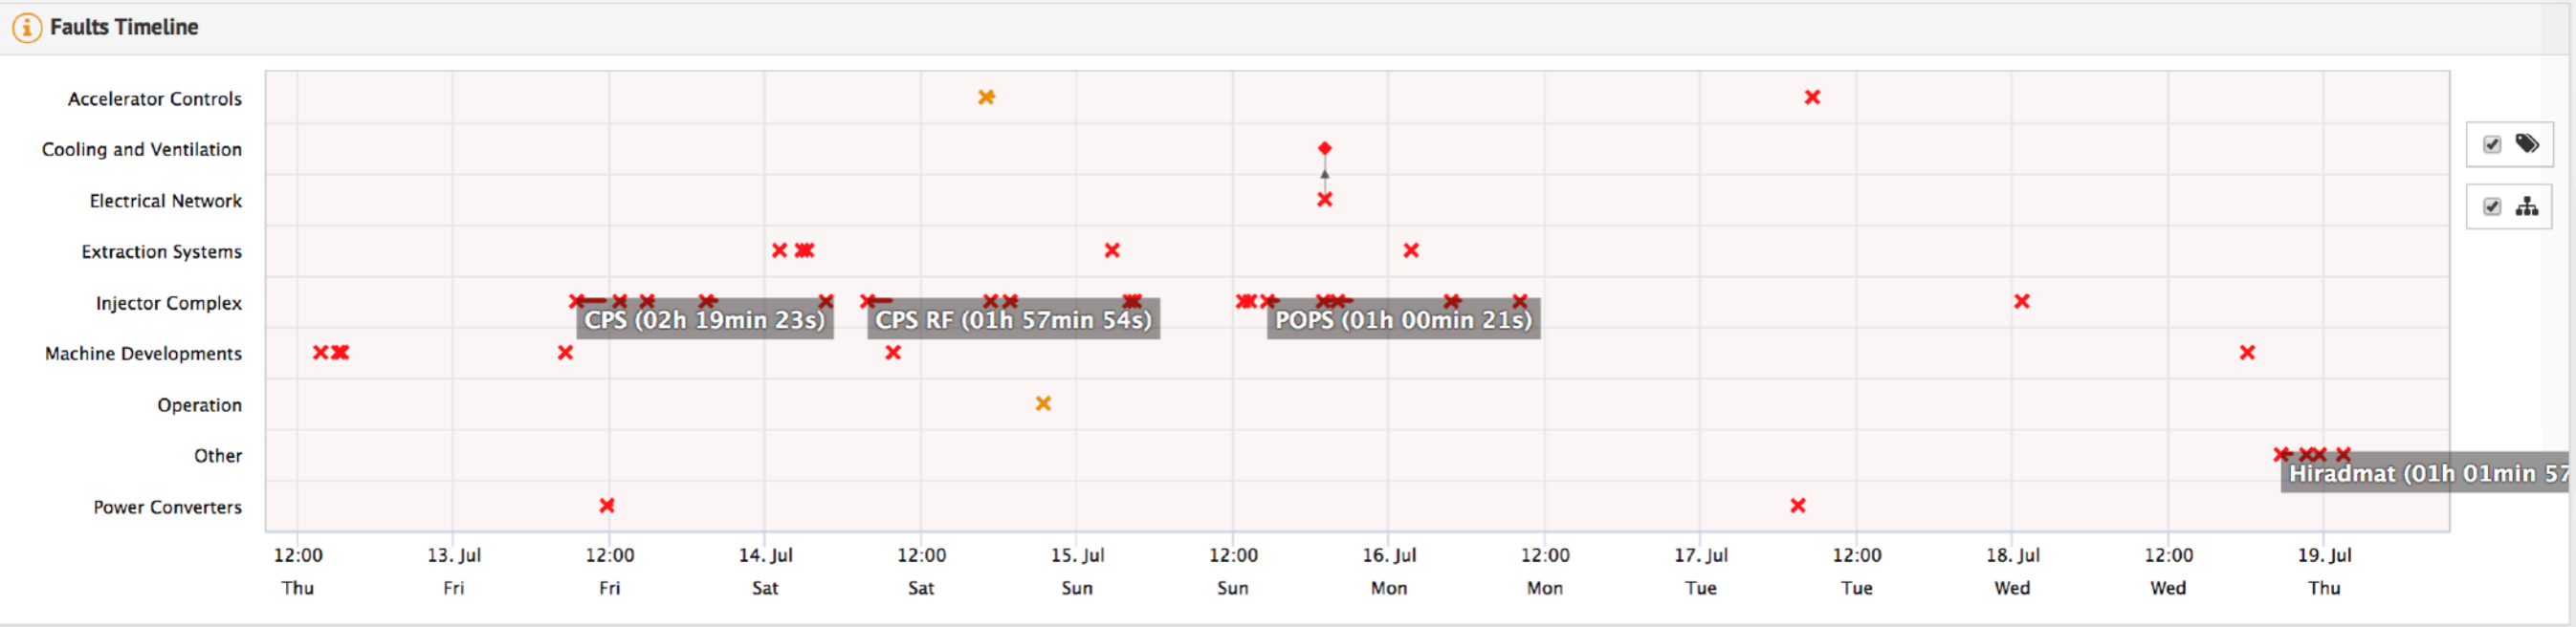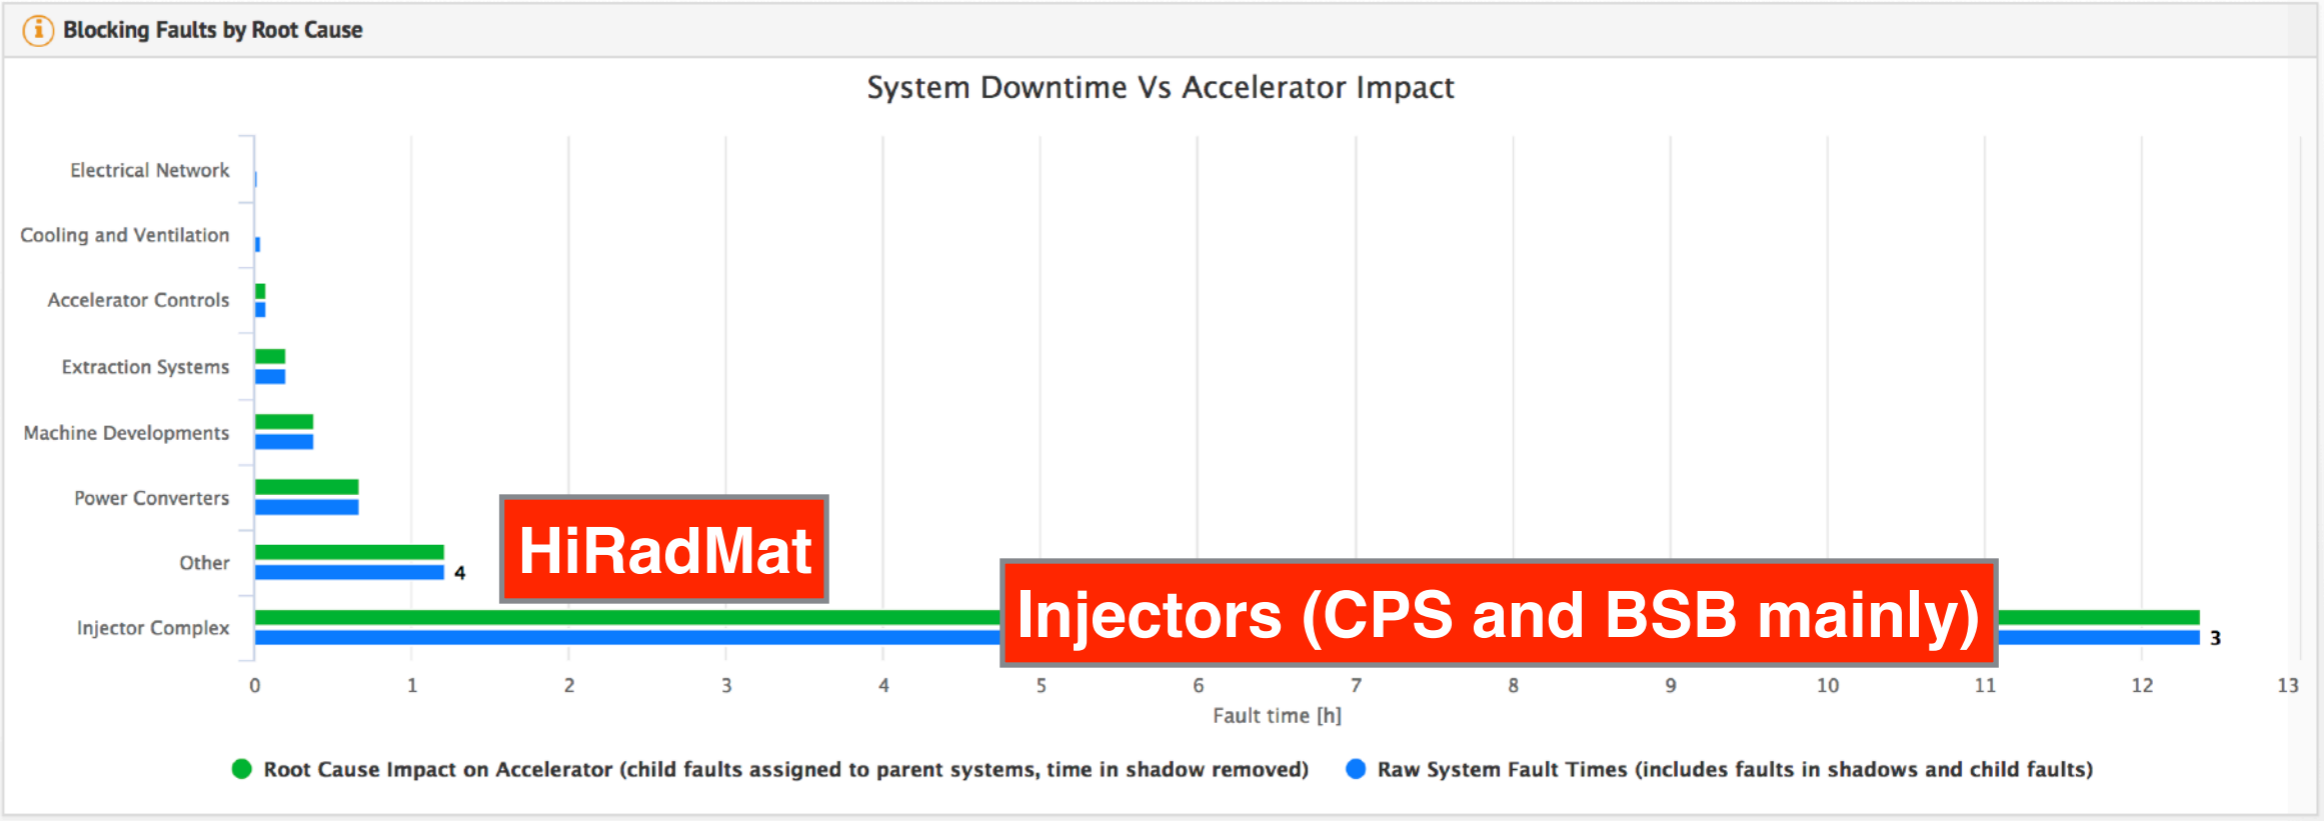

→ HiRadMad TCDIL:

- ↳ Finished this morning at about 1:30 AM
- ↳ All requested shots delivered - thanks for the dedicated time
- ↳ In the end it was well handled between production and HI shots

→ RF intervention this morning:

- ↳ Last week there was a replacement of an RF module
- ↳ It was then observed an offset between the RF phase and the reading of the phase pickup
- ↳ Today, 3h with low intensity SFTPRO beam or nothing to redo the 200 MHz cavity phasing and to re-adjust the 1-turn delay feedback for the 200 MHz cavity line 4
 - All changes will then be verified with beam
