


Machine status

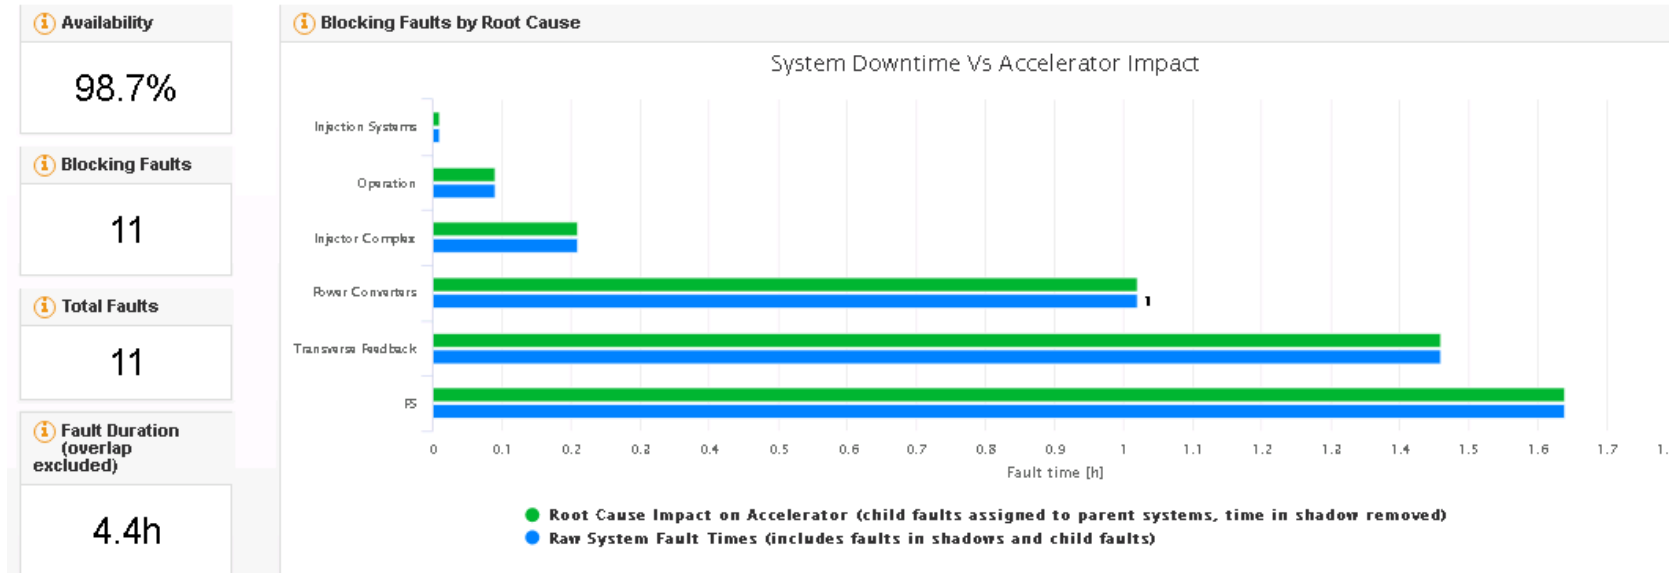

- Technical stop 1:
 - Main intervention for prototype wirescanner.
 - Restart ok after fixing TFB ring 2 and timing problem of distributor ring 1.
- The White Rabbit B Train distribution reliability run re-started.
- New TFB progressing with new HW and FESA class.

Beam status

- All operational beams available.
- Beams for LHC special runs (W25/W26) checked:
 - Van der Meer on all 4 rings.
 - LHC 100ns.
 - LHC 50ns.
- Request to re-check all 4 MD3305 cycles: “BSRT & BGI vs WS cross-calibration”
 - $dp/p = 0.5$
 - Em.long. = 0.3 eVs
 - Intensity = $1E11$ ppb.
 - Em. Trans. = 1,2,3,4
