ID		Task Name	Duration	Start	Finish
1		**Installation of PS Beam Dump AHU**			
2			**46 days**	**Mon 16/12/13**	**Mon 17/02/14**
3		**Design**	**20 days**	**Mon 16/12/13**	**Fri 10/01/14**
4		AHU Selection	3 days	Mon 16/12/13	Wed 18/12/13
5		Mechanical design	13 days	Thu 19/12/13	Mon 06/01/14
6		Electrical Design	17 days	Thu 19/12/13	Fri 10/01/14
7					
8		**Lead Times**	**35 days**	**Thu 19/12/13**	**Wed 05/02/14**
9		Air Handling Unit	21 days	Thu 19/12/13	Thu 16/01/14
10		Electrical Panel	18 days	Mon 13/01/14	Wed 05/02/14
11					
12		**Installation**	**23 days**	**Thu 16/01/14**	**Mon 17/02/14**
13		Strip out and modify existing ductwork	1 day	Thu 16/01/14	Thu 16/01/14
14		Site new AHU	1 day	Fri 17/01/14	Fri 17/01/14
15		Make new ductwork connections	4 days	Mon 20/01/14	Thu 23/01/14
16		Fit controls	1 day	Fri 24/01/14	Fri 24/01/14
17		Install compressed air to actuator	1 day	Mon 27/01/14	Mon 27/01/14
18		Field electrical terminations	2 days	Mon 27/01/14	Tue 28/01/14
19		Position panel	1 day	Thu 06/02/14	Thu 06/02/14
20		Panel Terminations	2 days	Fri 07/02/14	Mon 10/02/14
21		Commissioning	5 days	Tue 11/02/14	Mon 17/02/14

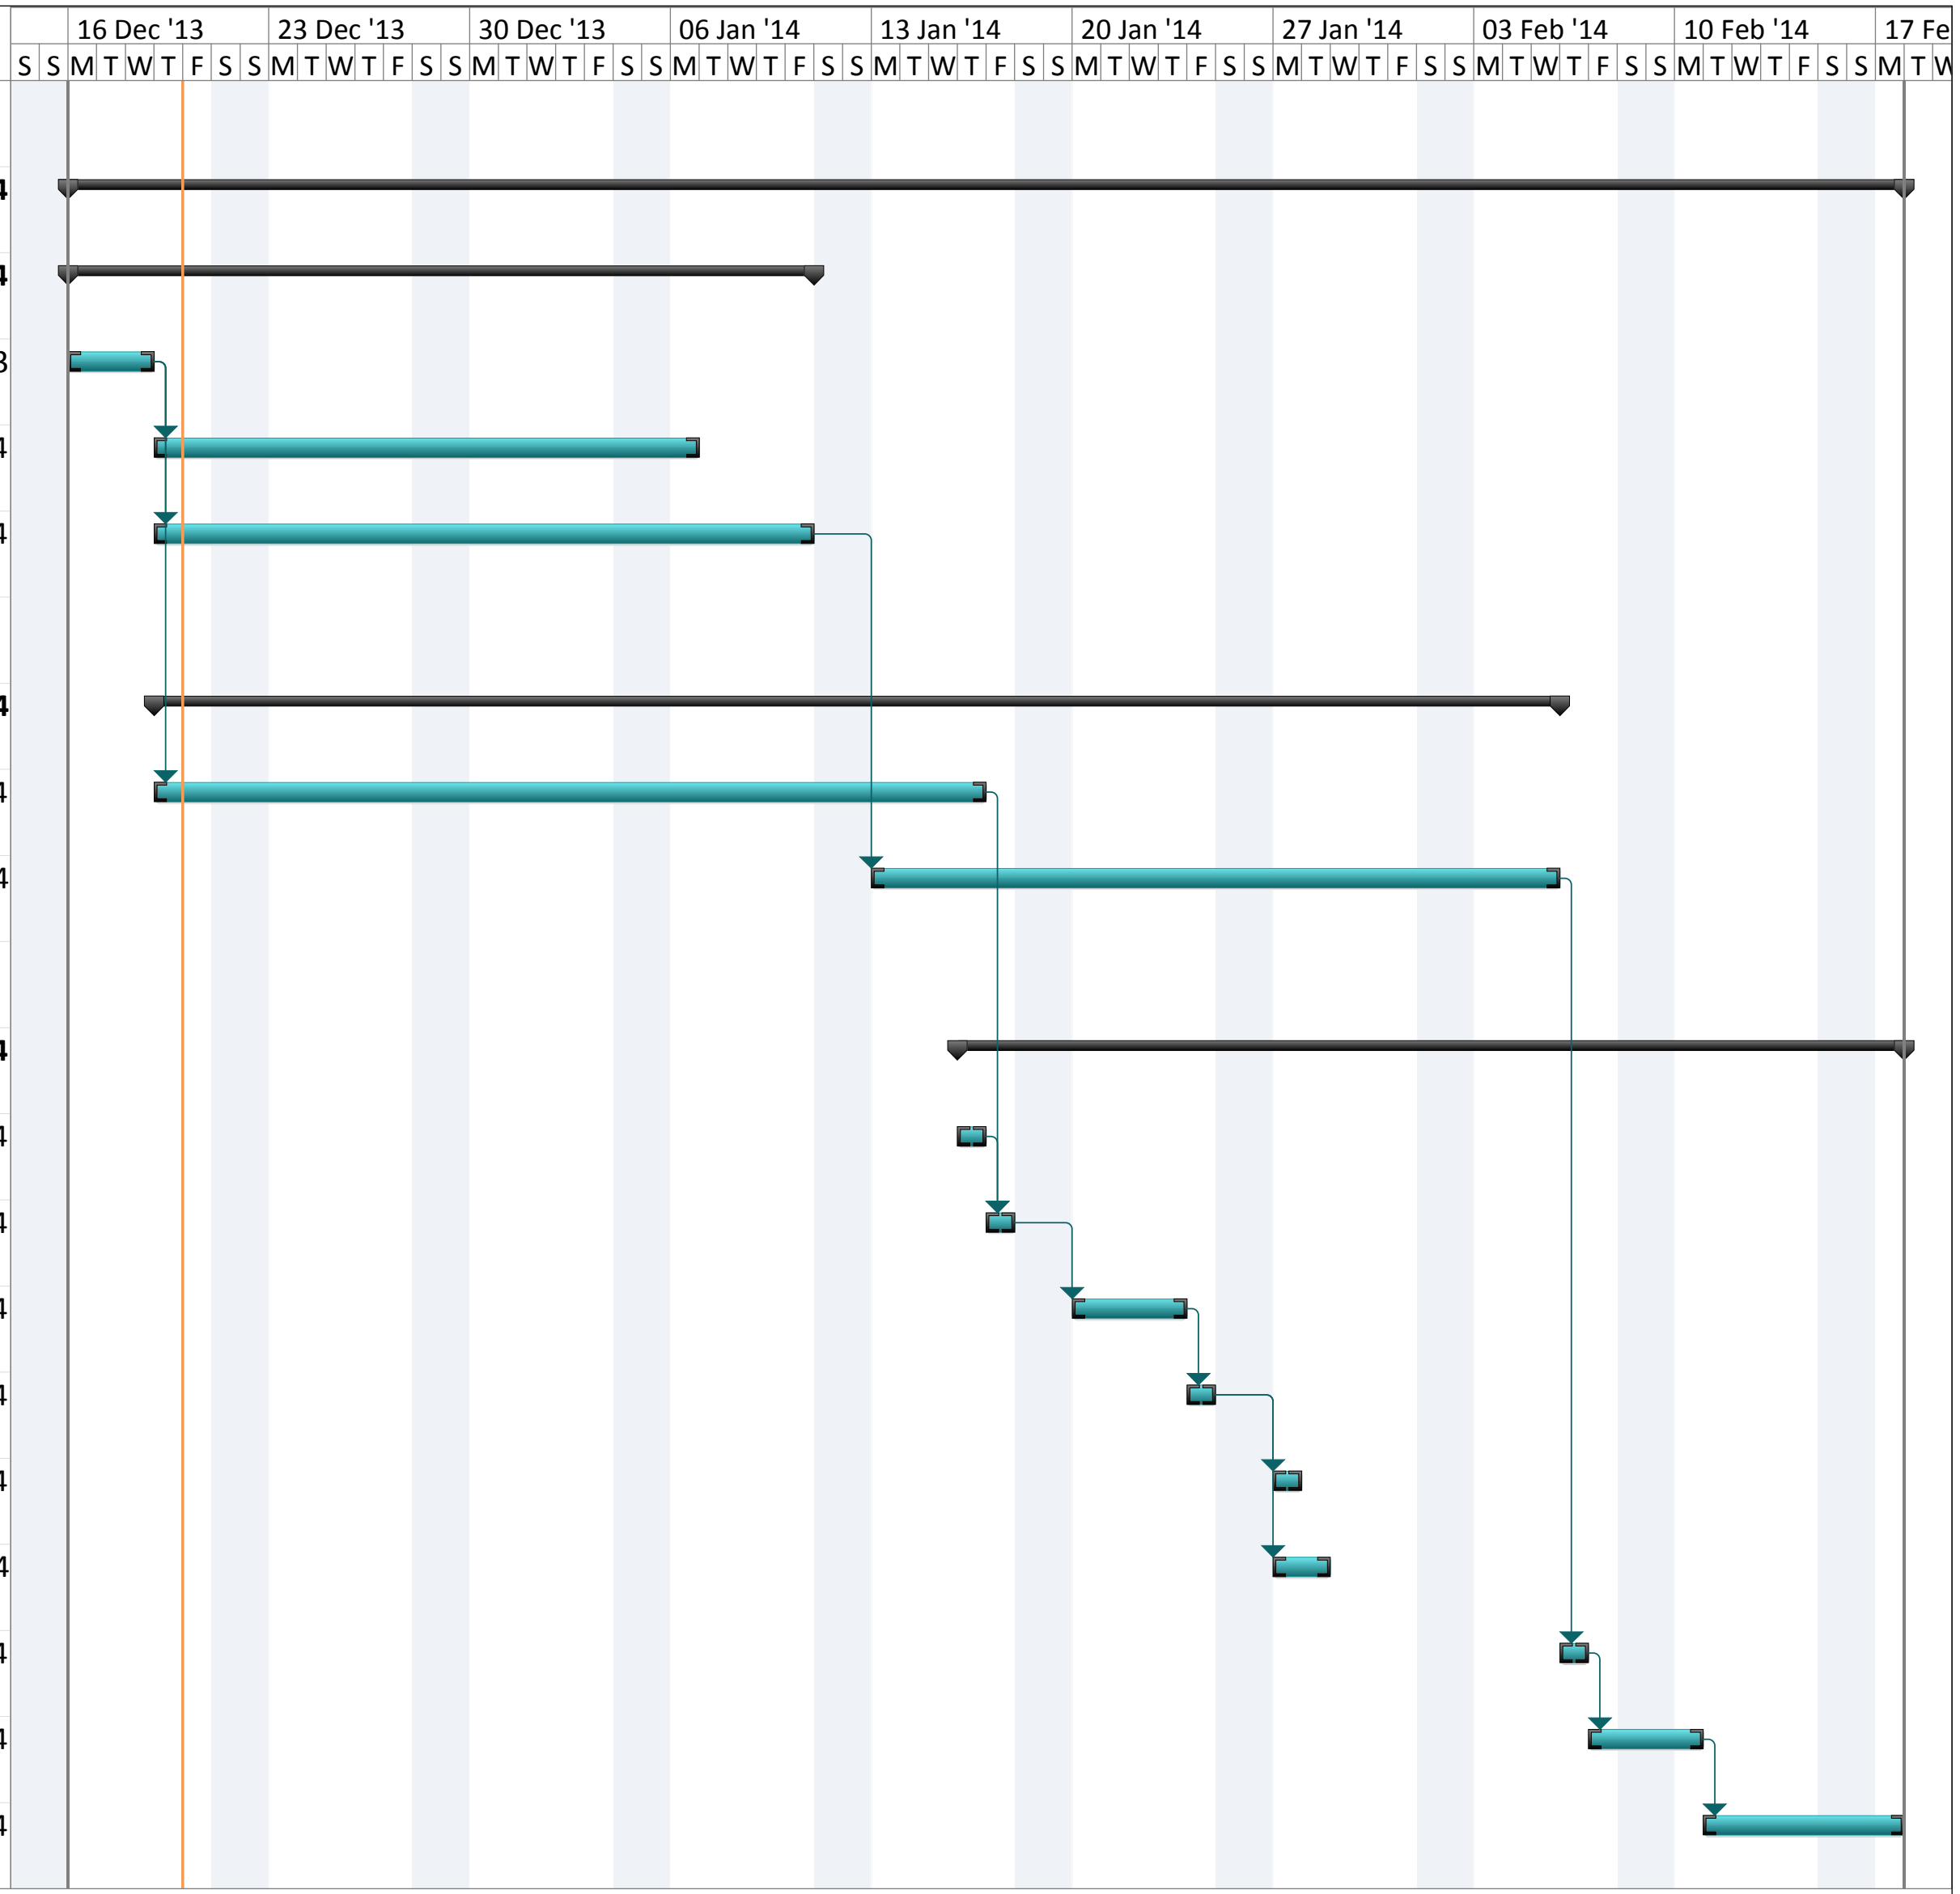

Project: PS Beam Dump Ventilatio
Date: Fri 20/12/13

Task	Project Summary	Inactive Milestone	Manual Summary Rollup
Split	External Tasks	Inactive Summary	Manual Summary
Milestone	External Milestone	Manual Task	Start-only
Summary	Inactive Task	Duration-only	Finish-only
Deadline	Progress		
