ID	Code	Task Name	Duration	Start	Finish	Activity responsible
1189		SPS	410.7 wks?	07/11/17	31/10/25	
1190		Power distribution	410.7 wks?	07/11/17	31/10/25	
1191		EN-EL Power Distribution	62.2 wks	21/01/19	27/03/20	
1		SPS tunnel - Safety lighting	62.2 wks	21/01/19	27/03/20	G.Velazquez
9		SPS3	49.2 wks	22/04/19	27/03/20	
10		Install safety lights and cable trays	4 wks	22/04/19	17/05/19	G.Velazquez
11		Cabling/connecting safety lights TA3 to TA4	2 wks	16/03/20	27/03/20	G.Velazquez
23		LSS3 renovation	25 wks	21/01/19	12/07/19	
24		Decabling	5 days	21/01/19	25/01/19	
25		Cable pulling	2 wks	01/07/19	12/07/19	
26		Socket boxes	2 wks	21/01/19	01/02/19	
27		User works	1 wk	21/01/19	25/01/19	
1269		SPS 3	130 wks	08/01/18	31/07/20	
1270		Power distribution	130 wks	08/01/18	31/07/20	
1271		AUG SP3 2019	1 day	07/01/19	07/01/19	H. De Maynard
1272		AUG SP3 2020	1 day	07/01/20	07/01/20	H. De Maynard
1273		SPS3 consolidation	77.6 wks	21/01/19	31/07/20	
1		EXECUTE	77.6 wks	21/01/19	31/07/20	G. Velazquez
2		STEP 1	8 wks	21/01/19	15/03/19	G. Velazquez
3		SVC dismantling + EMD4/B3	4 wks	21/01/19	15/02/19	G. Velazquez
4		EMD1/A3 dismantling - Antenna open	4 wks	21/01/19	15/02/19	G. Velazquez
5		EMD1/B3 dismantling	4 wks	18/02/19	15/03/19	G. Velazquez
6		STEP 2	19.4 wks	18/02/19	02/07/19	G. Velazquez
7		EMT209/A3 removal	3 days	18/03/19	20/03/19	G. Velazquez
8		EMT209/A3 installation	2 wks	21/03/19	03/04/19	G. Velazquez
9		EMT208/B3 removal	3 days	04/04/19	08/04/19	G. Velazquez
10		EMT208/B3 installation	2 wks	09/04/19	22/04/19	G. Velazquez
11		New EMD1/B3 installation team 1	12 wks	18/02/19	10/05/19	G. Velazquez
12		New EMD1/B3 installation team 2	3 wks	23/04/19	13/05/19	G. Velazquez
13		EBD1/B3 installation	3 wks	14/05/19	03/06/19	G. Velazquez
14		Load transfer from EMD2/B3 to EMD1/B3 - To be coordinated with VIC 2 FC	2 days	01/07/19	02/07/19	G. Velazquez
15		STEP 3	17 wks	03/07/19	29/10/19	G. Velazquez
16		EMD2/A3 removal	4 wks	03/07/19	30/07/19	G. Velazquez
17		EMD2/B3 removal	4 wks	03/07/19	30/07/19	G. Velazquez
18		EMD2/A3 installation	12 wks	31/07/19	22/10/19	G. Velazquez
19		EMD4/B3 installation	12 wks	31/07/19	22/10/19	G. Velazquez
20		Antenna Energization	1 wk	23/10/19	29/10/19	G. Velazquez
21		STEP 4	9 wks	30/10/19	16/01/20	G. Velazquez
22		EBD1/A3 installation	3 wks	30/10/19	19/11/19	G. Velazquez
23		EWD1/A3 installation	2 wks	20/11/19	03/12/19	G. Velazquez
24		EWD1/B3 intallation	2 wks	04/12/19	17/12/19	G. Velazquez
25		EBD11,12,13/A3 installation	2 wks	04/12/19	17/12/19	G. Velazquez
26		EBD11,12,13/B3 installation	2 wks	18/12/19	16/01/20	G. Velazquez
27		Cabling LV	30 wks	18/12/19	30/07/20	G. Velazquez
28		Cabling BA3	7 mons	18/12/19	16/07/20	G. Velazquez
29		Cabling BB3	7 mons	17/01/20	30/07/20	G. Velazquez
1274		BAF3	20 mons	08/01/18	01/08/19	Marcin Bartosz Szewc
1275		New SPS PPS - BA3	10 days	18/02/19	01/03/19	Marcin Bartosz Szewc
1276		SPS-Alim provisoires zones de sotckages et ateliers provisoires - BA3	3 days	05/08/19	07/08/19	Marcin Bartosz Szewc
1277		Consolidation racks electrical distribution BA3	25 days	02/09/19	04/10/19	Marcin Bartosz Szewc
1278		SPS Fixed water-based Fire Extinguishing System Project - SPS Fire Safety WP4 - BA3	2 days	05/08/19	06/08/19	Remy Fabrice Grimand
1279		Electrical powering for SPS Fire Safety Work Package 2 : fire detection and protection systems	10 days	19/08/19	30/08/19	Remy Fabrice Grimand
1280		Install the ventilation system for the Faraday Cage in BA3 - PJ_306	10 days	25/11/19	06/12/19	Marcin Bartosz Szewc
1281		SPS Underground toilet - Removal and replacement with toilet on the surface	1 day	04/05/20	04/05/20	Marcin Bartosz Szewc
1282		Modification des départs électriques pour la zone de test RF 905-R-003	20 days	04/05/20	29/05/20	Marcin Bartosz Szewc
1283		Maintenace	1 wk	20/01/20	24/01/20	
1284		Préventif systématique | Maintenance Parties fixes/Mobiles - tableaux MT | EMD3/B3	1 day	20/01/20	20/01/20	S.Delarue
1285		Préventif systématique | Maintenance Parties fixes/Mobiles - tableaux MT | EMD4/B3	0.2 wks	20/01/20	20/01/20	S.Delarue
1286		Préventif systématique | Maintenance Parties fixes/Mobiles - tableaux MT | EMD5/B3	0.2 wks	20/01/20	20/01/20	S.Delarue
1287		Préventif systématique | Maintenance redresseur + décharge batterie associée | ESU101/B3 - EBU102/B3	0.2 wks	20/01/20	20/01/20	A. Grinand
1288		Préventif systématique | Maintenance redresseur + décharge batterie associée | ESU201/A3 - EBU202/A3	0.2 wks	20/01/20	20/01/20	A. Grinand
1289		Préventif systématique | Maintenance redresseur + décharge batterie associée | ESU24/A3 - ESU25/A3	0.2 wks	20/01/20	20/01/20	A. Grinand
1290		Maintenance préventive Tableau type 1 - EBD4/A3	1 wk	20/01/20	24/01/20	CHRISTOPHE YVAN DI
1291		Maintenance préventive Tableau type 1 - EBD6/B3	1 wk	20/01/20	24/01/20	CHRISTOPHE YVAN DI
1292		Maintenance préventive Tableau type 1 - EBD8/B3	1 wk	20/01/20	24/01/20	CHRISTOPHE YVAN DI
1293		Maintenance préventive Tableau type 1 - ERD3/B3	1 wk	20/01/20	24/01/20	CHRISTOPHE YVAN DI
1294		Cabling	63.2 wks	03/09/18	29/11/19	
1295	SP3LIU0-CC05	LIU Cabling - New Building	11 wks	03/09/18	16/11/18	G. Gros
1296		Technical dossier to contractor	0 wks	03/09/18	03/09/18	G. Gros
1297		Tirage	3.7 wks	24/09/18	18/10/18	G. Gros
1298		Raccordment	1.7 wks	18/10/18	30/10/18	G. Gros
1299		Test	2 wks	31/10/18	13/11/18	G. Gros
1300		Delivery of test report and Analysis	3 days	14/11/18	16/11/18	G. Gros
1301	SP3CUC0-CD01, SF	Decabling project & Decabling LIU	23 wks	21/01/19	28/06/19	G. Kotsalos
1302		Surface	11 wks	21/01/19	05/04/19	G. Kotsalos
1303		CCR & BB3	2 wks	21/01/19	01/02/19	G. Kotsalos
1304		BA3 (BEA3)	9 wks	04/02/19	05/04/19	G. Kotsalos
1305		Underground	10 wks	08/04/19	14/06/19	G. Kotsalos
1306		PA3	3 wks	08/04/19	26/04/19	G. Kotsalos
1307		TA3	2 wks	29/04/19	10/05/19	G. Kotsalos
1308		TS3+ & TS3-	5 wks	13/05/19	14/06/19	G. Kotsalos
1309		Waste treatment, mechanical works and finition	2 wks	17/06/19	28/06/19	G. Kotsalos
1310		Cabling Campaigns SPS P3 (surface)	2 wks	01/07/19	12/07/19	G. Girardot
1311		Pulling	1 wk	01/07/19	05/07/19	0
1312		Raccordment	0.6 wks	08/07/19	10/07/19	0
1313		Test	0.4 wks	11/07/19	12/07/19	0
1314		Cabling Campaigns SPS P3 (underground + surface)	20 wks	15/07/19	29/11/19	G. Girardot
1315		Pulling	14 wks	15/07/19	18/10/19	0
1316		Raccordment	4 wks	21/10/19	15/11/19	0
1317		Test	2 wks	18/11/19	29/11/19	0
1318		Fibre	10.6 wks	13/05/19	24/07/19	
1319		Surface	7.4 wks	13/05/19	02/07/19	
1320	SP3FSF0-FL201	FIBRE FIRE SAFETY - SPS PT3 - LS2 PHASE 1	2 days	13/05/19	14/05/19	LASSAUCE
1321	SP3LIU0-FL201	FIBRE LIU - SPS PT3 - LS2 PHASE 1	5 days	15/05/19	21/05/19	BLANC
1322	SP3MOP0-FL201	FIBRE MOPOS - SPS PT3 - LS2 PHASE 1	30 days	22/05/19	02/07/19	BLANC
1323		Underground	3.2 wks	03/07/19	24/07/19	
1324	SP3OTN0-FL201	FIBRE OASIS - SPS PT3 - LS2 PHASE 1	3 days	03/07/19	05/07/19	BLANC
1325	SP3ORS0-FL201	FIBRE DOFRTS - SPS PT3 - LS2 PHASE 1	10 days	08/07/19	19/07/19	BLANC
1326	SP3PPS0-FL201	FIBRE PPS - SPS PT3 - LS2 PHASE 1	2 days	22/07/19	23/07/19	LASSAUCE
1327	SP3SMT0-FL201	FIBRE SPS PT3 SURF - LS2 PHASE 1	1 day	24/07/19	24/07/19	BLANC

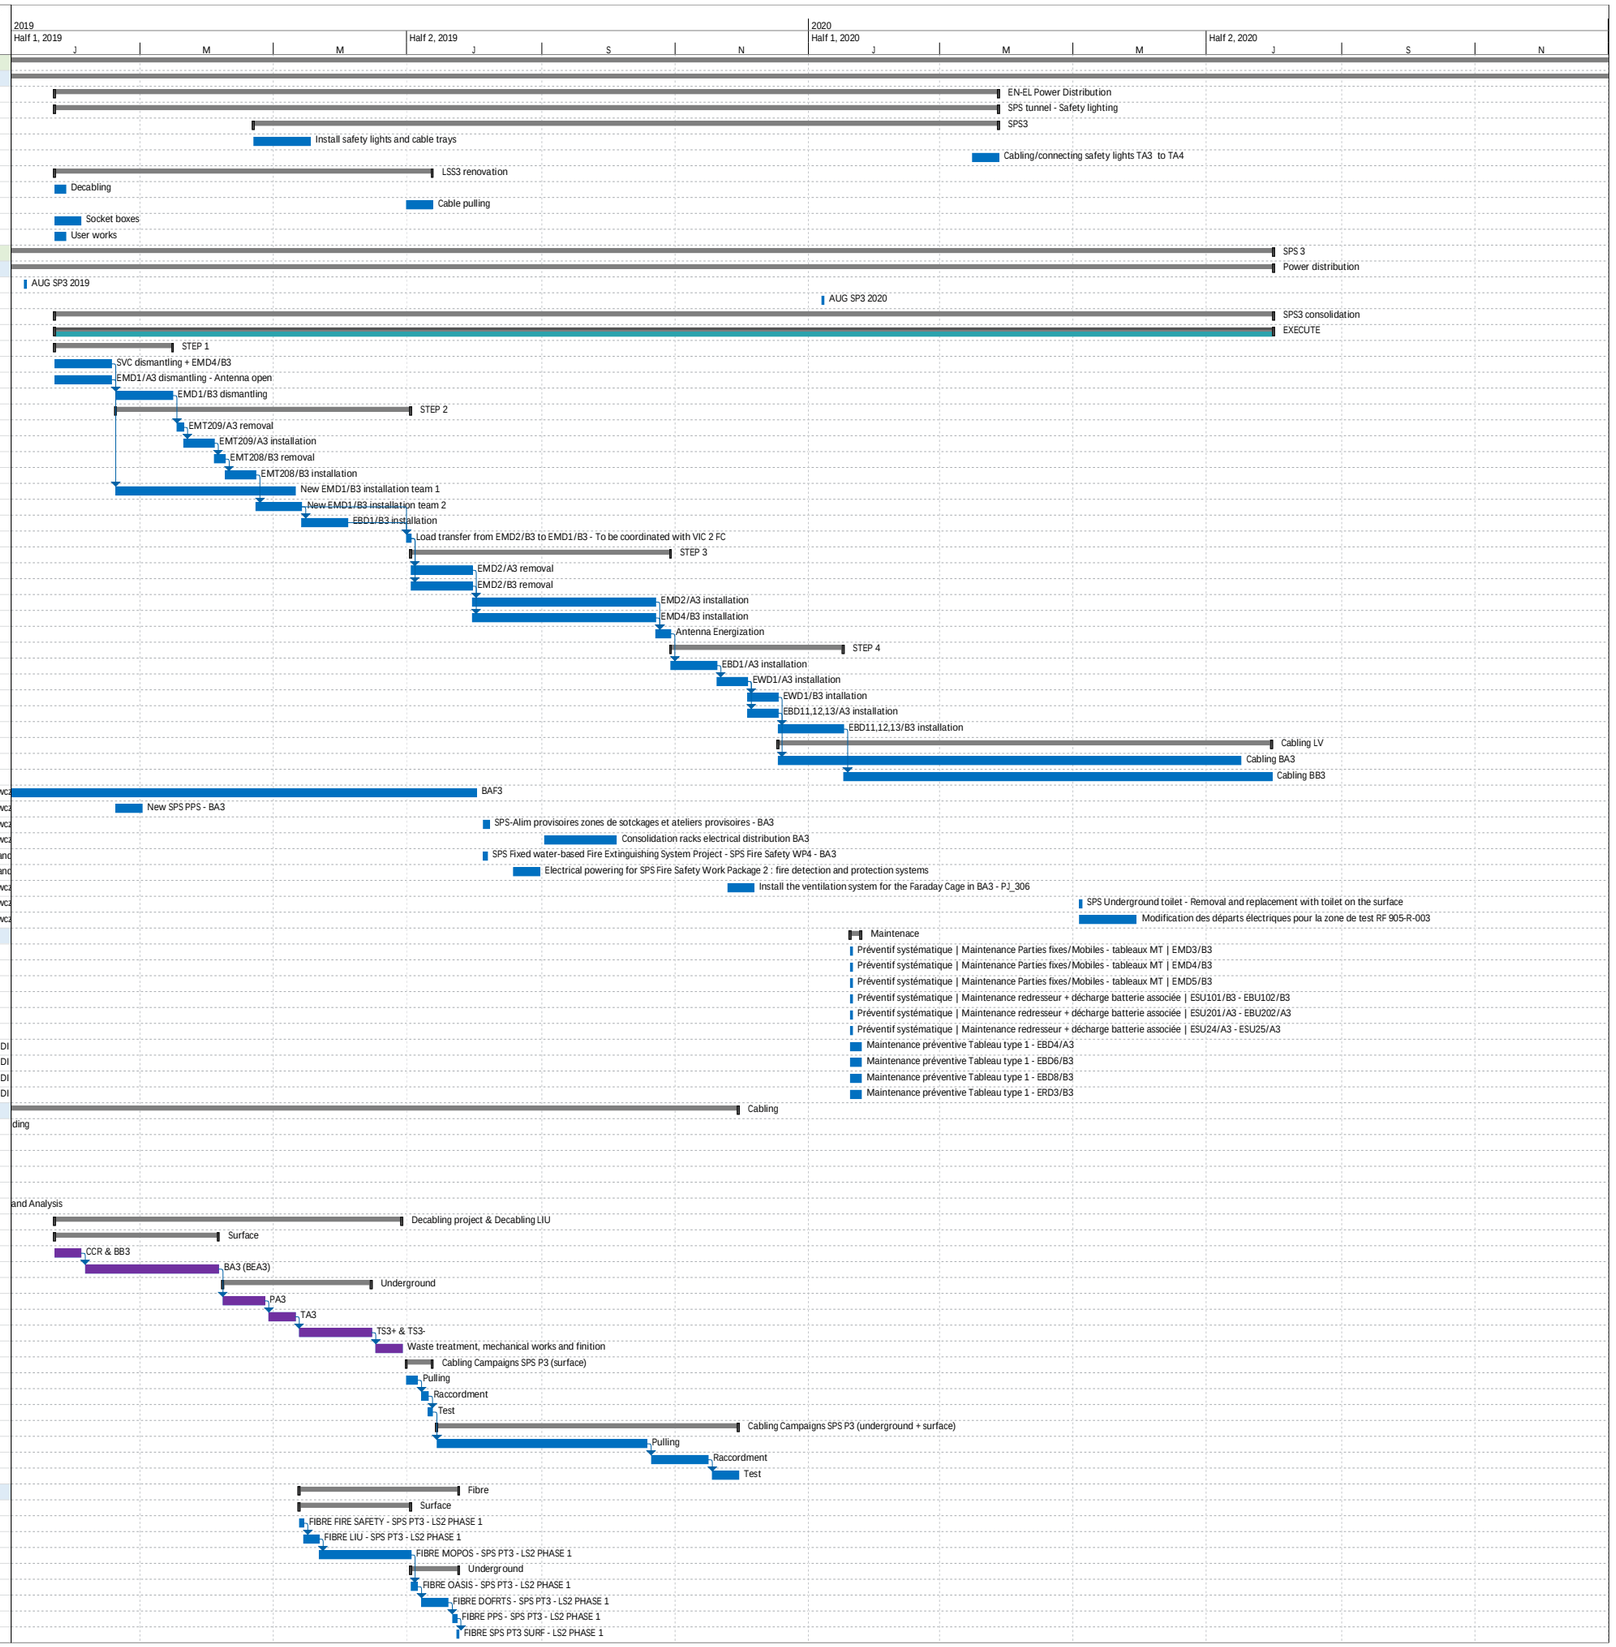

Author: Stefano Meroli
Mail: Stefano.Meroli@cern.ch
