


Original plan

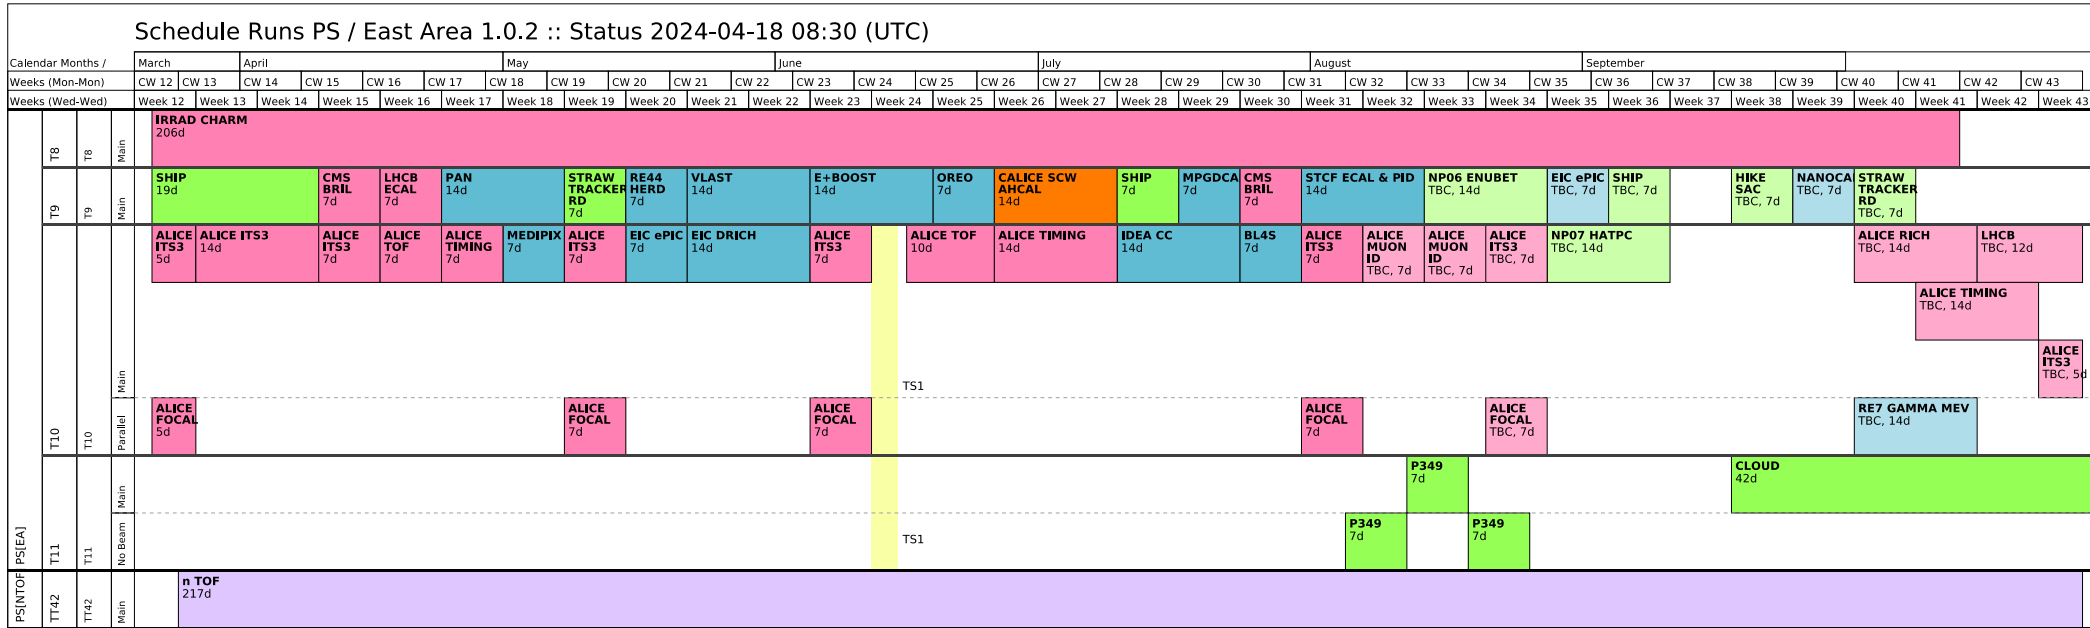

ALICE requests following publication of DRAFT version v0.6 of users schedule (27 February):

- swap BL4S with RICH in September; this is essential for RICH, as they have to deliver results by the end of w40;
- have TIMING as main user for at least one week towards end September-October; this is essential because as it is now (TIMING parasitic of RICH/LHCb) they would not be able to operate;
- postpone the w32-33 MUON ID slots by 4-6 weeks if possible; this would give more contingency to complete the construction of the setup.

Original plan

Schedule Runs PS / East Area 1.0.2 :: Status 2024-04-18 08:30 (UTC)

Calendar Months /		March			April			May			June			July			August			September																
Weeks (Mon-Mon)		CW 12	CW 13	CW 14	CW 15	CW 16	CW 17	CW 18	CW 19	CW 20	CW 21	CW 22	CW 23	CW 24	CW 25	CW 26	CW 27	CW 28	CW 29	CW 30	CW 31	CW 32	CW 33	CW 34	CW 35	CW 36	CW 37	CW 38	CW 39	CW 40	CW 41	CW 42	CW 43			
Weeks (Wed-Wed)		Week 12	Week 13	Week 14	Week 15	Week 16	Week 17	Week 18	Week 19	Week 20	Week 21	Week 22	Week 23	Week 24	Week 25	Week 26	Week 27	Week 28	Week 29	Week 30	Week 31	Week 32	Week 33	Week 34	Week 35	Week 36	Week 37	Week 38	Week 39	Week 40	Week 41	Week 42	Week 43			
PS[NTOF]	T8	T8	Main	IRRAD CHARM 206d																																
				T9	T9	Main	SHP 19d	CMS BRIL 7d	LHCB ECAL 7d	PAN 14d	STRAW TRACKER RD 7d	RE44 HERD 7d	VLAST 14d	E-BOOST 14d	OREO 7d	CALICE SCW AHCAL 14d	SHIP 7d	MPGDCA 7d	CMS BRIL 7d	STCF ECAL & PID 14d	NP06 ENUBET TBC, 14d	EIC ePIC TBC, 7d	SHIP TBC, 7d	HIKE SAC TBC, 7d	NANOCA TBC, 7d	STRAW TRACKER RD TBC, 7d										
	T10	T10	Main	ALICE ITS3 5d	ALICE ITS3 14d	ALICE ITS3 7d	ALICE TOF 7d	ALICE TIMING 7d	MEDIPIX 7d	ALICE ITS3 7d	EIC ePIC 7d	EIC DRICH 14d	ALICE ITS3 7d	ALICE TOF 10d	ALICE TIMING 14d	IDEA CC 14d	BL4S 7d	ALICE ITS3 7d	ALICE MUON ID TBC, 7d	ALICE MUON ID TBC, 7d	ALICE ITS3 TBC, 7d	NP07 HATPC TBC, 14d								ALICE RICH TBC, 14d	LHCB TBC, 12d					
	T10	T10	Parallel	ALICE FOCAL 5d						ALICE FOCAL 7d				ALICE FOCAL 7d	TS1																			ALICE TIMING TBC, 14d		
	T11	T11	No Beam												TS1																					
PS[NTOF]	T42	T42	Main	n TOF 217d																																

New plan v2.0.0

[DRAFT] Schedule Runs PS / East Area 2.0.0 :: Status 2024-04-29 17:00 (UTC)

Calendar Months /		March			April			May			June			July			August			September			October			November													
Weeks (Mon-Mon)		CW 12	CW 13	CW 14	CW 15	CW 16	CW 17	CW 18	CW 19	CW 20	CW 21	CW 22	CW 23	CW 24	CW 25	CW 26	CW 27	CW 28	CW 29	CW 30	CW 31	CW 32	CW 33	CW 34	CW 35	CW 36	CW 37	CW 38	CW 39	CW 40	CW 41	CW 42	CW 43	CW 44	CW 45	CW 46	CW 47	CW 48	
Weeks (Wed-Wed)		Week 12	Week 13	Week 14	Week 15	Week 16	Week 17	Week 18	Week 19	Week 20	Week 21	Week 22	Week 23	Week 24	Week 25	Week 26	Week 27	Week 28	Week 29	Week 30	Week 31	Week 32	Week 33	Week 34	Week 35	Week 36	Week 37	Week 38	Week 39	Week 40	Week 41	Week 42	Week 43	Week 44	Week 45	Week 46	Week 47	Week 48	
PS[NTOF]	T8	T8	Main	IRRAD CHARM 234d																																			
				T9	T9	Main	SHP 19d	CMS BRIL 7d	LHCB ECAL 7d	PAN 14d	STRAW TRACKER RD 7d	RE44 HERD 7d	VLAST 14d	E-BOOST 14d	OREO 7d	CALICE SCW AHCAL 14d	MPGDCA 7d	CMS BRIL 7d	STCF ECAL & PID 14d	NP06 ENUBET DRAFT 14d	EIC ePIC DRAFT 7d	SHIP DRAFT 7d	SHIP DRAFT 7d	HIKE SAC DRAFT 7d	NANOCA DRAFT 7d	STRAW TRACKER RD DRAFT 7d	WCTE DRAFT 42d										CHIMERA DRAFT 21d		
	T10	T10	Main	ALICE ITS3 5d	ALICE ITS3 14d	ALICE ITS3 7d	ALICE TOF 7d	ALICE TIMING 7d	MEDIPIX 7d	ALICE ITS3 7d	EIC DRICH 14d	ALICE ITS3 7d	ALICE TOF 10d	ALICE TIMING 14d	IDEA CC 14d	BL4S 7d	ALICE ITS3 7d		ALICE ITS3 DRAFT 7d		ALICE ITS3 DRAFT 7d	BL4S DRAFT 14d	ALICE RICH DRAFT 14d	ALICE TIMING DRAFT 14d	ALICE MUON ID DRAFT 7d	NP07 HATPC DRAFT 14d	LHCB DRAFT 14d												
	T10	T10	Parallel	ALICE FOCAL 5d						ALICE FOCAL 7d				ALICE FOCAL 7d	TS1																								
	T11	T11	No Beam												TS1																								
PS[NTOF]	T42	T42	Main	n TOF 245d																																			

New plan v2.0.0:

September October November

w33	w34	w35	w36	w37	w38	w39	w40	w41	w42	w43	w44	w45	w46	w47	w48
	ITS3		ITS3	BL4S	BL4S	RICH	RICH	TIM	TIM	MID	NP07	NP07	LHCb	LHCb	
	FOC		FOC			RE7	RE7		MID	ITS3					

Issues:

- RICH last days w40 (Sat-Wed: conflict with UW in cw41) → can live with that
- MID cannot run with TIM/ITS3 (3m long setup) AND should be scheduled between w38-41
- FOCal wants run parasitic after w41

NEW plan agreed today:

September October November

w33	w34	w35	w36	w37	w38	w39	w40	w41	w42	w43	w44	w45	w46	w47	w48
	ITS3		ITS3	BL4S	BL4S	RICH	RICH	MID	TIM	TIM	NP07	NP07	LHCb	LHCb	
	FOC		FOC			RE7	RE7	ITS3		FOC					
