


Configuration Management Task Status Report

Project Conference – Barcelona, May 2003

Piotr Poznanski



Architecture Overview

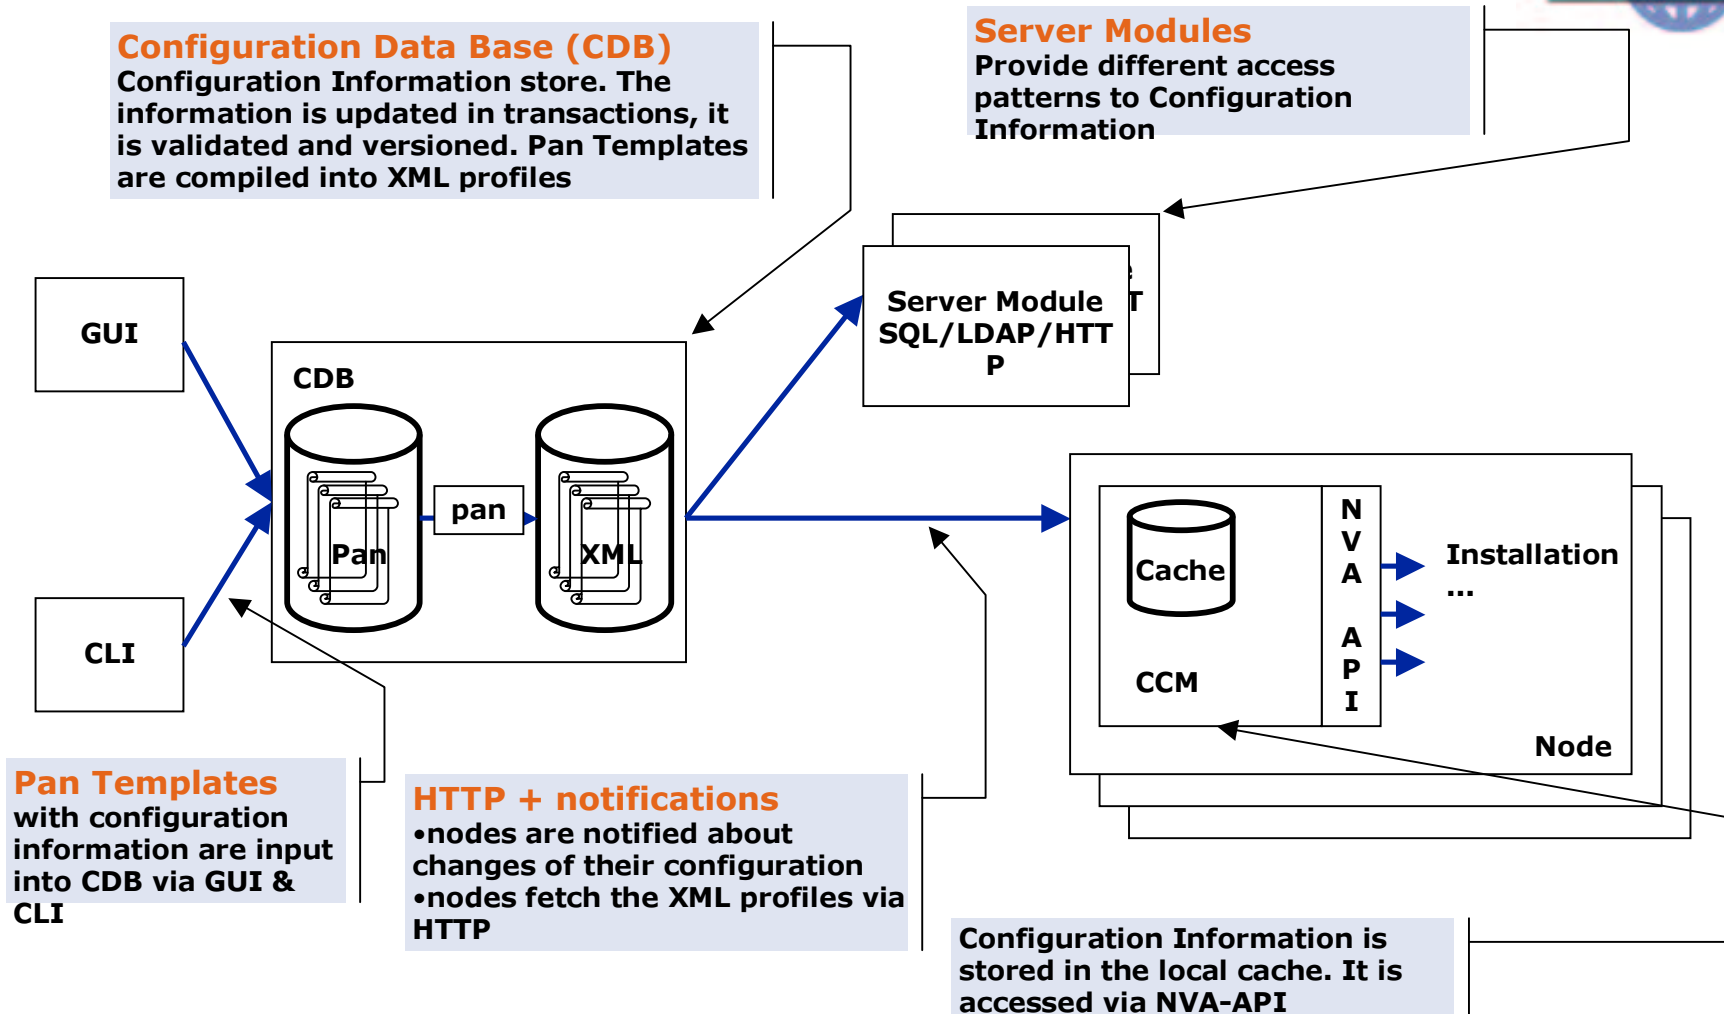

Developments till the end of the project



- ◆ 2.1.4. Scalability
- ◆ 2.1.5. CDB notification for synchronisation
- ◆ 2.1.6. CDB Server Module for XML Replication
- ◆ 2.1.7. CDB SQL Server Module
- ◆ 2.1.10. Command Line Interface
- ◆ 2.1.14. CCM Schema Checking
- ◆ 2.1.2. More built-in functions

- ◆ 2.1.9. Security
- ◆ 2.1.11. GUI

Delivery / Status

- ◆ 2.1.4. delayed, end of April -> June
- ◆ 2.1.5. delayed, end of April -> end of May / beginning of June
- ◆ 2.1.6. not started, middle May -> end of May
- ◆ 2.1.7. delayed, middle May -> end of May
- ◆ 2.1.10. not started, October
- ◆ 2.1.14. not started, end of May -> middle June
- ◆ 2.1.2. on-going, no deadlines

- ◆ 2.1.9. not started, -
- ◆ 2.1.11. -



Miscellaneous

- ◆ After Peaceful time, we're getting deployed:
 - Design/implementation getting validated
 - but also additional "unscheduled" work:
 - Providing help and expertise
 - New features (Pan namespaces)
 - (Implementation/Design) Bug and their fixes (CCM / CDB)
 - Source of requirements
- ◆ Getting contribution from Solaris people (maybe will help with GUI), already afford in porting CCM and CDB to Solaris



- ◆ Reshuffling tasks
