

# EYETS 16/17 BI ACTIVITIES


1

# GENERAL INFORMATION

## Technical stop duration:

- LINAC2: from 5/01/2017 to 10/03/2017
- LINAC3: from 12/12/2016 to 24/02/2017
- LEIR: from 12/12/2016 to 8/05/2017
- PS & TT2: from 15/12/16 @ 6:00 to 31/03/2017 @ 12:00
- PSB: from 15/12/2016 to 6/01/2017 and from 30/01/2017 to 17/03/2017

EYETS 2016-2017

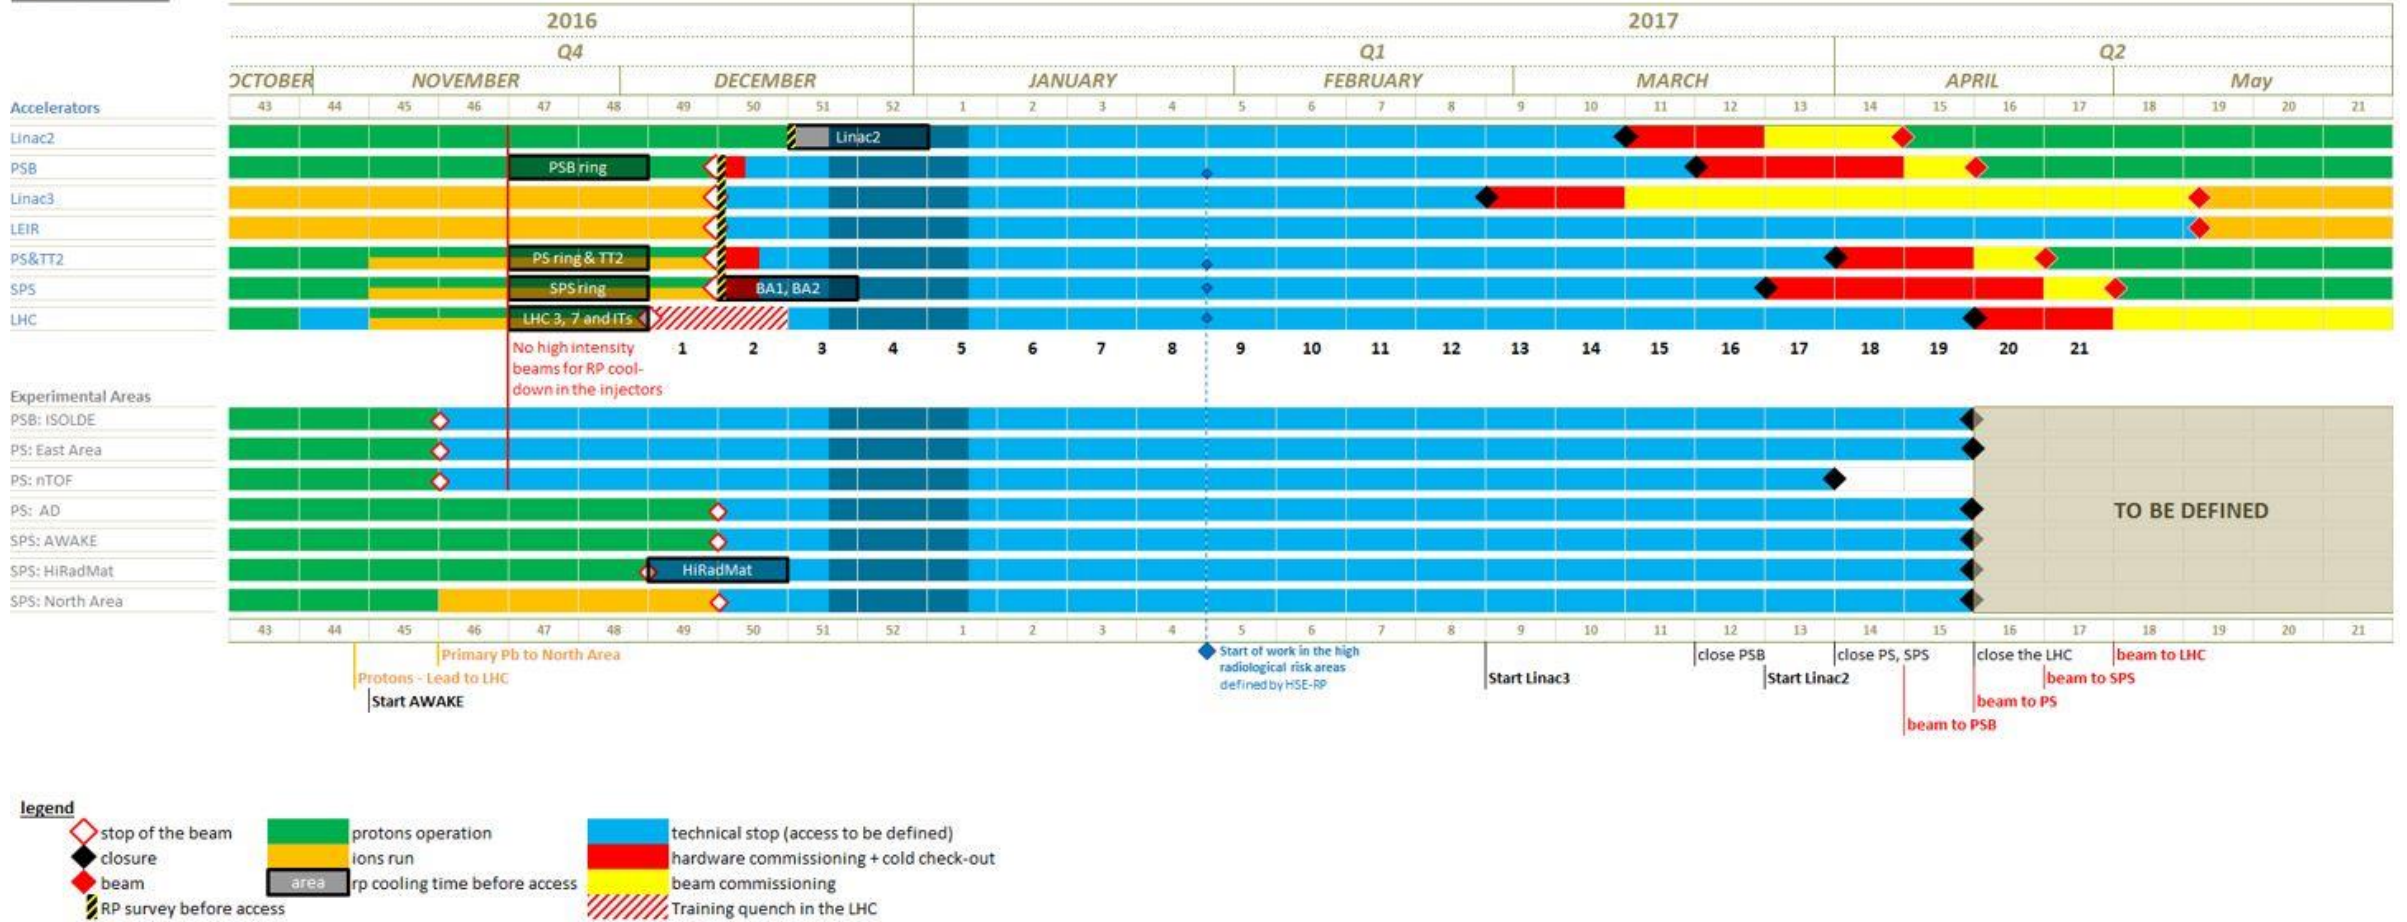

Official schedule: ATS-PM-MS-0001 EDMS [1470895](#)

- The following shows what I've been informed of and what I could dig out from IMPACT
- Inform me about any other activity not listed
- For interventions that concerns vacuum the proposed date are the ones suggested by TE/VSC. Each activity responsible has to contact directly Jose Somoza to organize the intervention and/or re negotiate the date if not ok.
- Contact Tobias Dobers(EN-ACE-SU) in case you need survey to schedule the intervention

# LINAC2-LINAC3-LEIR

instrument	description	location	vacuum	transport	survey	proposed date	responsible	comments	status	impact
SEM GRID	maintenance	LINAC3 ITF.MSG05	y	n	n	30-31/01/2017	C.Vuitton M.Duraffourg		A	86087
SEM GRID	maintenance	LEIR ITH.MSG11 ITH.MSG15	y	n	n	30-31/01/2017	C.Vuitton M.Duraffourg	zone inflecteur	A	86084
BCT	new instrument	LINAC 2 LT BCT30	y	y	n	9-15/02/2017	F.Lenardon	IMPACT	A	85342
SEM GRID	electronics upgrade	ETL	n	n	n	EYETS	F.Roncarolo	IMPACT	A	
DCCT	maintenance	LEIR ER.MTR12	n	n	n	EYETS	P.Odier		A	86474
orbit system	upgrade	LEIR	n	n	n	EYETS	L.Soby	IMPACT	A	
e-cooler	maintenance	LEIR	y	?	?	EYETS	J.Cenede	IMPACT	P	
BPM	new instrument	ITF	y	y	y	12/12/2016	L.Soby	IMPACT	P	

# PS

instrumen	description	locatio	vacuum	transpor	survey	proposed dat	responsibl	comments	status	IMPAC
BPM	maintenance	PS ring	n	n	n	EYETS	J.Belleman		A	85987
ion. BLM	new instrument	PS ring	n	n	n	EYETS	C.Zamantas	86817	A	
diam. BLM	new instrument	PS ring	n	n	n	EYETS	C.Zamantas	86845	A	
BTV	maintenance	PS ring	n	n	n	EYETS	S.Burger	need details	A	85421
BCT	new instrument	LT BCT40	y	y	n	EYETS	F.Lenardon	january	A	85339
BCT	new instrument	LT BCT50	y	y	n	EYETS	F.Lenardon	january	A	85339
BCT	new instrument	LT BCT60	y	y	n	EYETS	F.Lenardon	january	A	85339
BCT	new instrument	LBE BCT65	y	y	y	12-16/01/2017	F.Lenardon	january	A	85339
BCT	new instrument	LBS BCT62	y	y	y	05-11/01/2017	F.Lenardon	january	A	85339
septum 42	maintenance	SS 42	y	y	y	8/02=>9/03	J.Belleman C.Zamantas S.Burger	BI support on septum exchange BLM, PU and BTV IMPACT	A	
BTV	new instrument	BTP.BTV10	y	y	y	02-03/02/2017	P.Martins	vacuum issues	A	85606
WB PU	new instrument	SS90	y	y	y	16/01/2017	J.Belleman		A	85333
WB PU	maintenance	PS ring				january	J.Belleman		A	85987
DCCT	maintenance	TR34	n	n	n	13-17/03/2017	P.Odier		A	86473
WB PU	new instrument	BTP	y	y	y	02-03/02/2017	J.Belleman		A	85332
FWS	maintenance		y	n	n	EYETS	W.Andreazza	no need now, just in case	P	85324
BGI	new instrument	SS82	y	y	y	17/01/2017	G.Schneider	waiting vacuum approval	P	84505
SEM GRID	new instrument	SS 48	y	n	y	10/02/2017	P.Martins	production issues	P	86031
SEM GRID	new instrument	SS 52	y	n	y	24/01/2017	P.Martins	production issues	P	86031
SEM GRID	new instrument	SS 54	y	n	y	24/01/2017	P.Martins	production issues	P	86031

# TT2

instrument	description	location	vacuum	transport	survey	proposed date	responsible	comments	status	impact
BPM	maintenance	TT2	n	n	n	EYETS	T.Bogey	IMPACT	A	86056
BTV	maintenance	TT2	n	n	n	EYETS	S.Burger	need details	A	85421
WB PU	maintenance	TT2				january	J.Belleman		P	85985

# PSB

instrument	description	location	vacuum	transport	survey	proposed date	responsible	comments	status	IMPACT
BTV	relocation	BT	y	y	y	16-17/02/2017	W.Andreazza		A	85336
BR.TDM	maintenance	8L1	y	y	n	15/12/2016 dismantling	P.Odier		A	85282
WS	new instrument	4L1	y	y	y	15/12/2016	W.Andreazza		A	85329
BTV	maintenance	PSB rings	n	n	n	EYETS	S.Burger		A	85422
BLM	cabling	PSB ring inj and ejec	n	n	n	EYETS	C.Zamantas		A	86812
BLM	new instrument	PSB rings	n	n	n	EYETS	C.Zamantas		A	
BCT	new instrument	BI.BCT10	y	y	n	15-16/12/2017	F.Lenardon		A	85336
BCT	new instrument	BI.BCT20	y	y	n	02-08/02/2017	F.Lenardon	4 BCT	A	85336
BTMS	new instrument	PSB rings	n	n	n	EYETS	J.Belleman	cabling and electronic only	A	85986
	decabling campaign	PSB ring inj and ejec	n	n	n	EYETS	?		A	
BR.BCTDC	electronics	PSB rings	n	n	n	EYETS	L.Soby	impact	A	86472
FWS	maintenance		y	n	n	15/12/2016	W.Andreazza	completed	P	85326
BTV	relocation	BI	y	y	y		W.Andreazza	In case of an early L4 conn	P	
BTV	relocation	BT2	y	y	y		W.Andreazza	In case of an early L4 conn	P	
BTV	relocation	BT3	y	y	y		W.Andreazza	In case of an early L4 conn	P	
